

15. QA Automation Program – Leadership Working Update (As of 02/18/2026)

QA Automation Team – Velocity & Key Metrics (As of 02/18/2026)

This section aligns with the MAIN – Persistent Updates format: key achievements, velocity/growth, and metrics. QA Automation reports in **test cases added, coverage expansion, and bugs found** (not story points).

Team Structure & Focus

Name	Role	Primary Focus	Key Contribution (This / Last Period)
Swapnil Patil	Project Lead	Program delivery, intake, leadership alignment	Overall program execution; alignment on migration, V3 charter, pipeline, capacity.
Sunil Godiyal	Tech Lead (Offshore), Sr SDET	API Automation	~50 test cases added, modified, or fixed; worked with SMEs to identify gaps; created docs & manual cases in QTest.
Priti Choudhary	Performance Test Engineer	Perf testing (auth, enroll, txn)	40+ cases added; docs & QTest manual cases; platform-independent suites; working with Sri Mounica & Abhitosh on gap identification; getting suites ready for nightly regression.
Venkatesh Mallela	Sr SDET	Prime V2 automation	3 bugs found (this & last month); 50+ TCs added to V2 regression; framework enhancement & coverage expansion; flaky case fixes. Also supports monthly Unite release, nightly regression evaluation, bug documentation.
Dinesh Kumar	Sr SDET	Prime V3 regression	50+ TCs added; expanding V3 universe (IDP & UE); flaky fixes; more coverage. Also supports monthly Unite release, nightly regression evaluation, bug documentation.


Key Summary

- **V2:** 50+ new test cases; 3 bugs found; framework enhanced; flaky cases fixed; Venkatesh dedicated to V2 with release and nightly support.
- **V3:** 50+ new test cases; IDP & UE coverage expanded; flaky fixes; Dinesh dedicated to V3 with release and nightly support.
- **API:** ~50 test cases added/fixed; SME collaboration; docs & QTest manual cases; Sunil leading; ready for pipeline once direction set.
- **Performance:** 40+ cases added; platform-independent; docs & QTest; Priti with Sri Mounica & Abhitosh; suites readied for nightly regression.
- **Cross-cutting:** Venkatesh & Dinesh support monthly Unite release, nightly regression evaluation, and bug creation/documentation.
- **Total test-case velocity (this period): 190+** test cases added or made stable across V2, V3, API, and Performance.

Key Metrics (QA Automation – Not Story-Point Based)

Metric	Value	Notes
Test cases added / stabilized	190+	V2: 50+
Bugs found (V2)	3	This & last month (Venkatesh)
Regression suite size (V2)	381+	Up from ~250; 7 modules closed
Regression suite size (V3)	~255+	IDP, UE, web reg, CSR, profile
Release support	Monthly Unite	Venkatesh & Dinesh
Nightly regression & bug docs	Ongoing	Venkatesh & Dinesh
Pipeline readiness	API & Perf ready	Blocked on GitLab vs GitHub


Velocity Chart – Test Cases Added by Stream

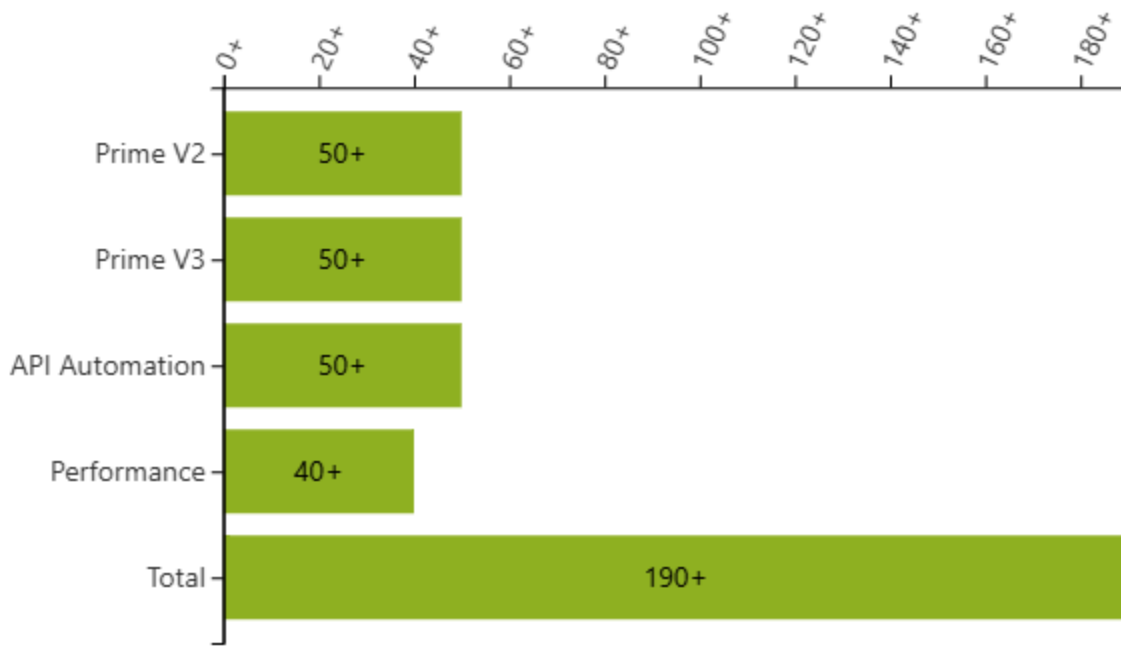

Stream	Test Cases Added	Owner
Prime V2	50+	Venkatesh
Prime V3	50+	Dinesh
API Automation	~50	Sunil
Performance	40+	Priti
Total	190+	—

Alternative: In Confluence, use **Insert Chart** and select Bar chart; use the table above as data source. Or paste the table into Excel and create a bar chart, then attach/screenshot.

Velocity Chart – Cumulative Regression Growth (Optional Trend)

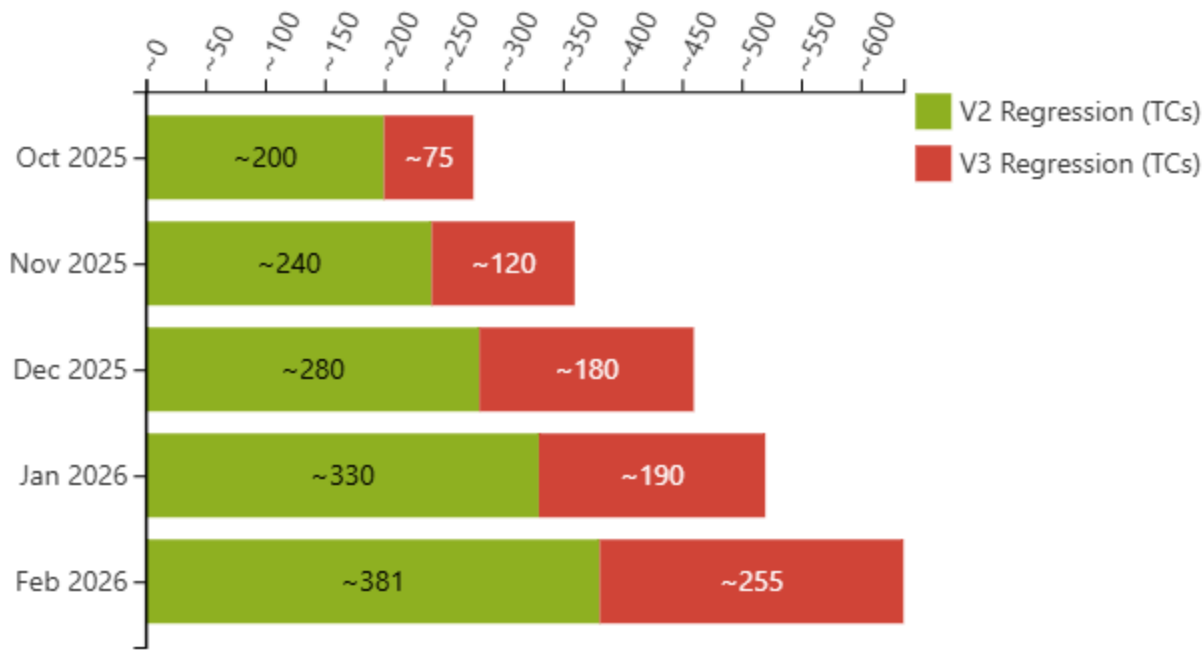

Month	V2 Regression (TCs)	V3 Regression (TCs)
Oct 2025	~200	~75
Nov 2025	~240	~120+
Dec 2025	~280	~180
Jan 2026	~330	~190+
Feb 2026	381+	~255+

Observations (Align with Other Scrum Teams' Format)

- **Velocity:** 190+ test cases added across V2, V3, API, and Performance this period; regression suite growth sustained.
- **Quality:** 3 bugs found in V2 (this & last month); nightly regression stable; release support sustained.
- **Delivery:** On-time support for monthly Unite release; nightly regression evaluation and bug documentation ongoing.
- **Blocker:** API & Performance pipelines ready but blocked on pipeline direction (GitLab vs GitHub).

1. Executive Context (What Changed Since Feb 4)

Since the Feb 4 leadership update, the QA Automation program has continued to execute strongly across Prime v2, Prime v3 (UE/IDP), API, and Performance—**execution is no longer the constraint**; clear ownership, priority alignment, and pipeline direction are now the gating factors. Key shifts this period:

- **V2 sustain/closure:** Regression coverage scaled from ~250 to **381+ test cases** with stable daily execution; all 7 core modules closed; offshore owns nightly regression, RCA, and release readiness; expansion to CAT + QC regions in progress.
- **V3 rapid growth:** Coverage at **~255+ test cases** driven by NYD requirements, IDP changes (e.g., international phone numbers), web registration, CSR account maintenance, profile updates, IDP login (positive, negative, forgot password, links); UE significantly expanded; working with Dom on pipeline enablement.
- **API & Performance ready but blocked:** Auth slice implemented and validated in Stage1/QC4; Auth + Metadata API suites running in QC4; Performance ownership under QA, auth flows stabilized, Priti on enrollment/withdrawal/account creation/login—technically ready for pipeline onboarding but blocked on **pipeline direction (GitLab vs GitHub)**.
- **Risks now in focus:** Plans migrating Legacy IDP without QA notification causing reactive rework and regression noise; V3 scope expanding organically without an explicitly agreed charter; increasing test volume and ad-hoc support putting pressure on capacity and JIRA hygiene.

2. Prime Version 2 – Sustain / Closure Mode

Progress Since Feb 4

- **Regression coverage** scaled from ~250 to **381+ test cases** with stable daily execution.
- **All 7 core modules** closed; documentation and sign-off artifacts completed.

- **Edge case coverage** added (e.g., subsequent weekly requirements); flaky cases resolved.
- **Multi-environment expansion:** Previously Stage1 only; now expanding to **CAT + QC** regions; multi-environment support in progress.
- **C5 moved to CAT;** lighter CSR-only regression suite planned.
- **Migration support:** Legacy IDP transitions supported (KSD, NYD); test cases moved from legacy to V3 IDP when required; gap analysis ongoing for reversal transfers, exchanges, and funds-related flows.

Execution Model

- Offshore team owns nightly regression, failure classification, RCA, and early-morning release readiness.
- V2 is effectively in **sustain/closure mode**; goal is multi-environment adaptability, release readiness, and identification of high-demand module gaps.

3. Prime Version 3 – IDP, Universal Enrollment & Expansion

Enhancements Since Feb 4

- **IDP:** Login (positive, negative, forgot password, links); IDP coverage stable; minimal flaky locator issue under investigation.
- **UE:** Coverage significantly expanded; Unite V3 coverage growing.
- **New coverage:** Web registration, CSR account maintenance, profile updates.
- **Pipeline:** Working with Dom on pipeline enablement; Entity planned for later nightly onboarding.
- **Next planned expansion:** IDP transaction flows (member side).

Coverage Summary

- V3 at ~255+ test cases driven by NYD requirements, IDP changes, and proactive gap closure.
- Primary automation surface for IDP and Universal Enrollment in Stage 1; regression execution stable.
- **Charter clarity needed:** Scope is expanding organically without an explicitly agreed charter (full regression successor to V2 vs. limited UE/IDP scope).

4. API Automation & Metadata Integration

Current State

- **Auth slice** implemented, validated in Stage1/QC4, and **ready for pipeline onboarding**.
- **Auth + Metadata API suites** created and running in QC4.
- **Environment dependency:** Data-centric validation prevents direct Stage1 portability; strategy in progress to make API tests environment-independent.
- **SME collaboration** completed; ready for regression onboarding once pipeline finalized.
- Postman/Swagger incorporated into ongoing work.

Next Focus

- Finalize pipeline direction (GitLab vs GitHub) so nightly execution can begin.
- Finalize lightweight regression for priority Account Services & Auth APIs; schedule CI/CD execution (no ad-hoc testing).

5. Performance Testing

Progress

- **Ownership** transitioned to QA; auth flows understood; baseline stabilization in progress.
- **Priti** working on enrollment, withdrawal, account creation, and login performance; new scripts created.
- **Blazemeter** dashboard being configured; manual test case documentation in progress.
- Plan: Add baseline performance cases to nightly pipeline; expand incrementally.

Next Focus

- Package existing assets into a repeatable regression suite; introduce API performance regression once pipeline direction is finalized; align execution and reporting cadence.

6. Cross-Team & Platform Support

QA Automation continues to support **platform-level and release efforts**:

- **Stage 5 CAT** support; Docker automation integration validation.
- **Scrum-of-Scrum** pipeline coordination.
- **Release failure investigations;** bug identification and resolution.
- Ad-hoc team support ongoing.

These efforts are high priority but often arrive **outside the planned intake model**, contributing to capacity pressure and JIRA hygiene strain.

7. Key Risk: Unplanned Support Load & Decision Blockers

What's Changing

- **Legacy IDP migration:** Plans migrating without QA notification are causing reactive rework and regression noise; migration ownership and advance notification need confirmation.
- **Prime v3 charter:** Scope expanding organically without an explicitly agreed charter (full successor to V2 vs. UE/IDP-only).
- **Pipeline direction:** API and Performance automation are technically ready but blocked on GitLab vs. GitHub decision—nightly execution cannot begin until finalized.
- **Capacity & intake:** Increasing test volume and ad-hoc support requests are putting pressure on capacity and JIRA hygiene.

Risk

Sustained unplanned support and delayed decisions can slow roadmap delivery, delay pipeline expansion, and reduce predictability. Part-time BA/scrum admin (30–40%) for intake, JIRA hygiene, and backlog health has been requested as team grows.

Leadership Alignment Needed

Alignment on **migration ownership**, **Prime v3 charter**, **pipeline direction**, **capacity protection** (BA/admin approval), and **intake discipline** (“no ad-hoc QA work outside JIRA”) is essential to sustain momentum and protect delivery focus.

8. Leadership Discussion Points (To Align On)

- **Migration ownership:** Confirm that teams migrating plans from Legacy to IDP must notify QA in advance and own coverage transition accountability.
- **Prime v3 charter:** Should Prime v3 become the full regression successor to Prime v2 (profile, balance, transactions, etc.), or remain limited to current UE/IDP scope?
- **Pipeline direction:** Finalize GitLab vs. GitHub for API and Performance automation so nightly execution can begin.
- **Capacity protection:** Approval for part-time BA/scrum admin (30–40%) to manage intake, JIRA hygiene, admin work, and backlog health as team grows.
- **Intake discipline:** Reinforce “no ad-hoc QA work outside JIRA” to prevent fragmentation and protect delivery focus.

9. Summary

Between Feb 4 and now, the team has:

- Scaled V2 regression to 381+ test cases with stable daily execution; closed all 7 modules; expanded toward CAT + QC; supported Legacy IDP migration (KSD, NYD) with gap analysis for reversals, exchanges, and funds.
- Grown V3 to ~255+ test cases (IDP login, forgot password, web registration, CSR maintenance, profile updates, UE expansion); stabilized IDP flakiness; advanced pipeline work with Dom.
- Delivered API auth slice and Auth + Metadata suites in QC4, ready for pipeline onboarding; advanced Performance ownership and baseline work—both blocked on pipeline direction.
- Continued cross-team support (Stage 5 CAT, Docker, SoS, release failures, bug resolution) while managing capacity and intake pressure.

The program is **executing strongly**—ownership, priority alignment, and pipeline direction are now the gating factors. **Leadership alignment on migration ownership, V3 charter, pipeline direction, capacity protection, and intake discipline** is requested to sustain momentum.
