

QA Automation Team – Leadership Guide - Dec 2025



Team Size: 5 total (Swapnil + 4)
New Joiners: Priti (~2–3 weeks), Sunil (~1 month)

1) Executive Summary

Over the last cycle, the QA Automation team shifted from “building test cases” to running a **governed automation program** with **stable nightly pipelines, measurable throughput, repeatable process, and ownership transfer to offshore**.

What’s materially different now

- **Prime V3 nightly GitLab regression is stable and governed** (UE pipeline green; IDP pipeline next).
- **Prime V2 suite is near closure** (major modules done; sign-off process active; flakiness logged as backlog).
- **JIRA working agreement is implemented and running** (cadence, DoR/DoD, dashboards, throughput).
- **API + Performance automation are now structured programs** (named owners, phased plan, pipeline enablement).
- Offshore team is operating as a true **shift-left execution + analysis unit** (daily report validation, RCA notes).

2) Current Coverage Snapshot (What’s Covered vs What’s Next)

Area	Framework	Coverage	Current Test Cases	Execution Pass %	Status
Enrollment (Specific Legacy / Legacy / NextGen)	Prime V2	~95%	41 (+40 upcoming)	~95%	Almost done (pipeline add + closure)
Enrollment (Universal Enrollment)	Prime V3 (UE)	~60%	137 (+50 upcoming)	~99%	Nightly GitLab pipeline GREEN
Web Registration (Legacy + First-Time)	Prime V2	~75%	9 (+10 upcoming)	~88%	In progress
Web Registration (IDP Web Reg)	Prime V3	~80%	~20	0% (not in pipeline)	Build + pipeline integration planned
Web Login (Legacy)	Prime V2	~75%	14 (+15 upcoming)	~79%	In progress
Web Login (IDP Login)	Prime V3 (IDP)	~95%	16+	~100% local / ~60% pipeline	Add to pipeline + stabilize
CSR Account/Profile Maintenance	Prime V2	~99%	16+	~99%	Closed
Contribution (Member + CSR)	Prime V2	~90%	50 (+20 upcoming)	~95%	Almost done
Withdrawal (Member + CSR)	Prime V2	~99%	80+	~95%	Closed
Balance Page Validation	Prime V2	~100%	10	~99%	Closed

QA Automation – Executive Delivery Roadmap

Executive Roadmap: Timeline View

Month-by-month delivery plan optimized for executive overview. This timeline-based visualization emphasizes outcomes over tasks, showing clear momentum and closure points across all automation workstreams.



Timeframe	Prime V2 Automation	Prime V3 Automation	API Automation	Performance Testing
Nov 2025	• Close remaining 3 modules• SME sign-off documentation• Regression stability at 85–90%	• Universal Enrollment pipeline stabilized• IDP Login automation completed	• Accounts Services KT (QA + Dev)• Review existing automation coverage	• KT from Nick / Abhitosh• Ownership transition started
Dec 2025	• All core modules added to pipeline• V2 regression suite release-ready	• IDP Login suite added to pipeline• UE expanded to additional plans	• Lightweight API regression pipeline live (1–2 endpoints)• Manual + automation baseline established	• Lightweight performance suite created• Initial pipeline execution enabled
Jan 2026	• Flaky test cleanup• Documentation finalization	• IDP Web Registration automation• Expanded UE coverage	• API coverage expansion• Dynamic test data strategy	• Baselines established• BlazeMeter dashboards live
Q1 2026	• Regression maintenance mode	• V3 regression expansion continues	• API QA process & governance live	• Full performance testing ownership• SDLC intake & governance implemented

Delivery Roadmap: Workstream View

Gantt-style visualization designed for demand planning and staffing discussions. This format makes capacity constraints visible and helps justify resource allocation decisions across parallel workstreams.



Prime V2 Regression

- Close remaining modules (Dec 2025)
- SME sign-offs & documentation (Nov / Dec 2025)
- Pipeline finalization (Dec 2025)
- Flaky test stabilization (Dec 2025)



Prime V3 Automation

- UE pipeline stabilization (Oct 20-30)
- IDP Login automation (Nov 2025)
- IDP Login pipeline integration (Dec 2025)
- UE plan expansion (Dec 2025)
- IDP Web Registration (Dec 2025)



API Automation

- KT & domain onboarding (Dec 2025)
- Accounts svc pipeline baseline (Dec 2025)
- Coverage expansion + data strategy (Dec 15-Jan 5)




Performance Testing

- KT & ownership transition (Dec 2025)
- Lightweight pipeline setup (Dec 2025)
- Baseline + dashboards (Jan 5-25)
- Governance & SDLC integration (Feb 1-25)

Flow-Based Dependencies

Sequential relationships that dictate delivery order. Understanding these dependencies is critical for realistic planning and explaining why certain work cannot be accelerated or resequenced.

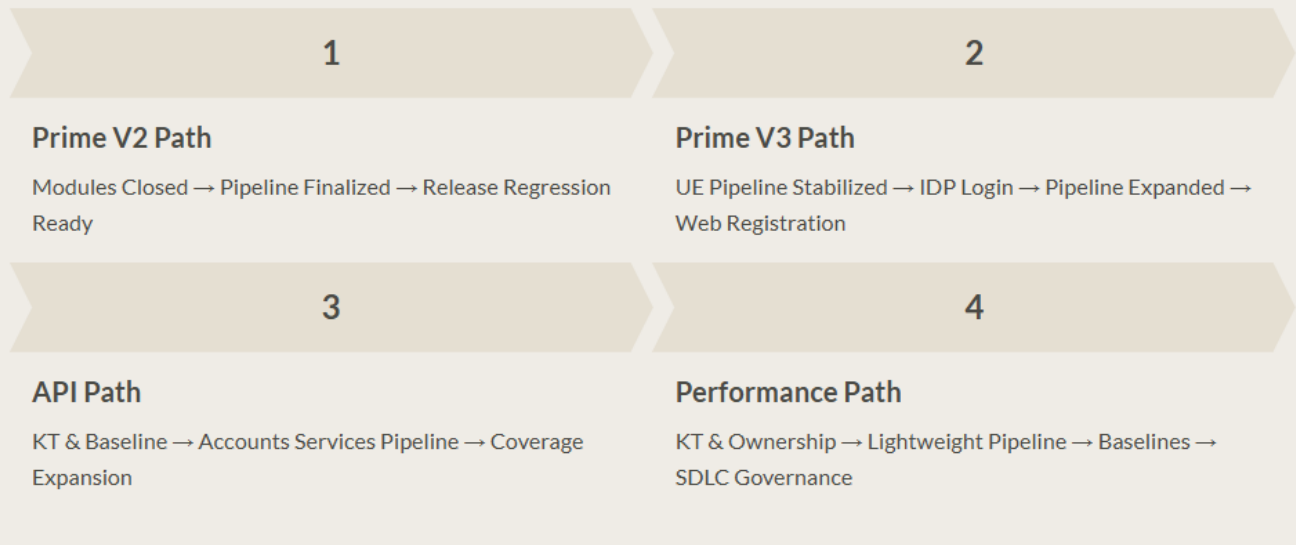

3) Prime Version 2 – Regression Expansion & Stabilization

What we completed (since last demand planning)

- **7 total modules in scope 4 modules fully closed** (SME sign-off docs prepared).
- Enrollment automation expanded across all required flavors:
 - **Member + CSR + Advisor** flows
 - Multi-plan expansion across **529 / ABLE / Advisor**
 - Plan variations: **IDP, NAA, Non-NAA, legacy variations**
- Stability materially improved:
 - **85–90% stable overall**, remaining flakiness captured as backlog items (not hidden).
- Confluence documentation updated for each module:
 - Plans included, flows, scenarios, known gaps, sign-off tracker.

Metrics (hard numbers leadership cares about)

- Test case growth:
 - **Oct 10:** 181
 - **Oct 29:** 239
 - **Nov 12:** ~250
 - **Expected by Nov 20:** ~280–290 (V2)

What's next (to close V2 properly)

- Close remaining **3 modules** + complete SME sign-off.
- Add "almost done" modules to pipeline and close.
- After closures: **dedicated flakiness cleanup sprint** + documentation finalization.

4) Prime Version 3 – Universal Enrollment + IDP + GitLab Pipeline

What we completed

- **Universal Enrollment GitLab pipeline is stable (99–100% pass)** after flakiness + data sync cleanup.
- Team now runs an operational loop:
 - nightly execution offshore analysis onshore triage bug/defect pipeline

What's built and ready

- **IDP Login automation suite created**
 - Positive flow
 - Negative flow
 - Forgot Password
 - Forgot Username
- Next: integrate into pipeline and stabilize (same model as UE).

What's next (high value)

- Expand UE coverage:
 - multiple plan types (Direct/ABLE/IDP/non-IDP)
 - multiple enrollment scenario variations
- Add **IDP Web Registration** (migrated legacy plans / first-time registration scenarios)

5) ABLE Plans – Coverage Expansion (V2 + V3)

What we completed

- ABLE test cases are now integrated into both frameworks:
 - Enrollment
 - Contributions
 - Withdrawals
 - Multi-plan variations (NAA vs non-NAA, IDP vs non-IDP)

What's next

- Build a single ABLE summary page (plans, flows, what's covered, what's pending)
- Confirm SME/prioritization from leadership to avoid random plan selection

6) Daily Regression Governance (Nightly Runs Morning Decisions)

What's live today

- Offshore team (Venkatesh & Dinesh) runs daily analysis at **7:00–7:30 AM EST**
 - failure classification (true defect vs data vs infra)
 - local reproduction + RCA notes
- Swapnil handles:
 - bug filing, ownership alignment, developer comms, governance decisions

Why it matters

- Faster turnaround before daily dev peak hours
- Reduced pipeline noise / reduced flakiness recurrence
- Creates a repeatable "regression operations" model (not hero work)

7) JIRA Process Implementation (Working Agreement Active)

What we implemented (done)

- Iteration cadence: refinement review retro loop
- **DoR / DoD** implemented
- WIP limits / expedite policies / sizing standards
- Dashboards for:
 - throughput, backlog health, work distribution, velocity trends
- Standups now run from JIRA board (no side spreadsheets)

What's next (maturity)

- Improve dashboard readability (leadership-friendly)
- Standard templates (spikes, stories, sign-off checklists)
- Better linkage: qTest Confluence JIRA for traceability

8) API Testing & Automation Program (Accounts Services First)

Why Accounts Services first

- Highest criticality + complexity (AuthServer / PXE / PixieFlow)
- Existing automation exists but is static-data dependent and not pipeline-ready

Phased plan (leadership-friendly)

- **Phase 1 (now end of year):** Get lightweight pipeline running for 1–2 endpoints (static data OK)
- **Phase 2 (next month):** Expand coverage + align manual + automation in qTest
- **Phase 3 (parallel):** Define API QA governance (DoR/DoD, deliverables, SDLC entry points)

Ownership

- **Sunil** owns execution (KT + build + pipeline)
- Swapnil owns governance and reporting model

API Automation Program: Accounts Services First

Strategic Rationale

Why Accounts Services?

- Highest business risk profile
- Maximum system complexity
- Existing automation exists but not pipeline-ready



Phased Execution Plan

01

Phase 1 (EOY)

Lightweight API pipeline with 1–2 critical endpoints; static data acceptable for baseline

02

Phase 2 (Next Month)

Coverage expansion with manual + automation alignment and dynamic data strategy

03

Phase 3 (Parallel)

API QA governance framework with SDLC entry criteria and standard deliverables

Ownership: Execution by **Sunil** | Governance & Reporting by Swapnil

9) Performance Testing Program (Ownership Transfer + Pipeline Model)

Reality check (leadership needs to hear this cleanly)

Performance testing is currently **high-demand but historically under-owned**.
We're fixing that by creating **a real owner + a real pipeline + a real intake process**.

Plan

- **Phase 1 (now end of next month):** stabilize IDP performance work + create a lightweight nightly pipeline
- **Phase 2:** Priti fully owns execution, baselines, reporting
- **Phase 3:** formal SDLC process + JIRA intake (no ad-hoc email testing)
- **Phase 4 (Q1):** expand coverage + standardize dashboards + build doc hub

Ownership

- **Priti** owns performance testing end-to-end (with QA leadership oversight)

10) Cross-Team Support (Controlled, Not “Drive-by” Work)

We support cross-team needs, but we’re pushing toward a model where support is:

- prioritized
- tracked
- owned
- and does not derail core charter deliverables

Current support examples:

- Stage 5 CAT environment guidance/testing support (Mark’s team)
- Scrum Of Scrum (Fred & Brian)
- White Cap Conversion (Henry & Jose)
- Automation guidance for other teams when needed
- KT and onboarding for new offshore resources
- Domain KT sessions added to onboarding plan

11) Roadmap (End of Year / Next Month / Next Quarter)

Roadmap Timeline (Leadership View)

By End of Year (Dec)

- **Prime V2**
 - Close remaining modules + complete SME sign-off
 - Add “almost done” suites into pipeline where pending
 - Finalize V2 regression documentation (what runs, plans, coverage)
- **Prime V3**
 - Keep UE pipeline stable and expand plan coverage
 - Add **IDP Login suite to pipeline** (initial stable baseline)
- **API**
 - Pipeline running for 1–2 critical endpoints (Accounts services)
- **Performance**
 - Priti operational ownership established + baseline suite defined + initial pipeline direction


Next Month (Dec Jan)

- Expand V3 UE + IDP plan matrix coverage
- Build IDP web registration automation plan + initial cases
- Move API from “static baseline” “coverage expansion”
- Performance dashboards/report templates established

Next Quarter (Q1)

- V2: Expand to other TXN modules
- V3: UE expansion + additional pipelines (Unite + Entity Mgmt)
- API: accounts services “done” model replicated to next services
- Performance: expand coverage + formal SDLC integration + pipeline maturity

Executive Roadmap: Time-Bound Commitments

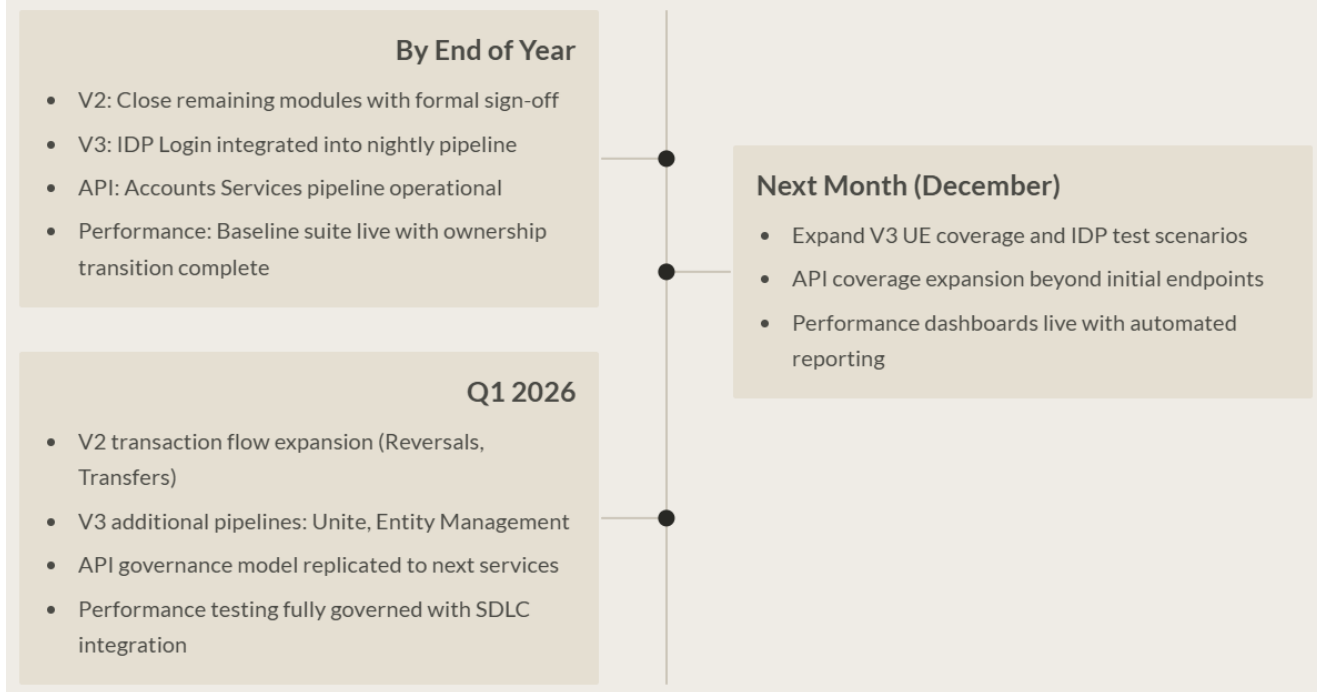

12) Leadership Questions / Decisions Needed (Do not skip this)

These are the “asks” required to keep velocity and avoid derailment.

V2 Scope Expansion (decision needed)

- Do we expand V2 automation into additional transaction modules:
 - **Reversals, transfers, exchanges, Ugifts, fund allocations**
- If yes: which are top 1–2 priorities and who is SME owner?

V3 Coverage Direction (decision needed)

- Should we prioritize **V3 IDP login + V3 transaction flows** next?
- Confirm which plans are **highest priority** for UE expansion (to avoid random plan selection)

Performance Testing (support needed)

- Confirm that performance testing work **must enter through JIRA intake**
- Align on what “minimum deliverable” looks like per request (baseline vs full-scale)

Pipeline/DevOps Support (dependency)

- For additional pipelines (Unite, Entity Mgmt, API, Performance), confirm:
 - do we get dedicated DevOps support or shared model?
 - expected timelines for runner/grid/config support?

13) QA Automation Team – End-to-End Operating Model

A governed, repeatable framework that ensures consistency across UI Automation, API Automation, and Performance Testing. This model drives quality through structured intake, automated execution, and continuous feedback loops.



Coverage Decision

Assess automation coverage



JIRA Intake

Prioritize and record work



Requirement Review

Validate and scope needs



SME Request

Submit business request

01

SME / Business Request

New feature, plan, flow, migration, or quality gap identified by stakeholders

03

JIRA Intake & Prioritization

Story created with Definition of Ready, added to Automation Kanban, priority aligned with release & risk

05

Local Build & Stabilization

Code/update tests, fix data dependencies, validate locally to achieve green baseline

01

Pipeline Enablement

GitLab / Jenkins integration configured, nightly execution enabled, pass/fail criteria defined

03

Offshore Morning Analysis (7:00–7:30 AM EST)

Failure classification performed, local reruns conducted, data vs defect identification completed

05

Fix → Retest → Stabilize Loop

Fix applied by development, revalidated locally by QA, monitored in subsequent nightly runs

02

Requirement Review with SMEs

Understand functional behavior, identify affected modules & plans, clarify scope (UI / API / Performance)

04

Coverage Assessment (Decision Point)

Already automated → stabilize & sync | Partially automated → enhance coverage | Not automated → create new automation

06

Regression Suite Integration

Add to correct suite (V2 / V3 / API / Performance), update documentation & traceability

02

Nightly Execution (Mon–Fri)

Automated regression runs executed, results published to stakeholders and dashboards

04

Onshore Triage & Bug Governance

Bug filing with root cause analysis, dev coordination, regression health tracking maintained

06

Continuous Expansion Loop

Work with SMEs to identify next high-priority areas, repeat model for new modules and features

Execution, Analysis & Continuous Improvement

Pipeline Enablement

GitLab/Jenkins integration ensures nightly execution with defined pass/fail criteria

Nightly Execution (Mon–Fri)

Automated regression runs with published results

Offshore Morning Analysis

7:00–7:30 AM EST: Failure classification, local reruns, data vs defect identification

Onshore Triage & Bug Governance

Bug filing with RCA, dev coordination, regression health tracking

Fix → Retest → Stabilize Loop

Fix applied, revalidated locally, monitored in nightly runs

Continuous Expansion Loop

Work with SMEs to identify next high-priority areas and repeat model for new modules



Execute

Automated nightly runs across all test suites



Analyze

Morning triage identifies root causes



Stabilize

Fixes applied and revalidated



Expand

Continuous coverage enhancement

14) Kudos / Recognition (Leadership-ready)

- Team stabilized and operationalized **Prime V3 UE nightly pipeline** (green baseline + governance loop).
- Offshore team runs daily analysis early morning, enabling faster dev turnaround and reducing noise.
- V2 module closures + sign-off discipline established (moving from “automation exists” to “automation reusable for releases”).
- New joiners (Sunil, Priti) onboarded quickly and already delivering into structured programs (API + performance).

Team Wins Worth Celebrating



Prime V3 Pipeline Excellence

Stabilized, governed, and running with 99–100% reliability in production



Offshore Independence

Team now runs daily regression operations independently with full RCA capability



V2 Maturity

Moved from "automation exists" to "automation is reusable and governed"



Rapid Onboarding

New team members delivering production work within weeks, not months



AI Productivity Gains

Active use of Copilot and Cursor accelerating code quality and delivery velocity
