

Infinity Sprint Review - 26.8 (4/15 - 4/28)

Sprint Goal Review

Status: **Achieved** 

Objective: Prepare PA GSP Flywire for planlevel testing by completing the remaining user experience, settlement file, and job orchestration work needed for endtoend withdrawals, while using targeted discovery to identify and document any remaining gaps in fee handling ahead of May 5 testing.

Sprint Narrative - This sprint, Team Infinity focused on getting PA GSP Flywire **ready for planlevel testing** by finishing the remaining user experience, settlement file, and job orchestration work needed for endtoend Flywire withdrawals, while using targeted discovery to confirm whether any feehandling gaps still existed ahead of May 5 testing. The team completed the planned fee daemon spike, and the outcome was reassuring: **no new gaps or followup items were identified**, which reduces risk as we move into partner testing.

On the delivery side, the team closed the remaining workflow and processing steps needed to support Flywire withdrawals endtoend. This includes completing the **WithdrawaltoSchool confirmation page**, finalizing the **new file naming/output location/transmission integration**, incorporating **Flywire fees into control totals and gross amounts**, updating the **ReconExportRequest** logic to include Flywire fees, ensuring withdrawals are properly flagged to enable settlement and ReconPlus file generation, and introducing **PA GSP nightly dependency logic** so Flywire settlement file population occurs in the correct order.

The final piece of the sprint goal is now focused on **internal endtoend testing** of Flywire withdrawals across the A&R and partner files, which remains in progress as we validate alignment across the full chain. To ensure everyone is aligned on how plan testing will run, we had a dedicated **testing plan call with the State just before this Review**, with the intent to confirm readiness and expectations for partner testing starting May 6 and running through the May 12 freeze.

Challenges/Obstacles:

- The primary obstacle the team has been working through this sprint is related to the **mandatory iOS SDK 26 upgrade**, required by Apple for all App Store submissions after **April 30, 2026**. From a development standpoint, the team has completed the necessary work. (Updated the iOS project configuration, deployment targets, build settings, schemes, and iOSspecific dependencies to align with the new SDK.)

However, progress has been blocked by an underlying **macOS upgrade issue** that is currently preventing us from successfully building the mobile application. This macOS constraint sits outside the app code itself and has required **DevOps assistance** to resolve. While DevOps has begun working with a newer Mac environment and the situation is improving, they are managing competing higherpriority work, which has limited how quickly this can be fully resolved. Oscar remains in constant coordination with DevOps to move this forward as quickly as possible.

Key Accomplishments

On the **Flywire integration (PA GSP)** side, we made **notable progress in the UI and backend**:

PA GSP - Flywire Implementation	88		18%	1%		92%	1/21/26	5/5/26
---------------------------------	----	------------------------	-----	----	------------------------	-----	---------	--------

- ☒ Spike: Research the PA GSP Fee Daemon **Done**
- ☒ PA GSP Flywire: UX Update – Withdrawal to School > Confirmation Page **Done**
- ☒ PA GSP Flywire: New File – File Naming, Output Location, and Transmission Integration **Done**
- ☒ PA GSP Flywire: New File – Include Flywire Fees in Control and Gross Amounts **Done**
- ☒ PA GSP Flywire: Job Update – ReconExportRequest File Update to Include Flywire Fees **Done**
- ☒ PA GSP Flywire: Set BACKEND_POSTED = 'Y' for Withdrawals After Posting to Enable Settlement & ReconPlus File Generation **Done**
- ☒ PA GSP Flywire: Introduce PA GSP Nightly Dependency Logic for Flywire Settlement File Population **Done**
- ☐ PA GSP Flywire: Internal Testing of Flywire Withdrawals Between A&R and Partner Files **In Progress**

Other:

- ☐ ILD - Hide Denied First Steps Accounts from Client View in Mobile App **In Progress**
- ☐ UP WD: API - Withdrawal API would need to support the IDP SSO token in addition to supporting PKCE **In Progress**
- ☐ Add Validation When a Relationship selection other than "Myself" Is Selected but AO SSN/DOB Is Entered **In Progress**

 **Mobile Accomplishments:** In parallel with the core PA GSP Flywire work, **Oscar focused heavily on mobile stability and readiness**, completing several longstanding mobile bugs related to dashboard loading, concurrency, and login race conditions. He also completed the necessary code and dependency updates to support **iOS SDK 26**; however, that work remains **blocked from being released** due to an ongoing macOS build issue outside of the application code. Work is continuing on remaining **ADRelated fixes**, which are still in progress as part of the broader mobile quality and compliance effort.


- ☒ Update iOS project configuration and dependencies to support iOS SDK 26 **Done**
- ☒ My Accounts page remains stuck in loading state when mobile dashboard API call fails due to unhandled error **Done**

- ☒ Concurrent mobile dashboard API calls after login due to cache bypass and parallel pipelines **Done**
- ☒ Race condition between Sardine login risk check and navigation causes session to clear after My Accounts load begins **Done**
- ☐ Resolve ADA Issues in Mobile App via Isolation Testing **In Progress**


Done In progress Not started
47% **35%** **18%**

Sprint burndown

19 points done, 21 points to go

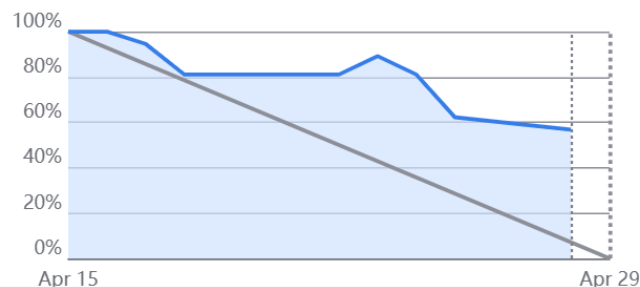

Burndown

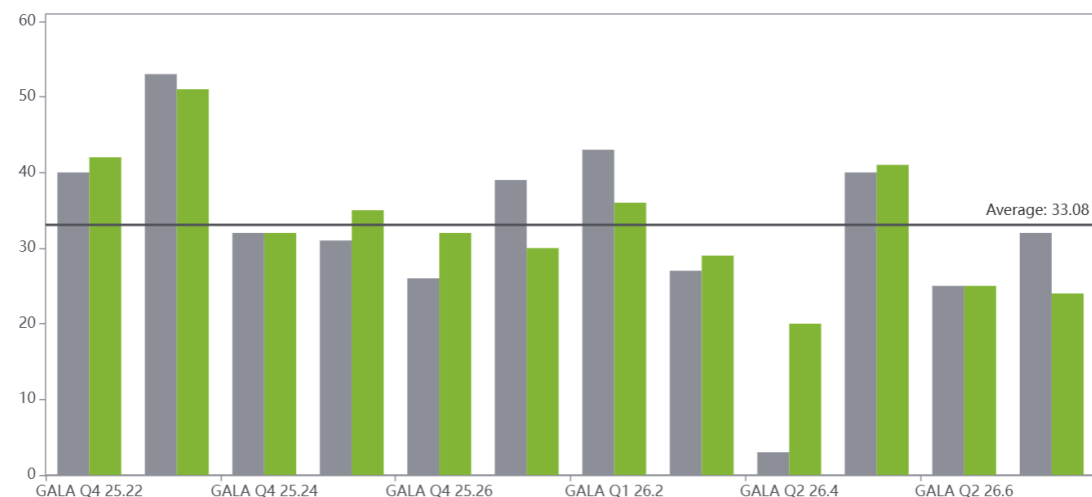

Velocity

QIPs: n/a

Escape Defects Resolved: 0

BUGs: 3 New BUGs logged

Personal Improvement

- **AI Utilization:**

Continuous Improvement

- **Continuous Improvement Item: Weekly AI Utilization Review/Goal**

After consolidating the notes and discussions from the retrospective, we identified two AI learning experiments to move forward with. These experiments will be added to our continuous improvement stories and bring it in our daily standup conversation to share progress, challenges and insights.

AIAssisted Unit Test Coverage

We want to learn how to use AI (Cursor) to generate and refine unit tests that meet coverage expectations before opening a merge request, so that merge requests are approved faster with minimal rework related to test coverage.

AI-Assisted Story Detailing & Requirements Engineering

We want to use AI (Cursor / Copilot) to draft and refine story descriptions, acceptance criteria, and implementation guidance, so that developers can start coding with clearer inputs and reduce backandforth clarification during development.

Roadmap Update

Upcoming Goals: *Our focus will be to*

Sprint 9 - In this upcoming Sprint the team will be working to finish up remaining Stories, working with our partner on testing and supporting any issue into the May 15th release..

- **Team Infinity – Roadmap Update**

- **PA GSP Flywire (Primary Focus):**
Continue progressing the PA GSP Flywire feature, with **full team engagement in Sprint 9 through delivery**.
- **Mobile Enhancements/Stability**
 - Delivery of the iOS SDK upgrade
 - We want to get back into solving remaining ADA item related to voice-over text
 - **UE Validation issue for "My Child" relationship option**
 - **Focused investigation and improved testing support for ADA remediation - Isolate accessibility issues by removing or bypassing components and testing with static data.**
 - **ILD - Hide Denied First Steps Accounts from Client View in Mobile App**
- **Advisor Enrollments API – Metadata (In Parallel Sprint 9 through Sprint 11):**
As part of the broader Advisor Enrollments API effort split across teams, Team Infinity will take ownership of the **Metadata work**, beginning with mapping and refinement. The focus in the upcoming sprint will be to **shape, define, and refine Metadata stories** so they are executionready to begin in **Sprint 8**, running in parallel with continued PA GSP work.
- **Advisor Enrollments API – GET Work (Shaping):**
After Metadata, Team Infinity will shift to the **GET API work**, sequencing it behind Metadata to ensure proper data availability and minimize rework.
- **Sardine Advisory Integration (Mapping):**
Team Infinity will also complete the **Sardine Advisory Integration** as a subsequent priority, currently sequenced as the **third major workstream** once PA GSP and initial Advisor API work are underway.
