



Unite MSC Automation Program

Weekly Leadership Update • July 17, 2026

QA AUTOMATION

AMSQUAD

Prepared for: Rajiv/Rajib, Henry, Kevin

Executive Summary

From fragmented legacy coverage to reusable canonical automation

Mobile 2 API

Baseline functionally complete — 88% endpoint coverage verified. Ready for leadership sign-off pending evidence refresh.

Mobile 1 API

Active sprint focus. Authentication foundation complete; business endpoint automation now underway.

Performance

Foundation live on MSC Jenkins. Non-IDP login flow complete; IDP and nightly schedule expanding.

Pipeline


GHA deployment validation slice complete. GitLab nightly regression job pending DevOps story approval.

V2/V3 UI

Stable nightly regression running. Daily triage cadence established and maintained by the team.


Program Metrics Snapshot

Readiness by workstream — as of July 17, 2026

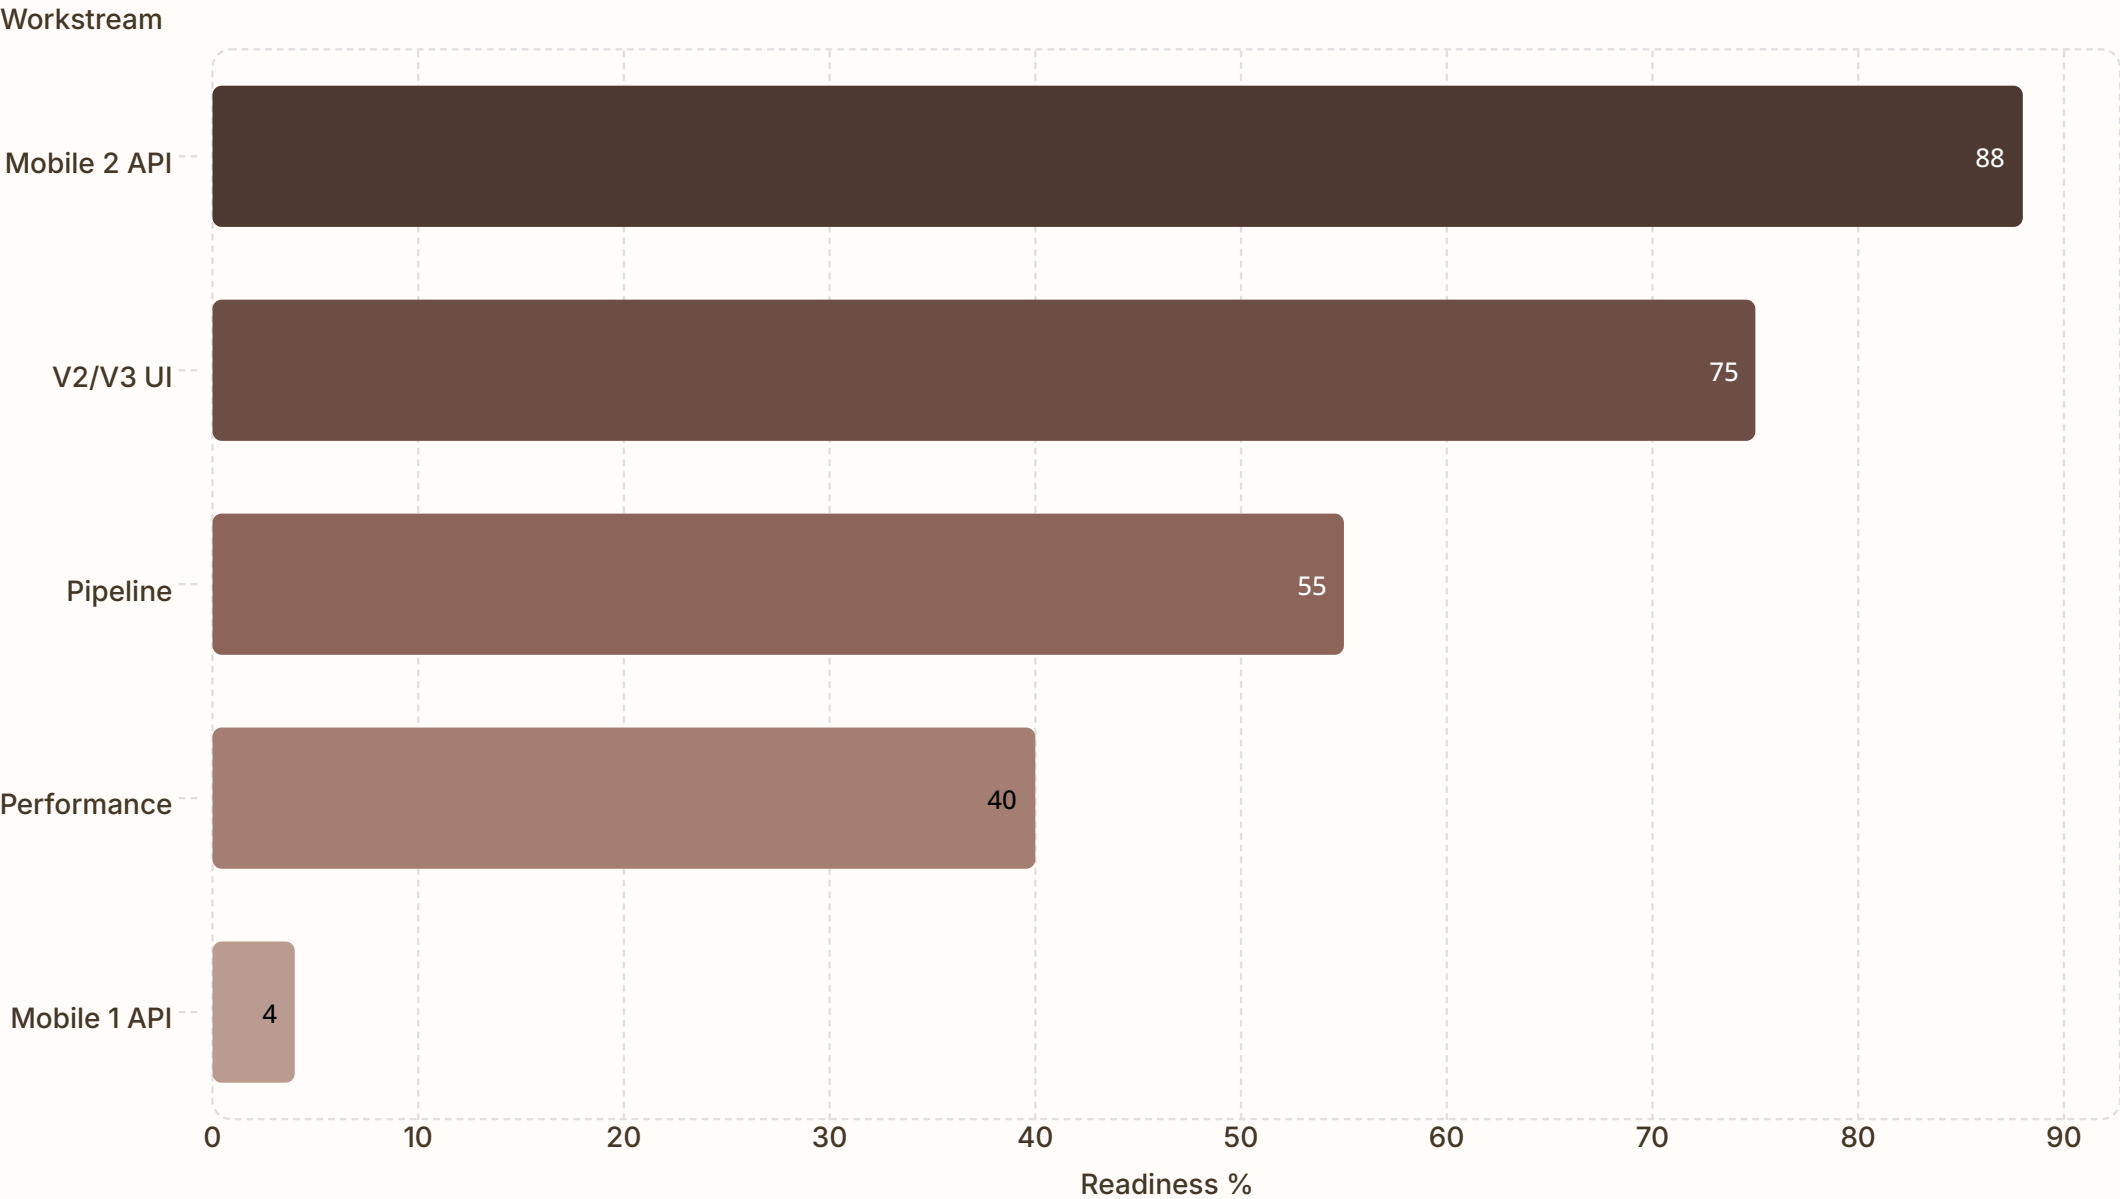

Note: Mobile 2 and Mobile 1 percentages reflect endpoint automation coverage. Pipeline, Performance, and V2/V3 UI reflect qualitative program readiness assessments.

Mobile 2 Endpoint Coverage

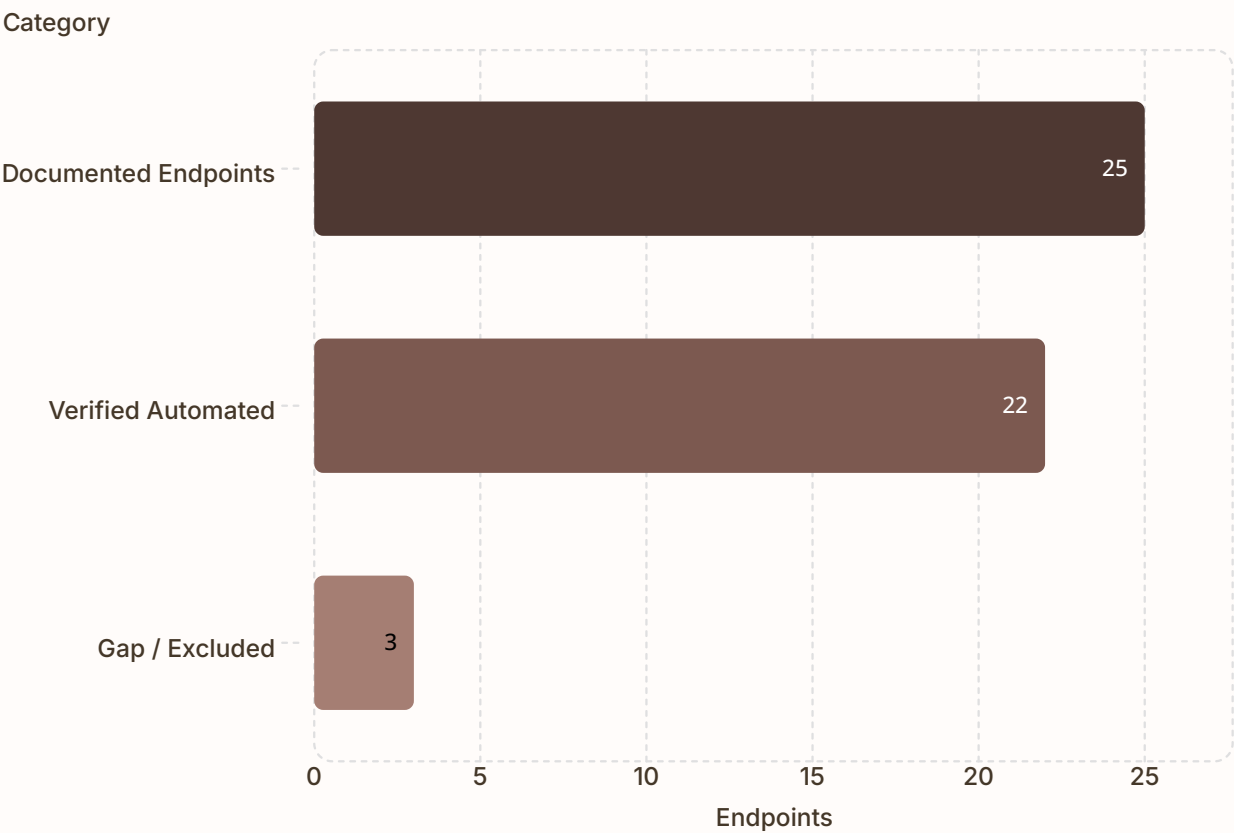

88% Verified

As of **2026-07-14** — the formal validation checkpoint.

Coverage is **not claimed at 100%**. Three endpoints remain excluded or in-gap pending team disposition.

Projected coverage increases after post-07/14 merges are incorporated. A refreshed validation run is required before final sign-off.

Mobile 2 Sign-Off Path

Baseline functionally complete — pending evidence refresh

☒ COMPLETED

→ **Canonical TestNG Migration**

Full migration from legacy framework to reusable canonical TestNG structure complete.

→ **OKD + NMD Environment Support**

Test suites validated against both OKD and NMD deployment targets.

→ **Dynamic SQL Auth + Master Suites**

Dynamic authentication via SQL and master suite orchestration fully implemented.

☐ OPEN ITEMS

→ **Final MR Merge**

Outstanding merge request must be closed before evidence snapshot is refreshed.

→ **QC4 + Stage 1 Execution Run**


Full suite execution required on QC4 and Stage 1 environments to confirm stability.

→ **GitLab Nightly Job Creation**

DevOps story approval required to establish the scheduled regression job in GitLab.




Mobile 1 — Active Sprint Focus

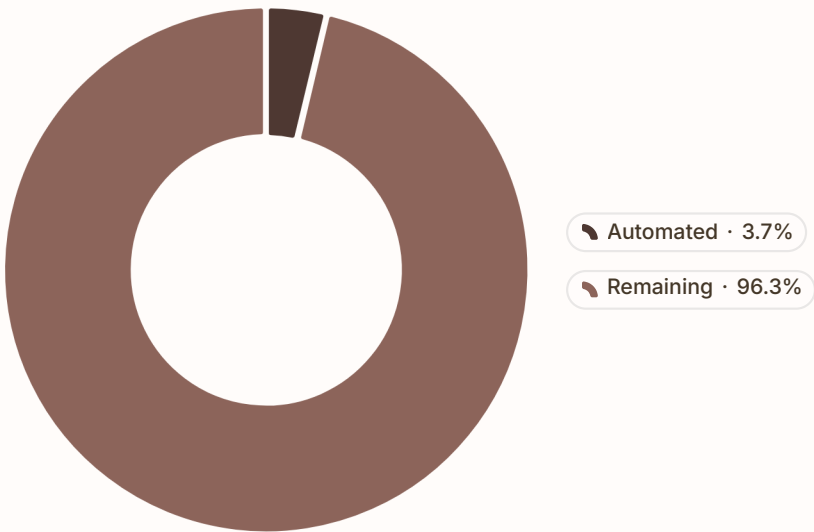

1 of 27 endpoints automated to date

Authentication Foundation Complete

The non-IDP authentication baseline has been established, enabling systematic business endpoint automation to begin this sprint. IDP compatibility work is scoped for the following sprint.

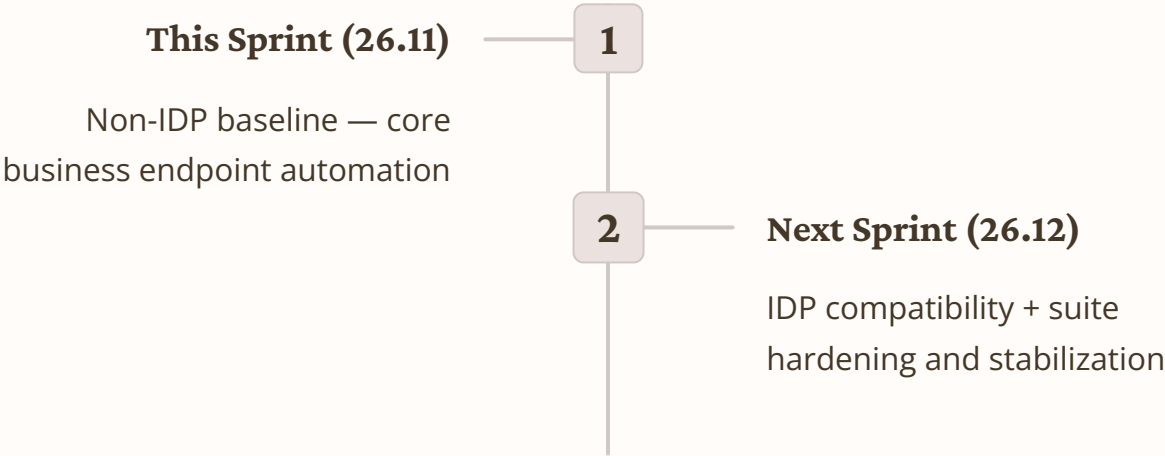

CI/CD Pipeline Workflow

GitHub Actions deployment validation is distinct from GitLab nightly regression



✔ COMPLETE

GitHub Actions Dashboard — Deployment validation slice confirmed live and operational.

◆ IN PROGRESS

Module Suites — Suite wiring to GHA pipeline actively being configured and tested.

□ PENDING

GitLab Nightly — Scheduled regression job requires DevOps story creation and approval.



Performance Regression Status

MSC Jenkins Job

✓ **Available** — Performance regression job provisioned on MSC Jenkins. Foundation infrastructure is live.

Non-IDP Login → Dashboard

✓ **Complete** — End-to-end non-IDP login through dashboard flow validated and passing.

IDP MSC Login

◆ **In Progress** — IDP-based login flow under active development. Blocked on clean manual validation baseline.

Nightly Schedule

□ **Pending** — Nightly execution will be enabled after manual validations pass cleanly and consistently.

Next flows in queue: Contribution, Banks, Activity, Mobile 1 — to be sequenced after IDP flow stabilization.

Risks & Dependencies

RAG Status — July 17, 2026

Risk / Dependency	Severity	Impact & Mitigation
GitLab Nightly Not Created	● High	Blocks continuous regression signal for Mobile 2 sign-off. Requires DevOps story approval this sprint.
Stage 1 / Stage 5 / QC2 Test Data	● Medium	Missing or inconsistent test data in environments delays suite execution and sign-off evidence.
Enrollment Encryption / Test-Data Utility	● Medium	Multi-sprint complexity. Dependency on shared utility development cadence outside team control.
Reporting / Admin Load	● Medium	Administrative overhead reducing available engineering sprint capacity. Escalation support requested.
Ad-Hoc Intake (Unstructured)	● Medium	Unplanned requests disrupting sprint commitments. Structured backlog intake enforcement needed.

Leadership Asks & Sprint Roadmap

Leadership Actions Requested

01

Approve DevOps Story

Authorize GitLab nightly regression job for Mobile 2 — critical for sign-off evidence.

02

Confirm Mobile 2 Sign-Off

Review and approve sign-off after refreshed evidence run is submitted by the team.

03

Confirm Mobile 1 Priority

Affirm sprint commitment to Mobile 1 non-IDP baseline this sprint (26.11).

04

Support Pipeline & Environments

Ensure environment readiness and DevOps alignment across Stage 1, QC4, and GitLab.

05

Enforce Backlog Intake + Protect Capacity

Structured intake for all ad-hoc requests. Support 30–40% capacity protection from BA/Scrum/admin load.

Sprint Roadmap

