

Persistent Updates

Date: 2/19/2026

Staffing:

- Ascensus Persistent Teams: <https://confluence.ascensus.com/x/Hbw8Eg>
- [Persistent Team Roster](#)
- Requirement tracker: [Ascensus GS Resource Status Tracker_2026.xlsx](#)
- New Offboarding -
 - NA

Open / In-Progress: Requirements: Persistent

Chapter Lead	Cost Center	Position	Location	Name	Status	Remarks
New						
Gerald Matthews	182001	Jave Angular UI Developer	Nearshore	Pablo Lopez	Selected	Onboarding in progress
Replacements						
Gerald Matthews	182001	Scrum Master - Cosmos & Alchemy	Offshore	Kiran Patil	Selected	Kiran will join PSL on 28th Feb. Meanwhile we have involved Akhilesh Dixit (From Retirement) to handle these two teams till we have new scrum master onboarded

Open / In-Progress: Requirements: Abstra / Assertia

- NA

Performance Cases

Name	Project	Skill	Location	Chapter Lead	Remarks
A		Java	Offshore	Gerald Mathews	Keeping a close eye on the availability, deliverables, quality of deliverable
B		Java	Offshore	Gerald Mathews	
C		Java	Onsite	Arun Dash	

Budget Tracker

Budget tracker for 2025: [Ascensus GS Budget Tracker_2025.xlsx](#)

Budget tracker for 2026: [Ascensus GS Budget Tracker_2026.xlsx](#)

Delivery Updates:


SUMMARY HIGHLIGHTS:

Teams	Key Summary	Key Metrics
-------	-------------	-------------

<u>Cosmos</u>	• SQL Injection Vulnerabilities remediation across UNITE ◦ Resolved 64+ SQL Injection risks across CSR 529 modules. ◦ Secured search pages in: Admin , Withdrawal Mgmt , Self-Service Reporting, Omnibus Account Enrollment • Justification on false positive for SQL Injection Vulnerabilities • Next steps: ◦ Address Security violation for "Server - side Request Forgery (SSRF)" vulnerabilities across UNITE ◦ Address Security violation for "Cross Site - Scripting (XSS)" vulnerabilities across UNITE	% Complete Velocity (Total SPs) Throughput (Stories) • Velocity, Throughput significant uplift in the last sprint • Consistent >=100% completion since last 5 Sprints • Observations - Limitation of stories slicing for security work. • On Time delivery, 0 Escape defects
<u>Alchemy</u>	• Kofax Sardine Integration Enrollment for 529 all flows (Owner , Guardian, AIP, Bank, Check, EBT/AIP) and ABLE all flows except 'Check' completed, along with 1 QIP targeting 20th Feb release • Next Steps: Completion of Kofax Sardine integration Enrollment work for 1 ABLE flow & start Contribution for 529 flows	% Complete Last 8 Sprints Velocity (Total SPs) Last 4 Sprints Throughput (Stories) Last 4 Sprints • All 3 Metrics improvement in the last sprint • Observations - Associate leave, scope of slicing improvement, 2 performance cases • On Time delivery, 0 Escape defects

Odyssey

- Recently delivered - NY UE on 1/23 & Umbraco Migrations on 1/30 successfully, well collaborating with cross functional teams.
- **Upcoming Releases:** -
 - WI UE enablement (Desktop + Mobile) - 2/22
 - Kansas (UE enablement) - 3/1
 - VA ABLE IDP & Entity Management Dashboard - 3/23
 - Michigan UE - 3/13
 - Trowe changes in stage 1 - 3/31
 - Minnesota - 4/17
- **Suggestions:**
 - Ongoing changes in business priority, diluting team focus, leading to reduced predictability, & operational efficiency. Need streamlined release schedule
 - New scope of UI changes (as per new Figma) performed in the release additionally
 - Adherence of SLA (code freeze date) by all other teams to ensure defects fixes, validation, closure before code freeze date.

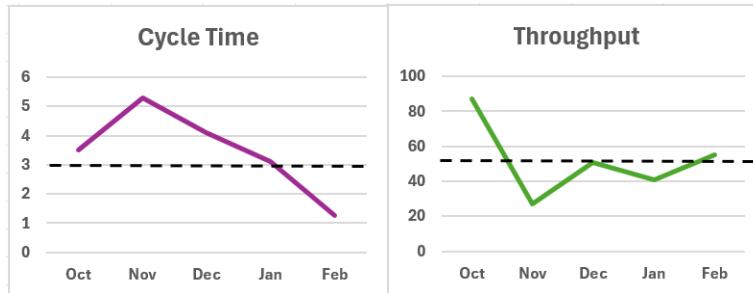



- Cycle time is achieved average 3 and 1.2 in Feb month
- Expecting increase in Throughput in Feb due to additional work scope added
- Observations - Dependencies on external teams (e.g. No Stage2 CSR access for QA, defect resolutions), changes in prioritization holding the story, events like DB refresh impacts the environments down and CT
- On Time delivery, 0 Escape defects

Synergy

- 104 RT tickets achieved (above set target of 80).
- 5 QIPs, 4 stories (PII Dashboard project)
 - Implementation & Testing of Reverse payroll, Excess contribution and Reverse bounce RTs on Stage1
- Expecting shift in focus from RTs due decentralizing initiative

Next steps: KT ongoing to support triage decentralization initiative. PII Dashboard automation work validation in Stage 1



QA Automation	• Prime V2 -Closure of flacky cases. New coverage of enrollment, regression, registration, web login, and withdrawal scenarios • Prime V3 – IDP & Universal Enrollment Expansion • API & Performance Foundations: <u>Next Steps:</u> Prime V3: Enable Unite pipeline for IDP Web Registration and UE CSR Withdrawals; expand regression post-pipeline; advance IDP transaction workflows.									
All	AI Adoption, Benefits - • Number of associates usage- All • Usage areas- Analysis, Development, Code Review, Unit testing, document generation mainly • Tools- Usage of Copilot, Cursor AI majorly and other tools like GPT models, Gamm app, Claude, Gitlab Due AI, JIRA built in AI assistants Total Tokens for entire team extracted from Cursor report Total Tokens <table><thead><tr><th>Month</th><th>Total Tokens (Approx.)</th></tr></thead><tbody><tr><td>Oct</td><td>250,000,000</td></tr><tr><td>Nov</td><td>650,000,000</td></tr><tr><td>Dec</td><td>680,000,000</td></tr></tbody></table>		Month	Total Tokens (Approx.)	Oct	250,000,000	Nov	650,000,000	Dec	680,000,000
Month	Total Tokens (Approx.)									
Oct	250,000,000									
Nov	650,000,000									
Dec	680,000,000									

1. Team Cosmos

Key Highlights:

- Team started from 17th Sept 25 (Sprint 0)
- **Work completed areas in 8 Sprints -**
 - 529 Unite portal Matching grant eligibility, Fortify privacy violations,' Advisor management Rep search, TN stars, John Hancock 529, Matching grant opt-in letter feature
 - Enable Transact (Higher One) expansion for MT, IA, NV and MD state plans in stage. Secure Page Enhancements – Updated new treasurer logo swap for enable savings plan.
 - Uniform email address for all email types in ABLE and 529 plans,
 - Matching Grant Opt_in Letter for Paper enrollments, Removal of SSO & API for few plans not supported on Transact platform, Setting up micro services for entity management dashboard.
 - Implementing Authorized Individual (AI) Type for entity-owned ABLE accounts across multiple plans in CSR, Fortify privacy violations.

- Updating Pennsylvania expense ratios, content updating in withdrawal flows in Missouri 529 compliance
- Snyk security violation vulnerabilities analysis, fixing.
- **Recent Completed - Sprint 9** - Resolving Snyk SQL Injection Vulnerabilities across 17 files by adding parametrized queries. Total 150 Vulnerabilities. Fixed 17. 50 are in SFRP area. Remaining 80 are targeted in next sprint
- **In Progress - Sprint 10** - Completing all the Snyk SQL Injection vulnerabilities and refining the Server-Side Request Forgery issues.

Risk / Issues/ Dependencies: NA

2. Team Alchemy

Key Highlights:

- Team started from 17th Sept 25 (Sprint 0)
- **Work completed areas in 7 Sprints** -
 - QIPs on Unite, Fortify violations, UI changes, Sardine implementation for Kofax paper withdraw (Unite, Librisk, Librisk web).
 - Sardine implementation for Kofax paper Withdrawal (ABLE, 529) . Go live 16th Dec.
 - Sardine Integration with Kofax Withdrawal live in Production, QIPs on Unite and Analysis for Sardine for Kofax paper Enrollment
 - Implementation for Sardine Integration with Kofax Enrollment (529), Update iSave529 and IN Contribution dropdown went live on Dec 31st.
 - Sardine 529 plans Integration Enrollment - AO, JAO, Guardian and Bank Verification.2 QIP's to update overnight fee logic.
- **Recent Completed - Sprint 9** - 1) Kofax Sardine integration for enrollment- AO, JAO, Guardian and Bank Verification along with 2 QIPs went to production on 30 Jan.
2) Completed Check, EBT/AIP for 529 Plans in QC4, ABLE- Backend logic and library update for Guardian and Bank verification is completed.
- **Sprint 10**- a) Kofax Sardine Integration Enrollment - Complete all remaining flows for Able (Owner, Guardian, AIP, Bank, Check, EBT/AIP) & 529 (EBT/AIP, Check) in Feb release on 20th Feb
b) QIP - Update overnight fee for NDD

Risk / Issues/ Dependencies: NA

3. Team Odyssey

- Odyssey's Previous release
 - NY UE - 1/23 - Completed
 - Umbraco Migrations: 1/30 - Completed
 - NYD
 - NYA
 - Performance Enhancements to IDP Tool added to scope
- **Odyssey's Upcoming release**
 - WI UE enablement (Desktop + Mobile) - **2/22**
 - Kansas (UE enablement) - **3/1**
- Process Metrics: [Team Odyssey Metrics - Jira](#)
- Metric insights for Jan :
 - Throughput increased compared to last month
 - Less bugs created this month but % of remaining bugs in the backlog increased
 - Flow Metrics Cycle time decreased in Jan, showing downward trend.
- December Share-out link: [Team Odyssey Monthly Shareout - Jan 2026](#) Conducted on Feb 4th.
- Upcoming Monthly Share out - Planned on Feb 25th.
- Enablement Queue: [Enablement Queue.ppt](#)

Risk / Issues/ Dependencies:

- Defects turnaround time is slower than expected from cross teams, causing delays in QA completion, overall release readiness, posing a direct risk on the release timelines, additional pressure on QA team in the final week.
 - Mitigation - Adherence of SLA (code freeze date) by all the teams to ensure defects fixes, validation, closure.
- Ongoing changes in business priority, diluting team focus, leading to reduced predictability, & operational efficiency
- New scope of UI changes (as per new Figma) performed in the release additionally

4. Team Synergy (QIPs and tier 1 triage support)

- Synergy Key Deliverables (Jan)
 - **104 RT Tickets** Went ABOVE our general RT target of 85-95 in Jan.
 - 5 QIPs None were overdue.
 - 4 stories - All relating to PII Dashboard Initiative
- Process metrics can be found here: [Synergy metrics dashboard](#).
- Metric insights:
 - Highest throughput in RTs to date, 104 RTS completed in the month of January.
- Confluence page for Synergy can be found clicking [here](#).
- Scope of current and upcoming work can be consulted in Aha! by clicking [here](#).
- Focus Area - GenAI tools (Co-Pilot and Cursor AI) to improve the throughput.

- Last Share-out link: [Team Synergy Monthly Shareout Dec-25](#) Team Synergy Monthly Shareout Dec - Conducted on January 14th.
- Upcoming Monthly Share out - Planned on Feb 11th.

Risk / Issues/ Dependencies: PII automation development completion is subject to resolution of dependencies on DevOps support like environment readiness, pipeline availability deployment schedules and approvals from security compliance team

Improvements:

- Cursor AI Agent usage to manage the content creations request.
- PII automation development - Implementation & Testing of Reverse payroll, Excess contribution and Reverse bounce RTs on Stage 1. ETA ~ Feb month

5. Automation Team

Detailed Reference: [QA Automation Leadership Update – 02/18](#)

One-Line Summary

QA Automation continues to execute strongly across Prime v2 (381+ cases), Prime v3 (255+ IDP/UE), API, and Performance; execution is no longer the constraint—ownership, pipeline direction, and intake discipline are the gating factors. Leadership alignment on migration ownership, V3 charter, pipeline finalization, and capacity protection is requested.

Key Highlights

- **Prime V2 – Sustain/Closure:** Regression scaled to 381+ test cases with stable daily execution; all 7 core modules closed; edge case coverage and flakiness resolved. Offshore owns nightly regression, RCA, and release readiness. Expansion to CAT + QC in progress; C5 moved to CAT with lighter CSR suite. Legacy IDP migration support (KSD, NYD) with gap analysis for reversals, exchanges, and funds.
- **Prime V3 – IDP & Universal Enrollment Expansion:** Coverage at ~255+ test cases driven by NYD, IDP changes (e.g., international phone), web registration, CSR account maintenance, profile updates, IDP login (positive, negative, forgot password, links). UE significantly expanded; Unite V3 growing. Working with Dom on pipeline; Entity planned for later. IDP stable with minimal flaky under investigation; next expansion: IDP transaction flows.
- **Regression Growth & Stability:** V2 and V3 coverage expanded; nightly stability maintained; multi-environment (Stage1, CAT, QC) support in progress. Offshore operates independently with daily RCA ownership and predictable handoffs.
- **Platform-Independent Automation Enablement:** Stage 5 CAT support; Docker automation integration validation; Scrum-of-Scrum pipeline coordination; release failure investigations and bug resolution. Ad-hoc support ongoing—often outside planned intake.
- **API & Performance Foundations:** API auth slice and Auth + Metadata suites implemented and validated in Stage1/QC4; running in QC4. Environment strategy for portability in progress; SME collaboration done; ready for regression once pipeline finalized. Performance: QA ownership; auth flows stabilized; Priti on enrollment, withdrawal, account creation, login; Blazemeter config and manual doc in progress; baseline to nightly planned—blocked on pipeline direction.
- **Critical Release & War-Room Support:** QA Automation is the default validation layer for release testing, platform efforts, and cross-team dependencies. Increasing test volume and ad-hoc requests are putting pressure on capacity and JIRA hygiene; intake discipline and capacity protection (part-time BA/admin) requested.

In Progress / Next Focus

- **Prime V2:** Sustain/closure; multi-environment (CAT, QC) expansion; no new scope.
- **Prime V3:** Pipeline enablement with Dom; IDP transaction flows; Entity nightly onboarding later; charter alignment (full successor vs. UE/IDP-only).
- **API Automation:** Finalize pipeline direction (GitLab vs. GitHub); lightweight regression for Account Services & Auth; CI/CD execution (no ad-hoc).
- **Performance Testing:** Repeatable regression suite; baseline cases to nightly pipeline; execution cadence—pending pipeline direction.

Initiatives & Execution Highlights

- **V2 Scale & Multi-Environment:** Regression at 381+ cases with CAT/QC expansion; C5 to CAT; migration support and gap analysis (reversals, exchanges, funds) enable release readiness across environments.
- **Offshore Ownership at Scale:** Offshore team operates independently with nightly regression, RCA, and release readiness; predictable handoffs and reduced onshore dependency.
- **V3 Organic Growth:** IDP, UE, web registration, CSR, profile coverage at 255+ cases; pipeline work with Dom; scope/charter alignment with leadership needed.
- **API & Performance Readiness:** Auth and Metadata suites ready for pipeline; Performance baseline and scripts in progress—blocked on GitLab vs. GitHub decision for nightly execution.
- **Program Maturity:** Execution is strong; gating factors are now ownership (migration, V3 charter), pipeline direction, capacity protection, and intake discipline—leadership alignment requested.

Call-Out for Leadership

QA Automation is executing strongly; execution is no longer the constraint.

- Plans migrating Legacy IDP without QA notification cause reactive rework and regression noise.
- Prime v3 scope is expanding without an agreed charter.
- API and Performance are technically ready but blocked on pipeline direction (GitLab vs. GitHub).
- Increasing volume and ad-hoc support are pressuring capacity and JIRA hygiene. Continued success requires alignment on:
 1. Migration ownership and advance notification
 2. Prime v3 charter
 3. pipeline finalization (Gitlab/GitHub)

4. part-time BA/scrum admin for intake and backlog health
5. intake discipline—no ad-hoc QA work outside JIRA.

Date: 2/5/2026

Staffing:

- Ascensus Persistent Teams: <https://confluence.ascensus.com/x/Hbw8Eg>
- [Persistent Team Roster](#)
- Requirement tracker: [Ascensus GS Resource Status Tracker_2025.xlsx](#)
- New Offboarding -
 - Anagha Jadhav

Open / In-Progress: Requirements: Persistent

Chapter Lead	Cost Center	Position	Location	Name	Status	Remarks
New						
Rajib Akhtar - CI/CD Pipeline	182002	DevOps Architect	Onshore	Chaitanya Bojja	Closed	Onboarded
	182002	DevOps Engineer	Onshore	Naga Santosh	Closed	Onboarded
	182002	DevOps Engineer	Onshore	Venkata S Naidu	Closed	Onboarded
	182002	DevOps Architect	Onshore	Ryan Johnson	Closed	Onboarded
	182002	DevOps Engineer	Onshore	Ronnie Jermaine	Closed	VM awaited. ETA 6th Feb
Gerald Matthews	182001	Jave Angular UI Developer	Nearshore	Horeb Misael Gastelum Miramontes - PSL	Closed	Onboarded
	182001	Jave Angular UI Developer	Nearshore	TBC	Open	Interviews are in progress
Replacements						
Gerald Matthews	182001	Scrum Master - Cosmos & Alchemy	Offshore	Kiran	Selected	Backup Interviews are in progress
	182001	QA Dev	Offshore	Chandan Kumar	Closed	Onboarded
Arun Dash	24525	Synergy Offshore Lead	Offshore	Suresh Mahto	Closed	Onboarded

Open / In-Progress: Requirements: Abstra / Assertia

Chapter Lead	Cost Center	Position	Location	Name	Status	Remarks
New						
Rajib Akhter	181090	Java Tech Lead	Nearshore	Eri Otero - Assertia	Closed	NA
	181090	Java Senior Software Engineer	Nearshore	Edwin Sánchez - Assertia	Closed	NA
	181090	Java Senior Software Engineer	Nearshore	GUSTAVO ARAUJO - Abstra	Closed	NA
	181090	Java Senior Software Engineer	Nearshore	Ernesto Mendez	Closed	NA
	181090	Java Senior Software Engineer	Nearshore	Douglas Capeletti	Closed	NA
Gerald Mathews	181090	QA Automation	Nearshore	Felipe	Closed	NA

Recently Released Team Member: Persistent

Name	Project	Skill	Location	Chapter Lead	Release Date
Anagha Jadhav	DB Prod Support	Oracle PL/SQL	Offshore	Lide Winburn	31 Jan 2026

Budget Tracker

Budget tracker for 2025: [Ascensus GS Budget Tracker_2025.xlsx](#)

Budget tracker for 2026: [Ascensus GS Budget Tracker_2026.xlsx](#)

Delivery Updates:

SUMMARY HIGHLIGHTS:


Teams	Key Summary																										
Cosmos	- Implementing Authorized Individual (AI) Type for entity-owned ABLE accounts across multiple plans in CSR - Snyk security violation vulnerabilities. Total 17 vulnerabilities fixed in recent sprint. ~ 25-30 are targeted next sprint. - Root cause identification, code knowledge upgrade - Team progress towards maturity focus, getting deeper understanding, showcasing improvements in KPIs Next steps: Completion of all open Synk security vulnerabilities fixing	Key Metrics <table><tr><th>Metric</th><th>1</th><th>2</th><th>3</th><th>4</th></tr><tr><td>Throughout (# Stories completed)</td><td>110</td><td>105</td><td>145</td><td>140</td></tr><tr><td>Velocity (avg of completed last 3 sprints)</td><td>100</td><td>100</td><td>135</td><td>130</td></tr><tr><td>% Complete</td><td>85</td><td>80</td><td>105</td><td>100</td></tr><tr><td>Cycle Time of Stories (Days)</td><td>10</td><td>8</td><td>5</td><td>5</td></tr></table>	Metric	1	2	3	4	Throughout (# Stories completed)	110	105	145	140	Velocity (avg of completed last 3 sprints)	100	100	135	130	% Complete	85	80	105	100	Cycle Time of Stories (Days)	10	8	5	5
Metric	1	2	3	4																							
Throughout (# Stories completed)	110	105	145	140																							
Velocity (avg of completed last 3 sprints)	100	100	135	130																							
% Complete	85	80	105	100																							
Cycle Time of Stories (Days)	10	8	5	5																							
Alchemy	- Implementation for Sardine Integration Enrollment for 529 plans (AO, JAO, Guardian and Bank Verification flows) along with 2 QIPs went live on 30th Jan - Kofax Sardine Integration Enrollment for remaining ABLE & 529 flows ((Owner, Guardian, AIP, Bank, Check, EBT/AIP)), targeting 20th Feb release - Team progress towards maturity focus, strengthening capability, domain understanding, showcasing improvements in KPIs Next Steps: Completion of Kofax Sardine integration Enrollment work for the flows in scope	Key Metrics <table><tr><th>Metric</th><th>1</th><th>2</th><th>3</th><th>4</th></tr><tr><td>Throughout (# Stories completed)</td><td>105</td><td>95</td><td>95</td><td>140</td></tr><tr><td>Velocity (avg of completed last 3 sprints)</td><td>95</td><td>90</td><td>90</td><td>125</td></tr><tr><td>% Complete</td><td>85</td><td>70</td><td>65</td><td>105</td></tr><tr><td>Cycle Time of Stories (Days)</td><td>12</td><td>10</td><td>5</td><td>5</td></tr></table>	Metric	1	2	3	4	Throughout (# Stories completed)	105	95	95	140	Velocity (avg of completed last 3 sprints)	95	90	90	125	% Complete	85	70	65	105	Cycle Time of Stories (Days)	12	10	5	5
Metric	1	2	3	4																							
Throughout (# Stories completed)	105	95	95	140																							
Velocity (avg of completed last 3 sprints)	95	90	90	125																							
% Complete	85	70	65	105																							
Cycle Time of Stories (Days)	12	10	5	5																							
Odyssey	- Recently delivered - NY UE on 1/23 & Umbraco Migrations on 1/30 successfully, well collaborating with cross functional teams. Next Steps: - - WI UE enablement (Desktop + Mobile) - 2/22 - Kansas (UE enablement) - 3/1 - VA ABLE IDP in QC4 - 2/5 - VA ABLE IDP in Stage1 - 2/11 - VA Entity Management Dashboard - 2/18 - Wisconsin UE in stage1 - 2/9 - Michigan UE in stage1 - Feb addition (TBD) - Trowe changes in stage 1 - 3/20 Suggestions: - Adherence of SLA (code freeze date) by all other teams to ensure defects fixes, validation, closure before code freeze date. - Ongoing changes in business priority, diluting team focus, leading to reduced predictability, & operational efficiency	<table><tr><th>Metric</th><th>1</th><th>2</th><th>3</th><th>4</th><th>5</th></tr><tr><td>Cycle Time</td><td>50</td><td>85</td><td>30</td><td>60</td><td>60</td></tr><tr><td>Throughput</td><td>45</td><td>80</td><td>25</td><td>50</td><td>45</td></tr></table>	Metric	1	2	3	4	5	Cycle Time	50	85	30	60	60	Throughput	45	80	25	50	45							
Metric	1	2	3	4	5																						
Cycle Time	50	85	30	60	60																						
Throughput	45	80	25	50	45																						

Synergy

- 104 RT tickets achieved (above set target of 80).
- 5 QIPs, 4 stories (PII Dashboard project)
 - Implementation & Testing of Reverse payroll, Excess contribution and Reverse bounce RTs on Stage1
- Expecting shift in focus from RTs due decentralizing initiative

Next steps: KT ongoing to support triage decentralization initiative. PII Dashboard automation work validation in Stage 1

Throughput

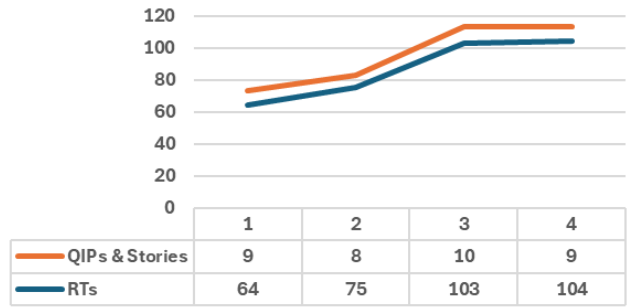

Last 4 Months

QA Automation

- Prime V2 -Closure of flacky cases. New coverage of enrollment, regression, registration, web login, and withdrawal scenarios
- Prime V3 – IDP & Universal Enrollment Expansion
- API & Performance Foundations:

Next Steps:


Prime V3: Enable Unite pipeline for IDP Web Registration and UE CSR Withdrawals; expand regression post-pipeline; advance IDP transaction workflows.

AI

AI Adoption, Benefits -

- Number of associates usage- All
- Usage areas- Analysis, Development, Code Review, Unit testing, document generation mainly
- Tools - Usage of Copilot, Cursor AI majorly and other tools like GPT models, Gamm app, Claude, Gitlab Due AI, JIRA built in AI assistants

Total Tokens for entire team extracted from Cursor report



1. Team Cosmos

Key Highlights:

- Team started from 17th Sept 25 (Sprint 0)
- **Work completed areas in 8 Sprints -**
 - 529 Unite portal Matching grant eligibility, Fortify privacy violations, Advisor management Rep search, TN stars, John Hancock 529, Matching grant opt-in letter feature
 - Enable Transact (Higher One) expansion for MT, IA, NV and MD state plans in stage. Secure Page Enhancements – Updated new treasurer logo swap for enable savings plan.
 - Uniform email address for all email types in ABLE and 529 plans,
 - Matching Grant Opt_in Letter for Paper enrollments, Removal of SSO & API for few plans not supported on Transact platform, Setting up micro services for entity management dashboard.
 - Implementing Authorized Individual (AI) Type for entity-owned ABLE accounts across multiple plans in CSR, Fortify privacy violations.
 - Updating Pennsylvania expense ratios, content updating in withdrawal flows in Missouri 529 compliance
 - Snyk security violation vulnerabilities analysis, fixing.
- **Recent Completed - Sprint 9** - Resolving Snyk SQL Injection Vulnerabilities across 17 files by adding parametrized queries. Total 150 Vulnerabilities. Fixed 17. 50 are in SFRP area. Remaining 80 are targeted in next sprint
- **In Progress - Sprint 10** - Completing all the Snyk SQL Injection vulnerabilities and refining the Server-Side Request Forgery issues.

Risk / Issues/ Dependencies: NA

2. Team Alchemy

Key Highlights:

- Team started from 17th Sept 25 (Sprint 0)
- **Work completed areas in 7 Sprints -**
 - QIPs on Unite, Fortify violations, UI changes, Sardine implementation for Kofax paper withdraw (Unite, Librisk, Librisk web).
 - Sardine implementation for Kofax paper Withdrawal (ABLE, 529) . Go live 16th Dec.
 - Sardine Integration with Kofax Withdrawal live in Production, QIPs on Unite and Analysis for Sardine for Kofax paper Enrollment
 - Implementation for Sardine Integration with Kofax Enrollment (529), Update iSave529 and IN Contribution dropdown went live on Dec 31st.
 - Sardine 529 plans Integration Enrollment - AO, JAO, Guardian and Bank Verification. 2 QIP's to update overnight fee logic.
- **Recent Completed - Sprint 9** - 1) Kofax Sardine integration for enrollment- AO, JAO, Guardian and Bank Verification along with 2 QIPs went to production on 30 Jan.
2) Completed Check, EBT/AIP for 529 Plans in QC4, ABLE- Backend logic and library update for Guardian and Bank verification is completed.
- **Sprint 10**- a) Kofax Sardine Integration Enrollment - Complete all remaining flows for Able (Owner, Guardian, AIP, Bank, Check, EBT/AIP) & 529 (EBT/AIP, Check) in Feb release on 20th Feb
b) QIP - Update overnight fee for NDD

Risk / Issues/ Dependencies: NA

3. Team Odyssey

- Odyssey's Previous release
 - NY UE - 1/23 - Completed
 - Umbraco Migrations: 1/30 - Completed
 - NYD
 - NYA
 - Performance Enhancements to IDP Tool added to scope
- **Odyssey's Upcoming release**
 - WI UE enablement (Desktop + Mobile) - **2/22**
 - Kansas (UE enablement) - **3/1**
- Process Metrics: [Team Odyssey Metrics - Jira](#)
- Metric insights for Jan :
 - Throughput increased compared to last month
 - Less bugs created this month but % of remaining bugs in the backlog increased
 - Flow Metrics Cycle time increased compared to last month Mostly due to Lead time and Queue time
 - Some items for NY UE remained in the backlog since the first planned release but had to be postponed.
- December Share-out link: [Team Odyssey Monthly Shareout - Jan 2026](#) Conducted on Feb 4th.
- Upcoming Monthly Share out - Planned on Feb 25th.
- Enablement Queue: [Enablement Queue.ppt](#)

Risk / Issues/ Dependencies:

- Defects turnaround time is slower than expected from cross teams, causing delays in QA completion, overall release readiness, posing a direct risk on the release timelines, additional pressure on QA team in the final week.
 - Mitigation - Adherence of SLA (code freeze date) by all the teams to ensure defects fixes, validation, closure.
- Ongoing changes in business priority, diluting team focus, leading to reduced predictability, & operational efficiency

4. Team Synergy (QIPs and tier 1 triage support)

- Synergy Key Deliverables (Jan)
 - **104 RT Tickets** Went ABOVE our general RT target of 85-95 in Jan.
 - 5 QIPs None were overdue.
 - 4 stories - All relating to PII Dashboard Initiative
- Process metrics can be found here: [Synergy metrics dashboard](#).
- Metric insights:
 - Highest throughput in RTs to date, 104 RTS completed in the month of January.
- Confluence page for Synergy can be found clicking [here](#).
- Scope of current and upcoming work can be consulted in Aha! by clicking [here](#).
- Focus Area - GenAI tools (Co-Pilot and Cursor AI) to improve the throughput.
- Last Share-out link: [Team Synergy Monthly Shareout Dec-25](#) Team Synergy Monthly Shareout Dec - Conducted on January 14th.
- Upcoming Monthly Share out - Planned on Feb 11th.

Risk / Issues/ Dependencies: PII automation development completion is subject to resolution of dependencies on DevOps support like environment readiness, pipeline availability deployment schedules and approvals from security compliance team

Improvements:

- Cursor AI Agent usage to manage the content creations request.
- PII automation development - Implementation & Testing of Reverse payroll, Excess contribution and Reverse bounce RTs on Stage 1. ETA ~ Feb month

5. Automation Team

Detailed Reference: [QA Automation Leadership Update – 02/04](#)

One-Line Summary

QA Automation closed V2 flakiness and expanded V3 IDP/UE coverage this cycle—completed integration analysis, stabilized regression, advanced API & performance foundations, and continued as the default validation layer for emergency releases and platform-level initiatives. Leadership alignment on intake discipline remains essential.

Key Highlights

- **Prime V2 – Closure Achieved:** Integration analysis completed; all known flaky cases closed across modules. New coverage added for enrollment, regression, registration, web login, and withdrawal scenarios. Modules confirmed up to date; documentation fully refreshed. Regression execution and reporting remain stable and repeatable.
- **Prime V3 – IDP & Universal Enrollment Expansion:** IDP login flows expanded; CSR IDP profile update and member update automation added. Universal Enrollment scenarios updated with additional coverage. V3 flakiness stabilized. IDP transaction workflows in progress. V3 now primary automation surface for IDP and UE in Stage 1.
- **Regression Growth & Stability:** V2 and V3 coverage expanded; nightly stability maintained. Offshore team owns daily execution, analysis, and early-morning readiness. Execution model operational and sustainable.
- **Platform-Independent Automation Enablement:** Supporting Scrum-of-Scrums for environment-agnostic regression; Stage 5 CAT access obtained; smoke suite creation pending. Enabling execution across Stage 2, Stage 5, CAT, and other regions as needed.
- **API & Performance Foundations:** Auth server finalized for pipeline prototype. Metadata integration in progress; CMS collaboration on account metadata and validation rules. Postman and Swagger incorporated. Performance: Priti with Nick on IDP analysis; new scripts created; API performance regression targeting mid-Feb.
- **Critical Release & War-Room Support:** QA Automation is the default validation layer for emergency releases, platform upgrades (Apache 2.4.x, Stage 5 CAT), and cross-team dependencies—often outside planned intake. Requests are urgent and valid but not consistently capacity-aligned.

In Progress / Next Focus

- **Prime V2:** Residual Login work; no new scope.
- **Prime V3:** Enable Unite pipeline for IDP Web Registration and UE CSR Withdrawals; expand regression post-pipeline; advance IDP transaction workflows.
- **API Automation:** Finalize lightweight regression for Account Services & Auth APIs; schedule CI/CD execution (no ad-hoc testing).
- **Performance Testing:** Package existing assets into repeatable regression suite; introduce API performance regression by mid-Feb; align execution and reporting cadence.

Initiatives & Execution Highlights

- **V2 Integration Rigor:** Detailed analysis surfaced and resolved integration issues; systematic flaky closure and withdrawal fine-tuning improved reliability.
- **Offshore Ownership at Scale:** Offshore engineers independently own nightly regression, failure triage, and early-morning readiness, enabling faster defect detection and reducing onshore dependency.
- **API Intake Discipline:** Auth server prototype and metadata-driven development establish a structured path for API automation; CMS collaboration clarifies validation expectations.
- **Performance Baseline Build:** IDP performance analysis and new scripts lay groundwork for mid-Feb API regression; Priti building familiarity with enrollment and account-related performance tests.
- **Program Maturity:** Automation program has shifted from coverage build-out to stability, pipeline enablement, and operational excellence—positioned to support both roadmap and critical release needs.

Call-Out for Leadership

QA Automation is now a dependency for emergency releases, platform upgrades, and cross-environment testing. Sustained unplanned support can slow roadmap delivery, delay pipeline expansion, and reduce predictability. Continued success requires alignment on intake discipline and prioritization to protect roadmap work while supporting critical business needs—this is a decision point, not a complaint.

Date: 1/22/2026

Staffing:

- Ascensus Persistent Teams: <https://confluence.ascensus.com/x/Hbw8Eg>
- [Persistent Team Roster](#)
- Requirement tracker: [Ascensus GS Resource Status Tracker_2025.xlsx](#)
- New Offboarding -
 - Anthony Cesar Ortiz Arteaga
 - Rahul Vishwakarma
 - Harshal Bhoge

Open / In-Progress: Requirements: Persistent

Chapter Lead	Cost Center	Position	Location	Name	Status	Remarks
New						
Mark Foong - CI/CD Pipeline	182002	DevOps Architect	Onshore	Chaitanya Bojja	Closed	Onboarded
	182002	DevOps Engineer	Onshore	Naga Santosh	Closed	Onboarded
	182002	DevOps Engineer	Onshore	Venkata S Naidu	Selected	Onboarding in progress
	182002	DevOps Architect	Onshore	Ryan Johnson	Selected	Onboarding in progress
	182002	DevOps Engineer	Onshore	Ronnie Jermaine	Selected	Onboarding in progress
	182002	DevOps Engineer	Onshore	TBC	In Progress	Interviews are in progress
	TBC	Data Architect	Onshore	Tao Jhao	Selected	Onboarding in progress
	182002	Java Lead	Onshore	TBC	In Progress	Interviews are in progress
Gerald Matthews	181090	Jave Angular UI Developer	Nearshore	Horeb Misael Gastelum Miramontes - PSL	Closed	Onboarded
Replacements						
Gerald Matthews	182001	Scrum Master - Cosmos & Alchemy	Offshore	TBC	In Progress	Interviews are in progress

Open / In-Progress: Requirements: Abstra / Assertia

Chapter Lead	Cost Center	Position	Location	Name	Status	Remarks
New						
Rajib Akhter	181090	Java Tech Lead	Nearshore	Eri Otero - Assertia	Selected	NA
	181090	Java Senior Software Engineer	Nearshore	Edwin Sánchez - Assertia	Selected	NA
	181090	Java Senior Software Engineer	Nearshore	GUSTAVO ARAUJO - Abstra	Selected	NA
	181090	Java Senior Software Engineer	Nearshore	Ernesto Mendez	Selected	NA

	181090	Java Senior Software Engineer	Nearshore	Douglas Capeletti	Selected	NA
Gerald Mathews	181090	QA Automation	Nearshore	Felipe	Selected	NA

Upcoming Team Member Release: Persistent

Name	Project	Skill	Location	Chapter Lead	Release Date
Anagha Jadhav	DB Prod Support	Oracle PL/SQL	Offshore	Lide Winburn	31 Jan 2026

Budget Tracker

Budget tracker for 2025: [Ascensus GS Budget Tracker_2025.xlsx](#)

Budget tracker for 2026: [Ascensus GS Budget Tracker_2026.xlsx](#)

Delivery Updates:

SUMMARY HIGHLIGHTS:


Teams	Key Summary
Cosmos	- Implementing Authorized Individual (AI) Type for entity-owned ABLE accounts across multiple plans in CSR - Snyk security violation vulnerabilities - Sprint completion rate has marked uplift (100%) over the last two sprints, reflecting stronger planning, disciplined execution. Next steps: Roadmap covers Synk security violations work mainly
Alchemy	- Implementation for Sardine Integration Enrollment for 529 plans. Go Live on 30th Jan - Starting ABLE plans in current sprint - Sprint completion rate and other metrics has marked uplift in last 2 sprints Next Steps: Continue enhancements in planning, handling unknowns etc, continue uplift in the metrics maturity. Sardine in roadmap
Odyssey	- Focus on current release on 23rd Jan - Umbraco migration, UE enrollment for NY, Accounts migration work. - Delayed cross team defect fixes & introduction of new work of enhancing account migration utility tool, imposing pressure on release readiness Next Steps: Explore more AI if possible, to handle the unplanned scope additions. Refining stories breakdown, helpful for increasing throughput, reducing cycle time. - Adherence of SLA (code freeze date) by all other teams to ensure defects fixes, validation, closure before code freeze date. - Kansas work on priority in the roadmap. Commitment as per capacity
Synergy	103 RT tickets achieved (above set target of 80). 11 QIPs - Consistent increase in Throughput - Internal PII App is a big focus for this month. First functionality rollout on Stage1 ~14th Jan Demoed 1/14, in progress with DevOps to get it into Stage1 Next steps: PII automation work progress.
QA Automation	- Prime V3 - IDP & Universal Enrollment - Regression Growth & Stability: Automation coverage expanded materially (v2: ~250 284, v3: ~140 250) while maintaining nightly stability - API & Performance Foundations: API automation baseline, documentation, and intake model established. - Critical Release & War-Room Support as QA Automation involvement is needed in unplanned critical business scenarios like emergency releases, platform upgrades, and cross-environment testing Next Steps: Prime V2 for flaky cases resolutions, V3 - Enable Unite pipeline to operationalize IDP Web Registration and UE CSR Withdrawals; expand regression execution post-pipeline. API Automation: Finalize lightweight regression for priority Account Services & Auth APIs and schedule CI/CD execution (no ad-hoc testing). Performance Testing: Package existing assets into a repeatable regression suite with aligned execution and reporting cadence.

AI

AI Adoption, Benefits -

- [Number of associates usage](#)- All
- [Usage areas](#) - Analysis, Development, Code Review, Unit testing, document generation mainly
- [Tools](#) - Usage of Copilot, Cursor AI majorly and other tools like GPT models, Gamm app, Claude, Gittlab Due AI, JIRA built in AI assistants

Total Tokens for entire team extracted from Cursor report



1. Team Cosmos

Key Highlights:

- Team started from 17th Sept 25 (Sprint 0)
- **Work completed areas in 7 Sprints -**
 - 529 Unite portal Matching grant eligibility, Fortify privacy violations, Advisor management Rep search, TN stars, John Hancock 529, Matching grant opt-in letter feature
 - Enable Transact (Higher One) expansion for MT, IA, NV and MD state plans in stage. Secure Page Enhancements – Updated new treasurer logo swap for enable savings plan.
 - Uniform email address for all email types in ABLE and 529 plans,
 - Matching Grant Opt_in Letter for Paper enrollments, Removal of SSO & API for few plans not supported on Transact platform, Setting up micro services for entity management dashboard.
 - Implementing Authorized Individual (AI) Type for entity-owned ABLE accounts across multiple plans in CSR, Fortify privacy violations.
 - Updating Pennsylvania expense ratios, content updating in withdrawal flows in Missouri 529 compliance
- **Recent Completed - Sprint 8 -** 1) CSR enhancements for Authorized Individual (AI) Type for all entity-owned ABLE accounts. 2) Snyk security violation vulnerabilities
- **In Progress - Sprint 9 -** Resolving Snyk SQL Injection Vulnerabilities.

Risk / Issues/ Dependencies: NA

Improvements

- AI Usage - Cursor, Copilot, Jira AI usage in activities like QA automation, Legacy code analysis, Code review, SQL optimization.
- Sprint completion rate has marked uplift (100%) over the last 3sprints, reflecting stronger planning, disciplined execution.

2. Team Alchemy

Key Highlights:

- Team started from 17th Sept 25 (Sprint 0)
- **Work completed areas in 7 Sprints -**
 - QIPs on Unite, Fortify violations, UI changes, Sardine implementation for Kofax paper withdraw (Unite, Librisk, Librisk web).
 - Sardine implementation for Kofax paper Withdrawal (ABLE, 529) . Go live 16th Dec.
 - Sardine Integration with Kofax Withdrawal live in Production, QIPs on Unite and Analysis for Sardine for Kofax paper Enrollment
 - Implementation for Sardine Integration with Kofax Enrollment (529), Update iSave529 and IN Contribution dropdown went live on Dec 31st.

- **Recent Completed - Sprint 8** - 1) Sardine 529 plans Integration Enrollment - AO, JAO, Guardian and Bank Verification. E2E in QC4 is Done. Present in Stage 1
2) 2 QIP's to update overnight fee logic.
- **In Progress - Sprint 9** - Sardine Integration Enrollment- Completion of EBT/AIP, Cheque flows for 529, along with 2 QIP's Production on 30th Jan . Start with Sardine ABLE Enrollment flow development

Risk / Issues/ Dependencies: NA

Improvements:

- Copilot & Cursor usage in existing code analysis, development, cross impact validation, code optimization mainly.

3. Team Odyssey

- Odyssey's Previous Release - 12/19 - Completed
 - Umbraco migrations:
 - T. Rowe
 - Maryland
 - DC
 - Idaho
- **Odyssey's Current release - 1/23**
 - NY UE
 - Umbraco Migrations:
 - NYD
 - NYA
 - Performance Enhancements to IDP Tool added to scope
- Process Metrics: [Team Odyssey Metrics - Jira](#)
- Metric insights for Dec :
 - Throughput increased compared to last month
 - Flow Metrics Cycle time decreased compared to last month from 5.3 to 4.1
 - Completed Q4 with no escape defects.
- December Share-out link: [Team Odyssey Monthly Shareout - Dec 2025](#) Conducted on Jan 7th.
- Upcoming Monthly Share out - Planned on Jan 28th.
- Enablement Queue: [Enablement Queue.ppt](#)

Risk / Issues/ Dependencies:

- Defects turnaround time is slower than expected from cross teams, causing delays in QA completion, overall release readiness, posing a direct risk on the release timelines, additional pressure on QA team in the final week.
 - Mitigation - Adherence of SLA (code freeze date) by all the teams to ensure defects fixes, validation, closure.
- IDP tool is not working as expected for high volume of records in account migration activity; had to undergo significant enhancements. This is unexpected additional work scope received, creating pressure on release readiness tasks like manage closure of cross teams defects, QA validations, follow-ups etc

Improvements:

- Copilot & Cursor usage in existing code analysis, development, QA.

4. Team Synergy (QIPs and tier 1 triage support)

- Synergy Key Deliverables (Dec)
 - **103 RT Tickets** Went ABOVE our targeted to achieve in December was 80 RTs.
 - 11 QIPs Completed all 11, none were overdue.
- Process metrics can be found here: [Synergy metrics dashboard](#).
- Metric insights:
 - Highest throughput in RTs to date, 103 RTS completed in the month of December.
- Confluence page for Synergy can be found clicking [here](#).
- Scope of current and upcoming work can be consulted in Aha! by clicking [here](#).
- Focus Area - GenAI tools (Co-Pilot and Cursor AI) to improve the throughput.
- Last Share-out link: [Team Synergy Monthly Shareout Dec-25](#) Team Synergy Monthly Shareout Dec - Conducted on January 14th.
- Upcoming Monthly Share out - Planned on Feb 11th.

Risk / Issues/ Dependencies: PII automation development completion is subject to resolution of dependencies on DevOps support like environment readiness, pipeline availability deployment schedules and approvals from security compliance team

Improvements:

- Cursor AI usage for code analysis, review, suggestions.
- Cursor AI Agent usage to manage the content creations request.
- PII automation development - Phase 1 work - Implementation & Testing of Reverse payroll, Excess contribution and Reverse bounce RTs on Stage 1. ETA ~ Jan month

5. Automation Team

Detailed Reference: [QA Automation Leadership Update – 01/21](#)

One-Line Summary

QA Automation transitioned from coverage build-out to operational maturity this cycle — closing planned v2/v3 scope, establishing API & performance foundations, enforcing governance, and serving as a critical execution partner for emergency and cross-platform initiatives.

Key Highlights

- **Prime V2 – Near Closure:** 6 of 7 modules closed. Remaining work limited to Web legacy Login and residual flaky scenarios under active cleanup. Regression execution and reporting remain stable and repeatable.
- **Prime V3 – IDP & Universal Enrollment:** IDP Login and Web Registration automation completed. CSR Withdrawal flows for Universal Enrollment (previously uncovered) added. NYD IDP coverage fully migrated from v2 to v3 related to IDP Login & UE in stage 1.
- **Regression Growth & Stability:** Automation coverage expanded materially (v2: ~250 284, v3: ~140 250) while maintaining nightly stability. Offshore team owns daily execution, analysis, and early-morning readiness.
- **Platform-Independent Automation Enablement:** Team actively supporting Scrum-of-Scrums to make automation regression environment-agnostic, enabling execution across Stage 2, Stage 5, CAT, and other regions as needed.
- **API & Performance Foundations:** API automation baseline, documentation, and intake model established. Performance testing ownership assumed for IDP flows, with regression structuring underway.
- **Critical Release & War-Room Support:** QA Automation served as a key validation partner for high-priority war-room issues and emergency production patching on 01/21, including long-weekend support. Offshore team played a critical role in rapid validation and issue identification.

In Progress / Next Focus

- **Prime V2:** Complete Login module and eliminate remaining flaky cases (no new scope).
- **Prime V3:** Enable Unite pipeline to operationalize IDP Web Registration and UE CSR Withdrawals; expand regression execution post-pipeline.
- **API Automation:** Finalize lightweight regression for priority Account Services & Auth APIs and schedule CI/CD execution (no ad-hoc testing).
- **Performance Testing:** Package existing assets into a repeatable regression suite with aligned execution and reporting cadence.

Initiatives & Execution Highlights

- **Execution Under Constraint:** The team delivered meaningful automation coverage across UI, API, and Performance despite limited SME availability, demonstrating strong ownership and rapid domain ramp-up.
- **Offshore Ownership at Scale:** Offshore engineers independently own nightly regression execution, analysis, and early-morning readiness (7:30 AM EST), enabling faster defect detection and reducing onshore dependency.
- **Quality Acceleration via AI:** Responsible adoption of AI tooling has materially improved test creation speed, debugging efficiency, and RCA quality across UI, API, and Performance automation.
- **Program Maturity Shift:** The automation program has transitioned from coverage build-out to stability, pipeline enablement, and operational excellence, positioning the team to support both roadmap and critical release needs.

Call-Out for Leadership

QA Automation is now a **dependency for emergency releases, platform upgrades, and cross-environment testing**. Continued success requires alignment on **intake discipline and prioritization** to protect roadmap delivery while supporting critical business needs.

Date: 1/8/2026

Staffing:

- Ascensus Persistent Teams: <https://confluence.ascensus.com/x/Hbw8Eg>
- [Persistent Team Roster](#)
- Requirement tracker: [Ascensus GS Resource Status Tracker_2025.xlsx](#)
- New Offboarding -
 - Anthony Cesar Ortiz Arteaga

Open / In-Progress: Requirements: Persistent

Chapter Lead	Cost Center	Position	Location	Name	Status	Remarks
--------------	-------------	----------	----------	------	--------	---------

New						
Mark Foong - CI/CD Pipeline	182002	DevOps Architect	Onshore	Chaitanya Bojja	Selected	BGV in progress. PSL onboarding will be initiated post BGV completion
	182002	DevOps Architect	Onshore	Naga Santosh	Selected	BGV in progress. PSL onboarding will be initiated post BGV completion
	182002	DevOps Engineer	Onshore	Venkata S Naidu	Selected	Sunny dropped out. Venkata S has been selected as replacement.
	182002	DevOps Engineer	Onshore	TBC	In Progress	Interviews are in progress
	182002	DevOps Engineer	Onshore	TBC	In Progress	Interviews are in progress
	182002	DevOps Engineer	Onshore	TBC	In Progress	Interviews are in progress
	TBC	Data Architect	Onshore	TBC	In Progress	Interviews are in progress
	182002	Java Lead	Onshore	TBC	In Progress	Interviews are in progress
Replacements						
Gerald Matthews	182001	Scrum Master - Cosmos & Alchemy	Offshore	TBC	In Progress	Amit Lole - Short listed Two more SM interviews will be scheduled today/ tomorrow, before making the final decision.

Open / In-Progress: Requirements: Abstra / Assertia / PSL

Chapter Lead	Cost Center	Position	Location	Name	Status	Remarks
New						
Rajib Akhter	181090	Java Tech Lead	Nearshore	Eri Otero - Assertia	Selected	NA
	181090	Java Senior Software Engineer	Nearshore	Edwin Sánchez - Assertia	Selected	NA
	181090	Java Senior Software Engineer	Nearshore	GUSTAVO ARAUJO - Abstra	Selected	NA
	181090	Java Senior Software Engineer	Nearshore	Ernesto Mendez	Selected	NA
	181090	Java Senior Software Engineer	Nearshore	Douglas Capeletti	Selected	NA
Gerald Mathews	181090	QA Automation	Nearshore	Felipe	Selected	NA
	181090	Jave Angular UI Developer	Nearshore	Horeb Misael Gastelum Miramontes - PSL	Selected	Onboarding in Progress

Offboarding List: Persistent

Name	Project	Skill	Location	Chapter Lead	Release Date
Shirish Wankhede	SFRP	Automation QA (with DB experience)	Offshore	Rajib Akhter / Dharmender Verma	12 Jan 2026
Rahul Vishwakarma	SFRP	Java Spring boot	Offshore	Rajib Akhter / Dharmender Verma	12 Jan 2026
Harshal Bhoge	SFRP	Oracle PL/SQL	Offshore	Rajib Akhter / Dharmender Verma	12 Jan 2026
Anthony Cesar Ortiz Arteaga	DevOps	Sr DevOps Engineer	Nearshore	Lide Winburn	31 Dec 2026
Anagha Jadhav	DB Prod Support	Oracle PL/SQL	Offshore	Lide Winburn	31 Jan 2026

- They were part of Ad-hoc requirements.
- They are good and trained team members on GS applications and can be utilized on any new positions in Ascensus.
- All were selected after putting lot of efforts from both Persistent and Ascensus.

Budget Tracker

Budget tracker for 2025: [Ascensus GS Budget Tracker_2025.xlsx](#)

Budget tracker for 2026: [Ascensus GS Budget Tracker_2026.xlsx](#)

Delivery Updates:

SUMMARY HIGHLIGHTS:

Teams	Key Summary								
Cosmos	- Implementing Authorized Individual (AI) Type for entity-owned ABLE accounts across multiple plans in CSR - Fortify violations analysis and reporting - Sprint completion rate has marked uplift (100%) over the last two sprints, reflecting stronger planning, disciplined execution. <u>Next steps:</u> Continue getting maturity in delivery, metrics, knowledge and more refinement in estimations								
Alchemy	- Implementation for Sardine Integration with Kofax Withdrawal (529) went live on 16th Dec. Sardine Enrollment work completion in current sprint (20th Jan) - Sprint completion rate and other metrics has marked uplift in last sprint <u>Next steps:</u> Enhancement in planning (Commitment as per capacity, handling unknowns), driving smooth delivery and uplift in the metrics maturity								
Odyssey	- Focus on Umbraco migration work - UE enrollment custom work for NY - Accounts migration work on Stage 1 and Prod <u>Next steps:</u> QA automation exploration using AI in current work. Refining stories breakdown, helpful for increasing throughput, reducing cycle time.								
Synergy	103 RT tickets achieved (above set target of 80). 11 QIPs - Consistent increase in Throughput - Internal PII App is a big focus for this month. First functionality rollout on Stage1 ~14th Jan <u>Next steps:</u> PII automation work progress.								
QA Automation	- The QA Automation team transitioned from coverage build-out to operational maturity this cycle. - Closure of all planned scope across Prime v2/v3 - Establishing API and performance foundations - Enforcing governance and demonstrating strong ownership with stable process implementation.								
All	AI Adoption, Benefits - <u>Number of associates usage-</u> All <u>Usage areas-</u> Analysis, Development, Code Review, Unit testing, document generation mainly <u>Tools -</u> Usage of Copilot, Cursor AI majorly and other tools like GPT models, Gamm app, Claude, Gitlab Due AI, JIRA built in AI assistants Total Tokens <table border="1"><thead><tr><th>Month</th><th>Total Tokens</th></tr></thead><tbody><tr><td>Oct</td><td>250,000,000</td></tr><tr><td>Nov</td><td>650,000,000</td></tr><tr><td>Dec</td><td>680,000,000</td></tr></tbody></table>	Month	Total Tokens	Oct	250,000,000	Nov	650,000,000	Dec	680,000,000
Month	Total Tokens								
Oct	250,000,000								
Nov	650,000,000								
Dec	680,000,000								

1. Team Cosmos

Key Highlights:

- Team started from 17th Sept 25 (Sprint 0)
- **Work completed areas in 6 Sprints -**
 - 529 Unite portal Matching grant eligibility, Fortify privacy violations, Advisor management Rep search, TN stars, John Hancock 529, Matching grant opt-in letter feature
 - Enable Transact (Higher One) expansion for MT, IA, NV and MD state plans in stage. Secure Page Enhancements – Updated new treasurer logo swap for enable savings plan.
 - Uniform email address for all email types in ABLE and 529 plans,
 - Matching Grant Opt_in Letter for Paper enrollments, Removal of SSO & API for few plans not supported on Transact platform, Setting up micro services for entity management dashboard.
- **Recent Completed - Sprint 7** - Updating Pennsylvania expense ratios, content updating in withdrawal flows in Missouri 529 compliance. Implementing Authorized Individual (AI) Type for entity-owned ABLE accounts across multiple plans in CSR (backend, UI, deployment, and QA). Fortify privacy violations.
- **In Progress - Sprint 8** - Extending CSR enhancements for Authorized Individual (AI) Type for entity-owned ABLE accounts. Analysis/remediation /resolutions of Fortify privacy violations where applicable

Risk / Issues/ Dependencies: NA

Improvements

- AI Usage - Cursor, Copilot, Jira AI usage in activities like QA automation, Legacy code analysis, Code review, SQL optimization. Benefited around 23% efforts in SDLC
- Sprint completion rate has marked uplift (100%) over the last two sprints, reflecting stronger planning, disciplined execution.

2. Team Alchemy

Key Highlights:

- Team started from 17th Sept 25 (Sprint 0)
- **Work completed areas in 6 Sprints -**
 - QIPs on Unite, Fortify violations, UI changes, Sardine implementation for Kofax paper withdraw (Unite, Librisk, Librisk web).
 - Sardine implementation for Kofax paper Withdrawal (ABLE, 529) . Go live 16th Dec.
 - Sardine Integration with Kofax Withdrawal live in Production, QIPs on Unite and Analysis for Sardine for Kofax paper Enrollment.
- **Recent Completed - Sprint 7** - Implementation for Sardine Integration with Kofax Enrollment (529), Update iSave529 and IN Contribution dropdown went live on Dec 31st.
- **In Progress - Sprint 8** - Completion of Enrollment for 529. 2 QIPs

Risk / Issues/ Dependencies: NA

Improvements:

- Copilot & Cursor usage in existing code analysis, development, cross impact validation, code optimization mainly. Benefited around 10% efforts in SDLC

3. Team Odyssey

- Odyssey's Previous Release - 12/19 - Completed
 - Umbraco migrations:
 - T. Rowe
 - Maryland
 - DC
 - Idaho
- Odyssey's Next release - 1/23
 - NY UE
 - Umbraco Migrations:
 - NYD
 - NYA
- Process Metrics: [Team Odyssey Metrics - Jira](#)
- Metric insights:
 - Throughput increased compared to last month
 - Flow Metrics Cycle time decreased compared to last month from 5.3 to 4.1
 - Completed Q4 with no escape defects.
- December Share-out link: [Team Odyssey Monthly Shareout - Nov 2025](#) Conducted on Jan 7th.
- Upcoming Monthly Share out - Planned on Jan 28th.
- Enablement Queue: [Enablement Queue.ppt](#)


Improvements:

- Copilot & Cursor usage in existing code analysis, development, QA. Benefited around 12% efforts in SDLC

4. Team Synergy (QIPs and tier 1 triage support)

- Synergy Key Deliverables (Dec)
 - **103 RT Tickets** Went ABOVE our targeted to achieve in December was 80 RTs.
 - 11 QIPs Completed all 11, none were overdue.

- Process metrics can be found here: [Synergy metrics dashboard](#).
- Metric insights:
 - Highest throughput in RTs to date, 103 RTS completed in the month of December.



-
- Confluence page for Synergy can be found clicking [here](#).
- Scope of current and upcoming work can be consulted in Aha! by clicking [here](#).
- Focus Area - GenAI tools (Co-Pilot and Cursor AI) to improve the throughput.
- Last Share-out link: [Team Synergy Monthly Shareout Nov](#)- Conducted on December 10th.
- Upcoming Monthly Share out - Planned on Jan 14th.

Improvements:

- Cursor AI usage for code analysis, review, suggestions. Benefited around 8% efforts in SDLC
- PII dashboard development - Phase 1 work - Implementation & Testing of Reverse payroll, Excess contribution and Reverse bounce RTs on Stage 1. ETA ~14th Jan

Initiatives:

- Cursor AI Agent usage to manage the content creations request.

5. Automation Team

Detailed Updates Reference: [QA Automation Leadership Update – 01/08](#)

Key Highlights

- **Prime V2 Regression Closure:** Automation coverage is near completion with **6 of 7 modules fully closed**. Only **Web legacy Login** remains, along with a small set of documented flaky scenarios currently under cleanup. Regression execution and reporting are stable and repeatable.
- **Prime V3 Universal Enrollment & IDP Coverage:** Web Registration (IDP) and Login automation are completed. **CSR Withdrawal flows for Universal Enrollment**, which previously had no automation coverage, have now been added. Remaining work is focused on V3 unite **pipeline enablement**, not coverage gaps.
- **Operational Maturity & Governance:** Daily regression execution, analysis, and RCA are now handled consistently by the offshore team with onshore governance. JIRA-based intake, prioritization, and execution cadence are fully enforced across UI, API, and Performance testing.
- **API & Performance Testing Enablement:** Despite limited initial SME support, the team established API automation foundations, regression structure, and documentation. Performance testing ownership has transitioned successfully, with baseline assets and regression planning underway.

Upcoming / In Progress (Key Work Items)

- **Prime V2**
 - Complete Login module
 - Resolve remaining flaky cases across modules (no new scope additions)
- **Prime V3**
 - Enable Unite pipeline to operationalize:
 - IDP Web Registration
 - CSR Withdrawal flows for Universal Enrollment
 - Expand regression execution once pipeline is available
- **API Automation**
 - Finalize lightweight regression suite for priority Account Services & Authentication APIs
 - Schedule execution via CI/CD pipeline (no ad-hoc testing)
- **Performance Testing**

- Package existing performance assets into a structured regression suite
- Establish repeatable execution and reporting cadence aligned with UI automation

Improvement Areas

- **Pipeline Dependencies:** V3 UE and IDP coverage is functionally complete; execution is pending pipeline readiness.
- **Dynamic Test Data (IDP):** SQL Server–based dynamic account retrieval remains a dependency (IDP MFA Strategy); coordination ongoing.
- **Performance Testing Standardization:** Formal planning, execution, and reporting templates are being finalized as ownership stabilizes.

Initiatives / Kudos

- **Strong Execution Under Constraints:** Team delivered meaningful automation coverage across UI, API, and Performance even when SME availability was limited, demonstrating ownership and domain ramp-up capability.
- **Offshore Ownership & Efficiency:** Offshore engineers independently performing early-morning regression analysis (7:30 AM EST), enabling faster defect detection and improved developer turnaround.
- **Governance & Process Adoption:** Successful rollout of standardized JIRA iteration model, dashboards, and intake governance — significantly improving visibility and predictability.
- **Quality Acceleration via AI:** Adoption of Cursor and GitHub Copilot has materially improved test creation speed, debugging efficiency, and RCA quality across the QE program.
- **Shift from Build-Out to Sustain & Scale:** Automation program is transitioning from coverage expansion to **stability, pipeline enablement, and operational excellence.**

Date: 12/11/25

Staffing:

- Ascensus Persistent Teams: <https://confluence.ascensus.com/x/Hbw8Eg>
- [Persistent Team Roster](#)
- Requirement tracker: [Ascensus GS Resource Status Tracker_2025.xlsx](#)
- New Offboarding -
 - Ravi Thongher
 - Roshni Pandey

Open / In-Progress: Requirements: Persistent

Chapter Lead	Cost Center	Position	Location	Name	Status	Remarks
New						
Rajib Akhter	181090	QA Automation (Sardine Implementation)	Offshore	Prachi K	Closed	Onboarded
Henry Dittmer	24525	QA Automation	Offshore	Priti Choudhary	Closed	Onboarded
Mark Foong - CI/CD Pipeline	TBC	DevOps Architect	Onshore	Chaitanya Bhoj	Selected	BGV in progress. PSL onboarding will be initiated post BGV completion
	TBC	DevOps Architect	Onshore	Naga Santosh	Selected	BGV in progress. PSL onboarding will be initiated post BGV completion
	TBC	DevOps Engineer	Onshore	Sunny Akhtar	Selected	BGV in progress. PSL onboarding will be initiated post BGV completion
	TBC	DevOps Engineer	Onshore	TBC	In Progress	Interviews are in progress
	TBC	Data Architect	Onshore	TBC	In Progress	Interviews are in progress
	TBC	Java Lead	Onshore	TBC	In Progress	Interviews are in progress
Replacements						

Gerald Matthews	182001	QA Lead - Alchemy (Replacement)	Offshore	Saranya B	Closed	Onboarded
		Scrum Master - Cosmos & Alchemy	Offshore	TBC	Open	Akhilesh's movement is rejected by Carl. Interviews are in progress.

Open / In-Progress: Requirements: Abstra / Assertia / PSL

Chapter Lead	Cost Center	Position	Location	Name	Status	Remarks
New						
Rajib Akhter	181090	Java Tech Lead	Nearshore	Eri Otero - Assertia	Selected	NA
	181090	Java Senior Software Engineer	Nearshore	Edwin Sánchez - Assertia	Selected	NA
	181090	Java Senior Software Engineer	Nearshore	GUSTAVO ARAUJO - Abstra	Selected	NA
	181090	Java Senior Software Engineer	Nearshore	FABIAN PAULINO GARCIA - PSL	Selected	BGV in progress. PSL onboarding will be initiated post BGV completion
	181090	Java Senior Software Engineer	Nearshore		In Progress	NA
Gerald Mathews	181090	QA Automation	Nearshore		Open	
	181090	Jave Angular UI Developer	Nearshore		Open	

Budget tracker: [Ascensus GS Budget Tracker_2025.xlsx](#)

Delivery Updates:

SUMMARY HIGHLIGHTS:

Teams	Key Summary
Cosmos	- JH & AK work is completed successfully as per agreed timelines. - Fortify violations analysis and reporting - Improvement in the Cursor automation coverage in Dev & QA areas
Alchemy	Sardine implementation work for Kofax paper withdraw (ABLE & 529) and Enrolment is continued, targeting completion by 23rd Dec
Odyssey	- Focus on Umbraco migration work - Improvement in the Cursor automation coverage in Dev (~80%)
Synergy	75 RT tickets achieved (above set target of 65-70) - Consistent increase in Throughput
QA Automation	- Continuous monitoring of Prime V2 Regression & V3 Universal Enrollment in 24*7 shift (via onsite-offshore coverage). Fail-Highlight-Resolve fast approach. 100% pipeline stability for V3 UE - New work - Prime V3 IDP Login automation & API Regression Suite - Significant uplift in test volume (+30%) within weeks; strong team momentum while onboarding new hires.

<u>All</u>	AI Adoption - - For Cursor AI - - Number of associates usage- All - Number of Tokens - 143% increase from Oct to Nov, expecting usage continuation in Dec - Usage in Document generation, Code review, Impact analysis - Other tools - Usage of Copilot, Cursor AI majorly and other tools like GPT models, Gamm app, Claude, Gitlab Due AI, JIRA built in AI assistants - Next steps - Velocity/Throughput monitoring in progress.
------------	---

1. Team Cosmos

Key Highlights:

- Team work started from 17th Sept 25 (Sprint 0)
- Work completed areas in 4 Sprints** - 529 Unite portal Matching grant eligibility, Fortify privacy violations, Advisor management Rep search, TN stars, John Hancock 529, Matching grant opt-in letter feature
- Recent Complete** - Sprint 5 -
 - Comprehensive support for John Hancock postproduction activities
 - Fortify Privacy violation issues
 - Enable Transact (Higher One) expansion for MT, IA, NV and MD state plans in stage. Secure Page Enhancements – Updated new treasurer logo swap for enable savings plan.
- In Progress - Sprint 6** - Uniform email address for all email types in ABLE and 529 plans, Matching Grant Opt_in Letter for Paper enrollments, Removal of SSO & API for few plans not supported on Transact platform, Setting up micro services for entity management dashboard.

Risk / Issues/ Dependencies: NA

Improvements

- Cursor, Copilot, Jira AI usage in activities like QA automation, Legacy code analysis, Code review, SQL optimization
 - Automation % approx.. - 80% in Analysis, 40% in Dev, 60% in QA

2. Team Alchemy

Key Highlights:

- Team work started from 17th Sept 25 (Sprint 0)
- Work completed areas in 4 Sprints** - QIPs on Unite, Fortify violations, UI changes, Sardine implementation for Kofax paper withdraw (Unite, Librisk, Librisk web)
- Recent Complete** - Sprint 5 - Sardine implementation for Kofax paper Withdrawal (ABLE, 529) . Go live 16th Dec
- In Progress** - Sprint 6 - Analysis and dev start for Sardine for Kofax paper Enrollment


Risk / Issues/ Dependencies: NA

Improvements:

- Copilot & Cursor usage in existing code analysis, development, cross impact validation, code optimization mainly.
 - Automation % approx.. - 80% in Analysis, 40% in Dev, 60% in QA

3. Team Odyssey

- Odyssey's Previous Release - 11/23. Completed
- Odyssey's Upcoming Release - 12/19
 - Umbraco migrations:
 - T. Rowe
 - Maryland
 - DC
 - Idaho
- Process Metrics: [Team Odyssey Metrics - Jira](#)
- Metric insights:
 - Flow Metrics System and lead team are both down this month as expected.
 - Flow Metrics Cycle time increased compared to last month but overall has a descending trend:

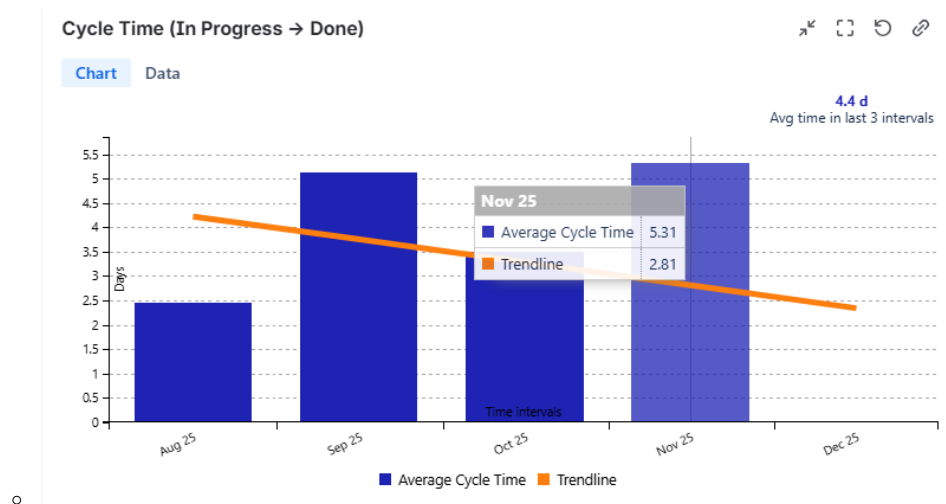


- November Share-out link: [Team Odyssey Monthly Shareout - Nov 2025](#) Conducted on Dec 3rd.
- Upcoming Monthly Share out - Planned on Dec 31st.
- Enablement Queue: [Enablement Queue.ppt](#)

Improvements:

- Copilot & Cursor usage in existing code analysis, development, QA.
 - Automation % approx... - 80% in Dev, 40% in QA

4. Team Synergy (QIPs and tier 1 triage support)

- Synergy Key Deliverables (Oct)
 - **75 RT Tickets** Went ABOVE our targeted to achieve in November was 65-70 RTs.
 - 7 QIPs Completed all 7, none were overdue.
 - 1 story (features) Non overdue.
- Process metrics can be found here: [Synergy metrics dashboard](#).
- Metric insights:
 - We expect the throughput to plateau starting this month until we have a breakthrough with enabling offshore to more data keeping in mind PII constraints.

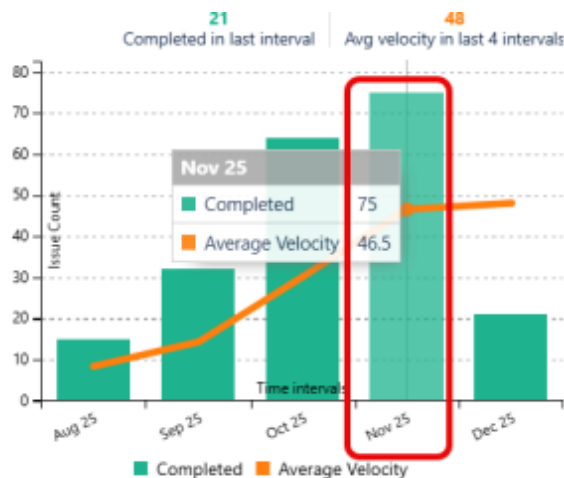

- Confluence page for Synergy can be found clicking [here](#).
- Scope of current and upcoming work can be consulted in Aha! by clicking [here](#).
- Focus Area - GenAI tools (Co-Pilot and Cursor AI) to improve the throughput.
- Last Share-out link: [Team Synergy Monthly Shareout Nov](#)- Conducted on December 10th.
- Upcoming Monthly Share out - Planned on Jan 14th.

Improvements:

- Cursor AI usage (~40%) for code analysis, review, suggestions, PII dashboard development

Initiatives:

- Cursor AI Agent usage to manage the content creations request.

5. Automation Team

Detailed Updates Reference: [Leadership Report – Nov 20, 2025](#)

Key Highlights

- Prime V2 Regression Suite: 4 of 7 modules fully closed with SME sign-off docs; enrollment (legacy + specific + advisor + ABLE) added across multiple plans. Stability improved to 85–90%.
- Prime V2 Coverage Growth: Suite expanded from 181 ~275+ cases; major gaps in enrollment and ABLE flows closed.
- Prime V3 Universal Enrollment: Pipeline remains 99–100% stable; nightly runs reviewed daily by offshore team.
- Prime V3 IDP Login Automation: Positive/negative/forgot-password/forgot-username flows completed; planned pipeline integration this week.
- Documentation Uplift: All V2/V3 regression suite details updated on Confluence (plans, scenarios, sign-off structure).

Upcoming / In Progress (Key Work Items)

- Add IDP Login suite to V3 pipeline; expand UE regression to more plan types (Direct, ABLE, IDP, non-IDP). *ETA* - 12 Dec 2025
- Begin API regression suite (Account Services & Auth Server API validation) and plan GitLab pipeline integration - Sunil will be dedicatedly working on API process implementation per the best practices.
- Started performance testing baseline setup under Priti (IDP flow ownership transition) eventually we will have same regression suite plan what we implemented for UI Automation.
- Increase coverage for new V3 Web Registration flows for migrated IDP plans.

Improvement Areas

- MFA Hybrid Strategy: Pending Dev/SME alignment; planned for next quarter (not blocking current UE/IDP testing).
- Dynamic Data Strategy: SQL Server data retrieval solution (IDP accounts) pending collaboration with Nick.
- Regression Reporting: Offshore team trained for daily validation; monthly reporting still requires partial onshore support.
- Performance Testing Process: Need standard planning & reporting framework; ownership transition underway.

Initiatives / Kudos

- Achieved high stability across V2 and V3 regression suites with rapid flakiness reduction.
- Offshore team (Venkatesh & Dinesh) independently performing 7:30 AM daily analysis, enabling faster defect turnaround.
- Major uplift in test volume (+30%) within weeks; strong team momentum while onboarding new hires.
- AI tools (Cursor, Copilot) significantly accelerating test creation and RCA across V2, V3, & other areas of QE.
- Successful adoption of new JIRA iteration workflow—refinements, dashboards, and velocity metrics are active and improving visibility.

6. Appreciation / Work Acknowledgement:

Cosmos :

"I just want to recognize the incredible work everyone put into this JH delivery. It's been intense, but your focus, ownership, and problem-solving have been outstanding. Even under pressure, you all stayed collaborative and steady, even sacrificing the weekend to hit the code freeze. Huge thank you, amazing job getting us across the finish line."

-Anwar

Product Owner (Team Cosmos/ Alchemy)

Session: 11/13/25

Staffing:

- Ascensus Persistent Teams: <https://confluence.ascensus.com/x/Hbw8Eg>
- [Persistent Team Roster](#)
- Requirement tracker: [Ascensus GS Resource Status Tracker_2025.xlsx](#)
- Offboarding - Onsite Data engineers - Anand Madan, Pawan Gupta. Offboarded
- Roshi Pandey (Feed Analyst) Position extended till Nov 30th.

Open / In-Progress: Requirements:

Chapter Lead	Cost Center	Position	Location	Name	Status	Remarks
New						
Rajib Akhter	181090	QA Automation (Sardine Implementation)	Offshore	Saroj Sethi	Closed	Onboarded
	181090	QA Automation (Sardine Implementation)	Offshore	T Dwaragnath	Closed	Onboarded
	181090	QA Automation (Sardine Implementation)	Offshore	Prachi K	Selected	VM in Progress. ETA: 17th Nov
Henry Dittmer	24525	QA Automation	Offshore	Sunil G	Closed	Onboarded
	24525	QA Performance	Offshore	Priti Choudhary	Selected	VM in Progress. ETA 24th Nov
Replacements						
Gerald Matthews	182001	QA Lead - Alchemy (Replacement)	Offshore	Saranya B	Selected	Saranya B. Earlier selected candidate (Gayatri Naik) did not join.
	182001	BA - Alchemy (Replacement)	Offshore	Ritesh Pathak	Closed	Onboarded

Delivery Updates:

SUMMARY HIGHLIGHTS:

Teams	Key Summary
Cosmos	• Dev, QA completion of JH & AK as per plan in Sprint 3. • Regression & Partner testing of JH AK in progress.
Alchemy	Sprint 4 started on 12th Nov - Sardine implementation work for Kofax paper withdraw continuation & targeting for dev completion
Odyssey	• Upcoming Release - 11/23 - ABLE plans & Nevada Umbraco Migration key work • ~ 90% QA automation achieved using Cursor AI • Decrease in the CT and Throughput increase
Synergy	• 63 RT tickets achieved (above set target of 50-55) • Consistent increase in Throughput
QA Automation	• Regression expansion in Prime V2 & V3 UE • 100% pipeline stability for V3 UE • Jira standardization with improved visibility & traceability • Unite and Entity Management pipeline setup in progress
All	AI Adoption - • For Cursor AI - ◦ Number of associates usage- 26 ◦ Number of Tokens - 19% increase from Oct to Mid Nov, expecting ~40% by Nov End ◦ Usage in Document generation, Code review, Impact analysis • Other tools - Usage of Copilot, Cursor AI majorly and other tools like GPT models, Gamm app, Claude, Gitlab Due AI, JIRA built in AI assistants • Next steps - Velocity/Throughput monitoring in progress.

1. Team Cosmos

Key Highlights:

- **Sprint 0** - 17th to 30th Sept - Completed.
- **Sprint 1** - 1st Oct to 14th Oct - Completed. 2 stories in scope. 1) Addition of fields in Tennessee 529 Unite portal Matching grant eligibility 2) updating the messaging on login page on Franklin Templeton" 3) Fortify privacy violations (11) Analysis & closure
- **Sprint 2** - Completed. 4 stories in scope (UI changes in 'Advisor management Rep search', ' Matching grant', 'TN stars')
- **Sprint 3** - Completed. John Hancock 529 (Alaska) annual maintenance fees sweep 2025.
 - Showcased demo to John Hancock SME. Received appreciation and confirmation on the work completed
- **Sprint 4 - In Progress** - Regression & Partner testing of JH AK. Matching grant opt-in letter feature Go Live planned on 19th Nov 25

Risk / Issues/ Dependencies:

- Dependency on JH AK to complete the partner testing by 17th Nov, as code freeze is on 18th Nov

Improvements

- Sprint 1 QA automation coverage 100%. Sprint 2 QA automation in progress. 50% complete (using Cursor AI 25%)
- Cursor, Copilot, Jira AI usage in activities like QA automation, Legacy code analysis, Code review, SQL optimization

2. Team Alchemy

Key Highlights:

- **Sprint 0** - Completed.

- **Sprint 1** (1st Oct to 14th Oct) - Completed - 2 QIPs on Unite & Fortify violations (14) analysis & closure
- **Sprint 2** - Completed - 7 stories in scope (4 UI + functionality changes, 1 spike for Sardine Integration.).
- **Sprint 3** - Completed - Sardine implementation for Kofax paper withdraw (Implementing business logic in Unite)
- **Sprint 4 - In Progress** - Sardine implementation for Kofax paper withdraw (Implementing business logic in Librisk & Librisk web)


Risk / Issues/ Dependencies: NA

Improvements:

- Sprint 1 QA automation coverage 100%.
- Copilot & Cursor usage in existing code analysis, development, cross impact validation, code optimization mainly.

3. Team Odyssey

- Odyssey's Previous Release - 10/31: Completed
- Odyssey's Upcoming Release - 11/23.
 - MT ABLE
 - Nevada Umbraco Migration (Implementation)
 - ABLE - QIP - Redirect links across entity products for new UE ABLE enrollment experience - Go live on 17th Dec
- Process Metrics: [Team Odyssey Metrics - Jira](#)
- Metric insights:
 - October Cycle Time Decreased from **5.13** to **3.5 days**.
 - **Increased** throughput,

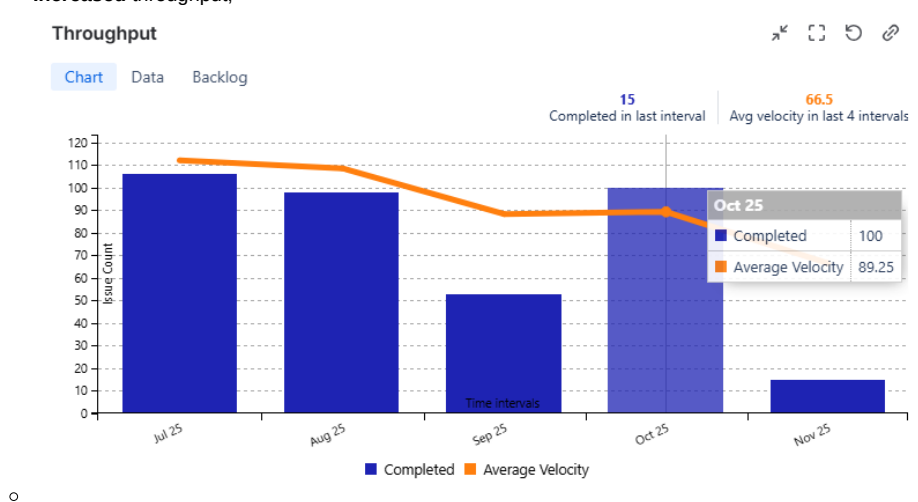


- September Share-out link: [Team Odyssey Monthly Shareout - Oct 2025](#) Conducted on Nov 5th.
- Upcoming Monthly Share out - Planned on Dec 31st.
- Enablement Queue: [Enablement Queue.ppt](#)

Improvements:

- Co-Pilot and Cursor AI usage for Dev, QA and code review activities. ~90% coverage in QA automation.

4. Team Synergy (QIPs and tier 1 triage support)

- Synergy Key Deliverables (Oct)
 - **63 RT Tickets** Went ABOVE our targeted to achieve in October is 50-55 RTs.
 - 6 QIPs Completed all 6, none were overdue.
 - 4 stories (features) All within expected time, 3 of these were ILD. Heavy month for ILD changes.
- Process metrics can be found here: [Synergy metrics dashboard](#).
- Metric insights:
 - Through put increase is consistent with the overall team goal of being a tier 1 support team to relief tier 2 volume of incidents 27% of triaged tickets were done by Synergy (almost tripled compared to last moth)

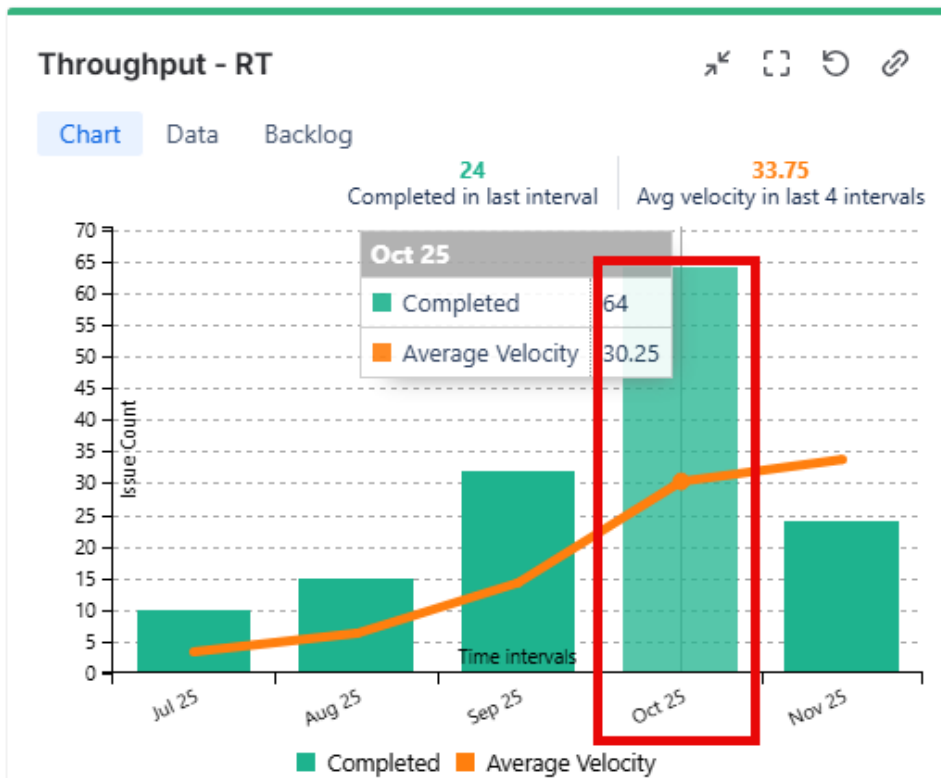

- Synergy Team took 64% of Astro related tickets Goal is 100% considering ASTRO FTP ticket outside of scope.
- Confluence page for Synergy can be found clicking [here](#).
- Scope of current and upcoming work can be consulted in Aha! by clicking [here](#).
- Focus Area - GenAI tools (Co-Pilot and Cursor AI) to improve the throughput.
- Last Share-out link: [Team Synergy Monthly Shareout Nov](#)- Conducted on November 12th.
- Upcoming Monthly Share out - Planned on Dec 10th.

Improvements:

- Cursor AI usage for code analysis, review, suggestions, PII dashboard development

Initiatives:

- Cursor AI Agent creation to manage the content creations request.

5. Automation Team

Detailed Updates Reference: [Leadership Report – Nov 12, 2025](#)

Key Highlights

- Prime V3 Universal Enrollment: Pipeline stable and running nightly (1 AM Mon–Fri). All 137 test cases now green after stabilization and data sync fixes.
- IDP Regression Suite: Positive, negative, forgot password/username flows created; integration into pipeline scheduled next week.
- Prime V2 Regression Expansion: Enrollment flows for member and CSR portals added (+ advisor plans & ABLE plans). Suite grew 25 30 %. Module sign-off documentation in progress.
- JIRA Process Implementation: New iteration workflow (DoR/DoD, refinements, retrospectives) active. Dashboards and velocity tracking operational. First refinement cycle completed successfully.
- Offshore Ownership: Daily V3 regression analysis handed over to offshore team; reduces flakiness and improves turnaround time.

Upcoming / In Progress (Key Work Items)

- Add IDP suite to Prime V3 pipeline and expand coverage to 4 plans.
- Continue ABLE plan evaluation and multi-plan coverage for V2 & V3.
- Initiate Unite and Entity Management pipeline setup (post UE stabilization).
- Conduct JIRA retrospectives and reviews as part of new cadence.
- Prepare leadership sign-off documents per module for release regression reuse.

Improvement Areas

- MFA Hybrid Strategy: Dev review in progress – target final solution mid-Nov.
- Dynamic Data Retrieval: Cross-DB integration (Oracle SQL Server) with Nick underway.
- Reporting Handover: Offshore team trained for daily regression validation; monthly reporting handover by mid-Nov.

Initiatives / Kudos

- Team successfully achieved 100 % pipeline stability for V3 Universal Enrollment.
- Offshore team independently handling daily regression analysis and bug validation.
- JIRA standardization completed – improved visibility and traceability across automation initiatives.
- AI enablement (*Copilot*, *Cursor* & *Gitlab Duo*) actively used by team for code generation and test data creation.

Session: 10/30/25

Staffing:

- Ascensus Persistent Teams: <https://confluence.ascensus.com/x/Hbw8Eg>
- [Persistent Team Roster](#)
- Requirement tracker: [Ascensus GS Resource Status Tracker_2025.xlsx](#)
- Offboarding - Onsite Data engineers - Anand Madan, Pawan Gupta. Need to initiate their offboarding on 1st Nov.
- Roshi Pandey (Feed Analyst) Position extended till Nov 30th.

Open / In-Progress: Requirements:

Chapter Lead	Cost Center	Position	Location	Name	Status	Remarks
New						
Rajib Akhter	181090	QA Automation (Sardine Implementation)	Offshore	Saroj Sethi	Closed	Onboarded
	181090	QA Automation (Sardine Implementation)	Offshore	T Dwaragnath	Closed	Onboarded
	181090	QA Automation (Sardine Implementation)	Offshore	Prachi K	Selected	BGV and Onboarding in Progress. ETA: 10th Nov
Henry Dittmer	24525	QA Automation	Offshore	Sunil G	Selected	Onboarding in Progress. ETA: 4th Nov
	24525	QA Performance	Offshore	TBC	In Progress	Interviews are in progress.
Replacements						
Gerald Matthews	182001	QA Lead - Alchemy (Replacement)	Offshore	Gayatri Nayak	Selected	BGV in progress. Persistent Joining Date: 12th Nov. Ascensus Start Date: 17th Nov
	182001	BA - Alchemy (Replacement)	Offshore	Ritesh Pathak	Selected	Onboarding in Progress. ETA: 4th Nov

Budget tracker: [Ascensus GS Budget Tracker_2025.xlsx](#)

Delivery Updates:

1. Team Odyssey - Green


- Odyssey's Previous Release - 10/03
- Odyssey's Upcoming Release - 10/31. QA Signoff Received.
 - Delaware ABLE Entity Management - **Green**
 - MS ABLE Entity Management - **Green**
 - CT ABLE Day2 item work (Management Entity link change) - **Green**
 - Nevada Umbraco Migration (Analysis only) - **Green**
- Process Metrics: [Team Odyssey Metrics - Jira](#)
- Metric insights:
 - October Cycle Time Decreased from **5.13** to **3.4 days** (awaiting month closure)
- September Share-out link: [Team Odyssey Monthly Shareout - September 2025 - Government Savings- Software Development. - Ascensus - Confluence](#) - Conducted on 24th September
- Enablement Queue: [Enablement Queue.ppt](#)
- Focus Area - GenAI tools (Co-Pilot and Cursor AI) to improve the throughput.

Initiatives:

- 2 Tier code reviews - Onsite tech lead needs access for 1st level of MR approvals. Currently managing manually
- Co-Pilot and Cursor AI usage for Dev, QA and code review activities

2. Team Synergy (QIPs and tier 1 triage support) - Green

- Synergy Key Deliverables (Oct)
 - **53 RT Tickets** Targeted to achieve in October is 50-55 RTs. 🍌
 - 6 QIPs 1 more to go this month.
 - 3 stories (features)
- Process metrics can be found here: [Synergy metrics dashboard](#).
- Metric insights:
 - System time, Lead time and Cycle time are all trending down.
 - These were very low as most throughput this month was RTs.
 - Through put increase is consistent with the overall team goal of being a tier 1 support team to relief tier 2 volume of incidents 10% of triaged tickets were done by Synergy

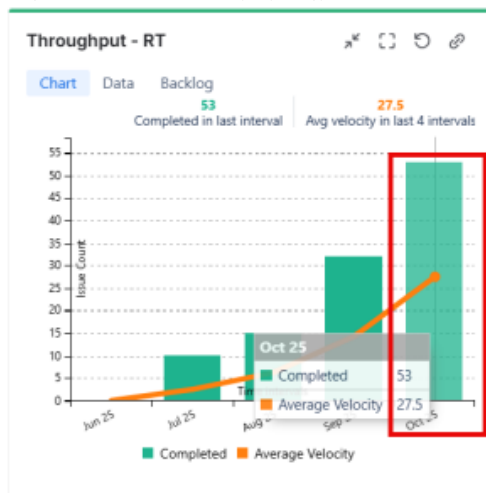

- Using AI tools, analyzed "Knowledge Gap" tickets are led by ASTRO, which was trained this month—setting us up for higher throughput next month.
- Confluence page for Synergy can be found clicking [here](#).
- Scope of current and upcoming work can be consulted in Aha! by clicking [here](#).
- Focus Area - GenAI tools (Co-Pilot and Cursor AI) to improve the throughput.
- Last Share-out link: [Team Synergy Monthly Shareout Oct-25](#)- Conducted on 9th October
- Upcoming Monthly Share out - Planned on Nov 12th.

Initiatives:

- Co-Pilot and Cursor AI usage for Dev, QA and code review activities

3. Automation Team - Green

Detailed Updates Reference: [Leadership Report – Oct 29, 2025](#)

Key Highlights:

- Prime V3 Universal Enrollment pipeline successfully added and now running nightly (Mon–Fri, 1 AM) — 137 test cases executed, all **Green**.
 - Baseline stabilized, failures fixed, and expanded coverage validated with SMEs.
- Jira process implementation completed — dashboards live, first refinement done this week; iteration, DOR/DOD standards, and visibility process finalized with Brenda.
- Prime V2 regression suite expanded by 25+% (181 239 test cases); module closure and SME sign-off documentation in progress.
- ABLE test cases for both Prime V2 & V3 added; evaluating additional plan variations (IDP, non-IDP, NAA vs non-NAA).
- Supporting IDP performance testing (Nick & Sree Pallavi) and CAT environment smoke test preparation.

Upcoming / In Progress (Key Work Items):

- Expand Prime V3 regression coverage to include IDP Login (positive / negative / forgot password / username) across 3–4 plans.
- Finalize SME sign-off workflow for module closure to support release regression optimization.
- Continue ABLE plan evaluation and add remaining test cases to nightly regression.
- Begin exploration of Unite & Entity Management pipelines — next in line after UE.
- Standardize JIRA documentation templates and meeting cadence (refinements, reviews, retros).

Improvement Areas:

- MFA hybrid strategy for IDP flows under Dev review – target finalization early Nov.
- Dynamic data strategy (Oracle vs SQL Server) – collaborating with Nick to automate IDP account retrieval.
- Reporting handover: Offshore team under training or daily regression analysis (7:30 AM EST); full monthly reporting transition in progress.

Initiatives:

- Co-Pilot and Cursor AI usage for automation creation

4. Team Cosmos - Green

Key Highlights:

- Sprint 0 - 17th to 30th Sept - Completed.
- **Sprint 1** - 1st Oct to 14th Oct - Partially went live. 2 stories in scope. 1) Addition of fields in Tennessee 529 Unite portal Matching grant eligibility - **Go live planned on 31st Oct** 2) updating the messaging on login page on Franklin Templeton" - Went live on 15th Oct 3) Fortify privacy violations (11) Analysis & closure
- **Sprint 2** - 4 stories in scope (UI changes in 'Advisor management Rep search', ' Matching grant', 'TN stars'), **Go live on 31st Oct**
- **Current Sprint - Sprint 3** - John Hancock 529 (Alaska) annual maintenance fees sweep 2025

Risk / Issues -

- Due to business criticality and urgency, JHAK work is scoped in Sprint 3. However, foresee a risk of completion due to potential unknowns and complexities that may arise.
- Dependency on JHAK to validate the functionality within given timelines

Improvements - Sprint 1 QA automation coverage 100%. Sprint 2 QA automation in progress

5. Team Alchemy - Green

Key Highlights:

- Sprint 0 - Completed.
- **Sprint 1** (1st Oct to 14th Oct) - Partially went live - 2 QIPs on Unite (1 went live on 15th Oct and **2nd planned on 31st Oct**) & Fortify violations (14) analysis & closure
- **Sprint 2** - 7 stories in scope (4 UI + functionality changes, 1 spike for Sardine Integration,). **Go live on 31st Oct**
- **Current sprint - Sprint 3** - Sardine implementation for Kofax paper withdraw

Risk / Issues: NA

Improvements - Sprint 1 QA automation coverage 100%.

Session: 10/16/25

Staffing:

- Ascensus Persistent Teams: <https://confluence.ascensus.com/x/Hbw8Eg>
- [Persistent Team Roster](#)
- Requirement tracker: [Ascensus GS Resource Status Tracker_2025.xlsx](#)

- Offboarding - Anuj Kohli (In Progress)

Open / In-Progress:: Requirements:

Chapter Lead	Cost Center	Position	Location	Name	Status	Remarks
New						
Dharmender Verma	182005	Java Developer	Offshore	Rahul Vishwakarma	Closed	Onboarded
Lide Winburn	24525	Java Developer	Offshore	Pramod Matsagar	Closed	Onboarded
	24525	QA Automation	Offshore	Ajay Kushwah	Closed	Onboarded
Rajib Akhter	181090	QA Automation (Sardine Implementation)	Offshore	Saroj Sethi	Closed	Ascensus Onboarding in progress. ETA - 22nd Oct
	181090	QA Automation (Sardine Implementation)	Offshore	T Dwaragnath	Closed	Ascensus Onboarding in progress. ETA - 22nd Oct
	181090	QA Automation (Sardine Implementation)	Offshore	TBC	In Progress	Interviews are in progress
Henry Dittmer	24525	QA Automation	Offshore	TBC	In Progress	Interviews are in progress
	24525	QA Performance	Offshore	TBC	In Progress	Interviews to be scheduled
Replacements						
Gerald Matthews	182001	QA Lead - Alchemy (Replacement)	Offshore	Gayatri Nayak	Selected	BGV in progress. ETA:: 10th Nov
	182001	BA - Alchemy (Replacement)	Offshore	TBV	In Progress	Interviews are in progress

Budget tracker: [Ascensus GS Budget Tracker_2025.xlsx](#)

Delivery Updates:

1. Team Odyssey - Green

- Odyssey's Previous Release - 10/03
 - PA Direct Universal Enrollment (Desktop + Mobile)
 - Assisted Innovator team for PA GSP QA - Regressing testing on Stage 1 and Sanity testing on Prod environment
 - CT ABLE Entity Management
 - ABLE MFA for NY
 - New York Secure / Public Site Navigation (QIP)
 - *All 4 items were released with no escape defects to date.*
- Odyssey's Upcoming Release - 10/31
 - Delaware ABLE Entity Management - **Green**
 - MS ABLE Entity Management - **Green**
 - CT ABLE Day2 item work (Management Entity link change) - **Green**
 - Nevada Umbraco Migration (Analysis only) - **Green**
- Process Metrics: [Team Odyssey Metrics - Jira](#)
- Metric insights:
 - September Cycle Time Increased to **5.13 days** Major contributors were regression testing of plans that were descopeed early September (NY and PA)
 - Flow Metrics Start time has improved a lot (faster prioritization), but work takes longer once started. Net result is **faster overall delivery (system + lead times are healthier)**.
 - Although overall flow metrics improved, backlog **continues to grow steadily** because throughput hasn't caught up.
- September Share-out link: [Team Odyssey Monthly Shareout - September 2025 - Government Savings- Software Development. - Ascensus - Confluence](#) - Conducted on 24th September
- Enablement Queue: [Enablement Queue.ppt](#)
- Focus Area - GenAI tools (Co-Pilot and Cursor AI) to improve the throughput.

Initiatives:


- Estimation enhancements and sprint work commitment based on team Capacity. Encouraging no late work scoping
- 2 Tier code reviews - Onsite tech lead needs access for 1st level of MR approvals. Currently managing manually
- Final sign off from QA, end of every release to decide Production Go/NoGo
- Co-Pilot and Cursor AI implementations in development and QA areas

Improvement Areas:

- Controlling regression recurring issues from other teams. Need UE regression pack integration with CI-CD to catch the issues fast and respective owners to fix the same and avoid risk of release delays
- 3rd Oct release observation - Change of approach in Branch separation process during deployment.
- Release plan discussion of all existing (known) production defects, identified during release testing

2. Team Synergy (QIPs and tier 1 triage support) - Green

- Synergy Key Deliverables (Sept)
 - **32 RT Tickets** [Work item search - JIRA](#). Targeting to achieve (**ACHIEVED!**) ~ 30 to 35 RT tickets in September.
 - October goal is 50-55 RTs.
 - 2 QIPs [Work item search - JIRA](#). Due to increasing complexity, 4 QIPs were descoped from Sept and placed into the Oct 3rd release.
 - 0 non-QIPs stories
- Process metrics can be found here: [Synergy metrics dashboard](#).
- Metric insights:
 - System time, Lead time and Cycle time are all trending down.
 - These were very low as most throughput this month was RTs.
 - Through put increase is consistent with the overall team goal of being a tier 1 support team to relief tier 2 volume of incidents 10% of triaged tickets were done by Synergy

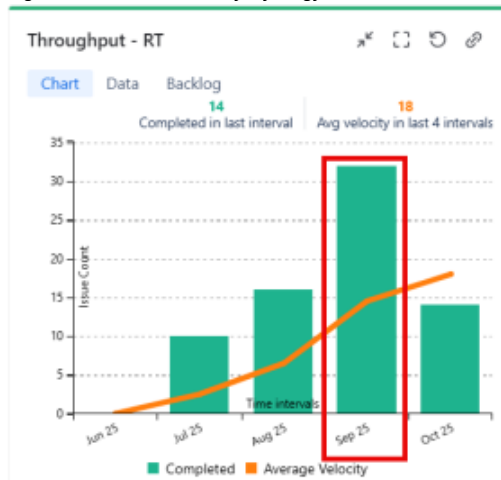

- Using AI tools, analyzed "Knowledge Gap" tickets are led by ASTRO, which was trained this month—setting us up for higher throughput next month.
- Confluence page for Synergy can be found clicking [here](#).
- Scope of current and upcoming work can be consulted in Aha! by clicking [here](#).
- Focus Area - GenAI tools (Co-Pilot and Cursor AI) to improve the throughput.
- Last Share-out link: [Team Synergy Monthly Shareout Oct-25](#)- Conducted on 9th October
- Upcoming Monthly Share out - Planned on Nov 12th.

Initiatives:

- Estimation enhancements and QIPs commitment based on team Capacity.
- 2 Tier code reviews - Onsite tech leads have got access for 1st level of MR approvals
- Co-Pilot and Cursor AI implementations in development

3. Automation Team - Green

Detailed Updates Reference: [Leadership Report – Oct 15, 2025](#)

Key Highlights:

- Expanded regression coverage for Prime V2 and Prime V3 (UE + IDP flows) — positive and negative test cases completed; MFA blocker for IDP login currently under Dev review.
- ABLE-related test cases integrated into the regression suite (V2 & V3), evaluation and optimization in progress.
- Supporting Sardine regression testing and IDP performance testing/documentation in collaboration with Sree Pallavi and Nick – ongoing high priority area

Upcoming / In Progress (Key Work Items):

- Prime V3 GitLab pipeline setup nearing completion – Selenium Grid/CSV path issue under fix with DevOps. ~ ETA: Oct 18
- Working with Brenda to standardize backlog visibility, iteration cycles, and JIRA dashboards for the automation team.
- Continuing NeoLoad vs BlazeMeter evaluation for future performance testing strategy and process standardization.

Improvement Areas:

- Reporting cadence (automation dashboards and weekly visibility) under refinement – will be aligned with the new JIRA process implementation.
- MFA hybrid fix for IDP flows under review with the Dev team.

- Daily regression suite execution report analysis – handover to Venkatesh for initial review; if bugs are identified, Swapnil leads follow-up and resolution.

4. Team Cosmos - Green

- Sprint 0 - 17th to 30th Sept - Completed.
- Sprint 1 - 1st Oct to 14th Oct - Completed 2 stories in scope. 1) Addition of fields in Tennessee 529 Unite portal Matching grant eligibility - Go live planned on 31st Oct 2) updating the messaging on login page on Franklin Templeton" - Go live on 15th Oct 3) Fortify privacy violations (11) Analysis & closure
- Sprint 2 - 4 stories in scope (UI changes in 'Advisor management Rep search', ' Matching grant', 'TN stars'), Fortify privacy violations
- Risk / Issues - Insufficient backlog items

5. Team Alchemy - Green

- Kick-off Call done on 2/9/2025
- Code Setup / Access Software and Repository Access: Completed
- Sprint 0 - 17th to 30th Sept - Completed. Backlog refinement for further sprints is progressing.
- Sprint 1 - 1st Oct to 14th Oct - Completed. 2 QIPs on Unite (1 Go live on 15th Oct and 2nd planned on 31st Oct) & Fortify violations (14) analysis & closure
- Sprint 2 - 7 stories in scope (5 UI + functionality changes, 1 spike for Sardine Integration, Fortify violations (3))
- Risk / Issues :
 - Insufficient backlog prioritization
 - QA Lead - Rajesh Meshram - Resigned
 - Replacement Candidate - Gayatri Naik Selected. BGV in progress.
 - BA - Shivali Pawar - Replacement planned; interviews are in progress

Feedback:

Team Synergy:

- **Sanchita D** (Offshore Lead). She has shown exceptional technical expertise and reliability. Sanchita consistently delivers high-quality solutions, from resolving complex RT tickets to providing clear onboarding documentation and supporting team members with technical guidance.
- **Krishna R** (Onshore Lead). He has been instrumental in driving our projects forward with diligence and leadership. Krishna's commitment to supporting team operations—eg. handling Astro RTs, leading knowledge transfer sessions. He continues to push us forward aggressively and has a tremendous delivery mindset. Star player.
- **Brenda Montoya** (Scrum Master). Brenda excels at organizing team processes, maintaining clear documentation, and facilitating effective communication across teams. Her attention to detail in backlog management, triage meetings, and process improvement initiatives has greatly enhanced our team's efficiency and accountability.

Team Odyssey:

- **QA Team:** QA group has been thorough in testing and often asked to retest due to several variables inside and out the team. They test willingly and without hesitation as the situation calls for it. I would highlight the leadership from Savita and her continued work to coordinate with the team and other teams.

Session: 10/1/25

Staffing:

- Ascensus Persistent Teams: <https://confluence.ascensus.com/x/Hbw8Eg>
- Requirement tracker: [Ascensus GS Resource Status Tracker_2025.xlsx](#)
- Offboarding - Mahesh Kumar Yerram (Completed), Sagar Rath (Completed)
- All GS Persistent members moved from Anuj Kohli to Piyush Pawar

Rolling Requirements:

Chapter Lead	Cost Center	Position	Location	Name	Status	Remarks
Dharmender Verma	182005	Java Automation Dev	Offshore	Rahul Vishwakarma	Selected	BGV/ Persistent onboarding in progress. ETA: 6th Oct.
	24525	Java Developer	Offshore	Pramod Matsagar	Closed	Ascensus onboarding in progress. ETA: 6th Oct.

Lide Winburn						
	24525	QA Automation	Offshore	Ajay Kushwah	Closed	Ascensus onboarding in progress. ETA: 6th Oct.
Rajib Akhter	181090	QA Automation	Offshore	Saroj Sethi	Selected	BGV/ Persistent onboarding in progress. ETA: 13th Oct.
	181090	QA Automation	Offshore	TBC	In Progress	Interviews are in Progress

Aniket Dubey - Java developer has been onboarded to Ascensus for Team Cosmos/ Alchemy. This is an investment position

Budget tracker: [Ascensus GS Budget Tracker_2025.xlsx](#)

Delivery Updates:

1. Team Odyssey - Green

- Odyssey's Latest Release - 9/7
 - Nevada Patch Release (Day 2 items)- 9/7
- Odyssey's Next Release - 10/03
 - PA Direct Universal Enrollment (Desktop + Mobile) - **Green**
 - CT ABLE Entity Management - **Green**
 - ABLE MFA for NY - **Green**
 - New York Secure / Public Site Navigation (QIP) - **Green**
- Process Metrics: [Team Odyssey Metrics - Jira](#)
- Metric insights (unchanged from last share-out):
 - Cycle Time Increased to **5.13 days**
 - Flow Metrics Start time has improved a lot (faster prioritization), but work takes longer once started. Net result is **faster overall delivery (system + lead times are healthier)**.
 - Although overall flow metrics improved, backlog **continues to grow steadily** because throughput hasn't caught up.
- September Share-out link: [Team Odyssey Monthly Shareout - September 2025 - Government Savings- Software Development. - Ascensus - Confluence](#) - Conducted on 24th September
- Enablement Queue: [Enablement Queue.ppt](#)
- Focus Area - GenAI tools (Co-Pilot and Cursor AI) to improve the throughput.

2. Team Synergy (QIPs and tier 1 triage support) - Green

- Synergy Key Deliverables (Sep)
 - 31 RT Tickets** [\[Team Synergy - RT Tickets Completed Last Month \(Dashboard\)\] Work item search - JIRA](#). Targeting to achieve (**ACHIEVED!**) ~ 30 to 35 RT tickets in September.
 - 2 QIPs [\[Team Synergy - QIPs Completed Last Month \(Dashboard\)\] Work item search - JIRA](#). Due to increasing complexity, 4 QIPs were descope from Sept and placed into the Oct 3rd release.
 - 0 non-QIPs stories
- Process metrics can be found here: [Synergy metrics dashboard](#).
- Metric insights:
 - RT tickets have nearly doubled compared to August! ~ 93% improvement** in throughput month-over-month.
- Confluence page for Synergy can be found clicking [here](#).
- Scope of current and upcoming work can be consulted in Aha! by clicking [here](#).
- Focus Area - GenAI tools (Co-Pilot and Cursor AI) to improve the throughput.
- Monthly Shareout - Planned on 8th Oct

3. Automation Team - Green

Detailed Updates Reference: [Leadership Report – Sep 17, 2025](#)

Key Highlights:

- Regression coverage with new/negative test cases (including ABLE & systematic withdrawal) and stabilized UE/IDP flows on Prime Version 3 framework - In Progress
- Regression testing for Sardine - In Progress. High Priority -ETA - 3rd Oct
- Performance testing support for IDP login deadlock issue - High Priority - Completed

Upcoming / In Progress (Key Work Items):

- Prime V3 GitLab pipeline setup (UE + IDP regression) in progress; access/configuration pending Ops..
 - Pipeline delays due to first-time Ops setup; Dev-Ops is working on it. ~ ETA - Oct 3rd.
- Able related test cases to be added to regression test suite
- Exploring Cursor AI for regression test suite automation

Improvement Areas:

- Reporting cadence (qTest dashboards & daily/weekly email automation) requires further streamlining and KT handoff to offshore team - In Progress - 80 % completed. ETA Oct 15th
- Daily Regression Suite Execution Report Analysis - Handover to offshore - In Progress - 90 % completed - ETA Oct 10th

4. Team Cosmos - Green

- Kick-off Call done on 2/9/2025
- Code Setup / Access Software and Repository Access: Completed
- Sprint 0 - 17th to 30th Sept - Completed. Backlog refinement for further sprints is progressing.
- Sprint 1 - 1st Oct to 14th Oct - Started. 2 stories are scoped (Addition of fields in Tennessee 529 Unite portal Matching grant eligibility & updating the messaging on login page on Franklin Templeton)
- Risk / Issues - NA

5. Team Alchemy - Green

- Kick-off Call done on 2/9/2025
- Code Setup / Access Software and Repository Access: Completed
- Sprint 0 - 17th to 30th Sept - Completed. Backlog refinement for further sprints is progressing.
- Sprint 1 - 1st Oct to 14th Oct - Started. 2 QIPs on Unite are scoped (Updating contents on NAA Secure page and renaming label links on personal details page)
- Risk / Issues :
 - QA Lead - Rajesh Meshram - Resigned - Working on his replacement. Interviews are planned.

Session: 9/18/25

Staffing:

- Ascensus Persistent Teams: <https://confluence.ascensus.com/x/Hbw8Eg>
- Requirement tracker: [09-12-2025 Ascensus GS Resource Status Tracker.xlsx](#)
- Offboarding - Mahesh Kumar Yerram (In-Progress), Sagar Rath (Completed)

Rolling Requirements:

Chapter Lead	Cost Center	Position	Location	Name	Status	Remarks
Lide Winburn	181090	Data Engineer (Support)	Offshore	Anagha Jadhav	Closed	
Dharmender Verma	182005	Java Automation Dev	Offshore	TBC	Open	Interviews are in progress
Lide Winburn	24525	Java Developer	Offshore	Pramod Matsagar	Selected	BGV/ Persistent onboarding in progress. ETA: 6th Oct.
	24525	QA Automation	Offshore	TBC	Open	Interviews are in progress

Team - Cosmos

Scrum Master will be shared between these two teams

Chapter Lead	Cost Center	Position	Location	No of Positions	No of Selections	Name of Selected Candidates	External /Internal	Projected Onboarding Date (Ascensus)	Status
Arun Dash	181090	Java Tech Lead	Onsite	1	1	Pragna Koneru	Internal	Onboarded	Closed
	181090	Dev Lead	Offshore	1	1	Kaushik Dutta	Internal	Onboarded	Closed
	181090	QA Lead	Offshore	1	1	Sampada Kulkarni	Internal	Onboarded	Closed
	181090	Java Developer	Offshore	1	1	Vijay Pingili	Internal	Onboarded	Closed
	181090	QA Developer	Offshore	1	1	Avinash Savekar	Internal	Onboarded	Closed
	181090	BA	Offshore	1	1	Anoop Naik	Internal	Onboarded	Closed
	181090	Scrum Master	Offshore	1	1	Brahmomoy Bose	Internal	Onboarded	Closed

Team - Alchemy

Scrum Master will be shared between these two teams

Chapter Lead	Cost Center	Position	Location	No of Positions	No of Selections	Name of Selected Candidates	External /Internal	Projected Onboarding Date (Ascensus)	Status
Gerald Matthews	181090	Java Tech Lead	Onsite	1	1	Sushma P	External	Onboarded	Closed
	181090	Dev Lead	Offshore	1	1	Ravindra Kumar Dhyani	Internal	Onboarded	Closed
	181090	QA Lead	Offshore	1	1	Rajesh Meshram	Internal	Onboarded	Closed
	181090	Java Developer	Offshore	1	1	Mudhshar Uddin	Internal	Onboarded	Closed
	181090	QA Developer	Offshore	1	1	Payal Rout	Internal	Onboarded	Closed
	181090	BA	Offshore	1	1	Shivali Pawar	Internal	Onboarded	Closed

Budget tracker: [09-12-2025 Ascensus GS Budget Tracker.xlsx](#)

Delivery Updates:

1. Team Odyssey - Green

- Odyssey's Latest Release - 9/7
 - Nevada Patch Release (Day 2 items)- 9/7
- Odyssey's Next Release - 10/03
 - PA Direct Universal Enrollment (Desktop + Mobile)
 - CT ABLE Entity Management
 - ABLE MFA for NY
 - New York Secure / Public Site Navigation (QIP)
- Process Metrics: [Team Odyssey Metrics - Jira](#)
- Metric insights (unchanged from last share-out):
 - Created vs. Resolved is 0, which means the backlog didn't grow.
 - Opportunity:** Improve backlog refinement outputs.
 - Cycle Time reduced to 2.54 days**, which shows:
 - Delivering right number of items allowed work to flow faster — now we need to balance speed with overall throughput.
 - Opportunity:** Tighter WIP limits can speed up flow — though the reduced throughput also reminds us that finding the right balance between focus and delivery volume is key.
- August Share-out link: [Team Odyssey Monthly Shareout - August 2025 - Government Savings- Software Development. - Ascensus - Confluence.](#)
- Next Share-out Date: 24th Sept
- Enablement Queue: [Enablement Queue.ppt](#)
- Focus Area - GenAI tools (Co-Pilot and Cursor AI) to improve the throughput.

2. Team Synergy (QIPs and tier 1 triage support) - Green

- Synergy Key Deliverables (Sep)
 - 20 RT Tickets** [\[Team Synergy - RT Tickets Completed Last Month \(Dashboard\)\] Work item search - JIRA](#). Targeting to achieve ~ 30 to 35 RT tickets in September.
 - 2 QIPs [\[Team Synergy - QIPs Completed Last Month \(Dashboard\)\] Work item search - Jira](#)
 - 0 non-QIPs stories
- Process metrics can be found here: [Synergy metrics dashboard](#).
- Metric insights:
 - RT tickets have already exceeded August throughput with 2 weeks left!. ~ 20 -25% improvement from last month throughput.
- Confluence page for Synergy can be found clicking [here](#).
- Scope of current and upcoming work can be consulted in Aha! by clicking [here](#).
- Focus Area - GenAI tools (Co-Pilot and Cursor AI) to improve the throughput.

3. Team Cosmos & Alchemy - Green

- Kick-off Call done on 2/9/2025
- Code Setup / Access Software and Repository Access: Completed
- Sprint 0 - 17th to 30th Sept - In Progress, Sprint refinement call setup today.
- Sprint 1 - 1st Oct
- Risk / Issues - NA

4. Automation Team - Green

Detailed Updates Reference: [Leadership Report – Sep 17, 2025](#)

Key Highlights:

- Expanded regression coverage with new/negative test cases (including ABLE & systematic withdrawal) and stabilized UE/IDP flows on Prime Version 3 framework.
- Regression testing for Stardine in progress. High Priority - ETA 3rd Oct.
- Support performance testing for IDP deadlock issue. - High Priority - Completed

Upcoming / In Progress (Key Work Items):

- Prime V3 GitLab pipeline setup (UE + IDP regression) in progress; access/configuration pending Ops..
 - Pipeline delays due to first-time Ops setup; Dev-Ops is working on it. ~ ETA - Oct 3rd
- Able testcases will be added in the regression test suite.
- Exploring Cursor AI for regression suite automation

Improvement Areas:

- Reporting cadence (qTest dashboards & daily/weekly email automation) requires further streamlining and KT handoff to offshore team - 80% completed. ETA Oct 15th 2025
- Daily Regression Suite Execution Report Analysis - Handover to offshore - 00% completed. ETA Oct 10th 2025

Session: 9/4/25

Staffing:

- Ascensus Persistent Teams: <https://confluence.ascensus.com/x/Hbw8Eg>
- Requirement tracker: [08-29-2025 Ascensus GS Resource Status Tracker.xlsx](#)

Rolling Requirements:

Chapter Lead	Cost Center	Position	Location	Name	Status	Remarks
Lide Winburn	181090	Data Engineer (Support)	Offshore	Anagha Jadhav	Selected	Ascensus onboarding in progress. ETA 9th Sept
Dharmender Verma	182005	Java Automation Dev	Offshore	TBC	Open	Interviews are in progress
Mark Foong	24525	iOS Mobile Developer	Nearshore	Oscar Fernando Espinosa Rocha	Closed	Onboarded
Lide Winburn	24525	Java Developer (Mid-Senior)	Offshore	TBC	Open	Interviews are in progress
	24525	QA Automation (Mid-Senior)	Offshore	TBC	Open	Interviews are in progress

New Scrum Team Requirements

Team - Cosmos

Scrum Master will be shared between these two teams

Chapter Lead	Cost Center	Position	Location	No of Positions	No of Selections	Name of Selected Candidates	External /Internal	Projected Onboarding Date (Ascensus)	Status
Arun Dash	181090	Java Tech Lead	Onsite	1	1	Pragna Koneru	Internal	Onboarded	Onboarded
	181090	Dev Lead	Offshore	1	1	Kaushik Dutta	Internal	Sept 9th	Ascensus Onboarding in progress.
	181090	QA Lead	Offshore	1	1	Sampada Kulkarni	Internal	Onboarded	Onboarded
	181090	Java Developer	Offshore	1	1	Vijay Pingili	Internal	Onboarded	Onboarded
	181090		Offshore	1	1	Avinash Savekar	Internal	Onboarded	Onboarded

		QA Developer							
	181090	BA	Offshore	1	1	Anoop Naik	Internal	Onboarded	Onboarded
	181090	Scrum Master	Offshore	1	1	Brahmomo Bose	Internal	Onboarded	Onboarded

Sprint 1: September 17th

Team - Alchemy

Scrum Master will be shared between these two teams

Chapter Lead	Cost Center	Position	Location	No of Positions	No of Selections	Name of Selected Candidates	External /Internal	Projected Onboarding Date (Ascensus)	Status
Gerald Matthews	181090	Java Tech Lead	Onsite	1	1	Sushma P	External	Sept 12th	Ascensus Onboarding in progress
	181090	Dev Lead	Offshore	1	1	Ravindra Kumar Dhyani	Internal	Sept 9th	Ascensus Onboarding in progress
	181090	QA Lead	Offshore	1	1	Rajesh Meshram	Internal	Onboarded	Onboarded
	181090	Java Developer	Offshore	1	1	Mudhshar Uddin	Internal	Onboarded	Onboarded
	181090	QA Developer	Offshore	1	1	Payal Rout	Internal	Onboarded	Onboarded
	181090	BA	Offshore	1	1	Shivali Pawar	Internal	Onboarded	Onboarded

Sprint 1: September 17th

Budget tracker: [08-29-2025 Ascensus GS Budget Tracker.xlsx](#)

Delivery Updates:

Team Odyssey

- Odyssey's Latest Release 9/7)
 - ~~New York UE (Mobile and Desktop)~~ Descoped from 9/7
 - ~~Pennsylvania UE (Mobile and Desktop)~~ Descoped 9/7
 - Nevada Patch Release (Day 2 items)- 9/7 - **Green**
- Process Metrics: [Team Odyssey Metrics - Jira](#)
- Metric insights:
 - Created vs. Resolved is 0, which means the backlog didn't grow.
 - Opportunity:** Improve backlog refinement outputs.
 - Cycle Time reduced to 2.54 days**, which shows:
 - Delivering right number of items items allowed work to flow faster — now we need to balance speed with overall throughput.
 - Opportunity:** Tighter WIP limits can speed up flow — though the reduced throughput also reminds us that finding the right balance between focus and delivery volume is key.
- August Share-out link: [Team Odyssey Monthly Shareout - August 2025 - Government Savings- Software Development. - Ascensus - Confluence](#)
- Retro Meeting conducted on 3rd September 2025.
- Enablement Queue: [Enablement Queue.ppt](#)

Team Synergy (QIPs and tier 1 triage support)

- Synergy Key Deliverables (Aug)
 - 16 RT Tickets [\[Team Synergy - RT Tickets Completed Last Month \(Dashboard\)\] Work item search - JIRA](#)
 - 7 QIPs [\[Team Synergy - QIPs Completed Last Month \(Dashboard\)\] Work item search - Jira](#)
 - 2 non-QIPs stories: SYN-41 and SYN-61.
- Process metrics can be found here: [Synergy metrics dashboard](#).
- Metric insights:
 - Increase in triage output 10 tickets completed in July vs. 16 tickets completed in Aug.
- Continuous Improvement
 - Tier System Metrics Granuraity in routing ticket flow to track process compliance.
 - KT's based on weekly incoming work with IOS
- Confluence page for Synergy can be found clicking [here](#).
- Scope of current and upcoming work can be consulted in Aha! by clicking [here](#).

Team Cosmos & Alchemy

- Kick-off Call done on 2/9/2025
- Knowledge Transition - In Progress

- Code Setup / Access - In Progress
- Sprint 1 - Expected to Start from September 17th

Automation Team

Detailed Updates Reference: <https://confluence.ascensus.com/x/lyYNF>

- **Key Deliverables in August**
 - Expanded and stabilized the regression suite by adding new scenarios (including negative and MFA flows) to ensure consistent daily runs.
 - Finalized QAC Lab onboarding syllabus and standardized qTest folder structure with legacy script archival underway.
- **Upcoming / In progress (Key work Items)**
 - Prime V3 regression suite and GitLab pipeline setup in progress for UE + IDP flows.
 - qTest result automation and daily reporting being finalized for email delivery.
 - **Improvement areas**
 - Need help on administration work (Jira dashboard, process setup etc.). - We will observe if new scrum team's scrum master can assist here based on available capacity
 - Regular regression/reporting visibility needs streamlining (KT to be offloaded to QA).

Session: 7/30/25

Staffing:

- Ascensus Persistent Teams: <https://confluence.ascensus.com/x/Hbw8Eg>
- Requirement tracker: [07-25-2025 Ascensus GS Resource Status Tracker.xlsx](#)

Rolling Requirements:

Chapter Lead	Cost Center	Position	Location	Name	Status	Remarks
Lide Winburn	181090	Data Engineer	Onsite	Santhosh Kumar Gudipati	Selected	Candidate onboarded
	181090	Data Engineer	Onsite	Pawan Gupta	Selected	Candidate onboarded
	181090	Data QA	Onsite	Anand Madan	Selected	Ascensus onboarding in Progress
	181090	Data Engineer (Support)	Offshore	TBC	Open	Selected candidate did not join. Interviews are scheduled
Dharmender Verma	181090	Oracle PL/SQL Dev	Offshore	Harshal Bhoge	Selected	Ascensus onboarding in Progress
	181090	Java Dev	Offshore	Gaurav Ambekar	Selected	Ascensus onboarding in Progress
	181090	Java Automation Dev	Offshore	Tharkesh N	Selected	Ascensus onboarding in Progress
	181090	Oracle PL SQL QA	Offshore	Shirish Wankhede	Selected	BGV/ Ascensus onboarding in Progress
Mark Foong	181090	iOS Mobile Developer	Nearshore	TBC	Selected	One candidate selected. Backup Interview is scheduled today
Henry Dittmer	181090	Data Engineers (with Dell Boomi experience)	Offshore	Ravi Thongher	Selected	BGV/ Ascensus onboarding in Progress
	181090	Data Engineers (with Dell Boomi experience)	Offshore		Hold	Interviews are in progress
Rajib Akhter	181090	DevOps (AWS, Jenkins etc)	Offshore		Paused	Screening / Interviews are in progress DevOps Candidates with AWS certification are rare. Wait time is high
	181090	Java +PL/SQL Dev	Offshore		Paused	

Henry Dittmer						Screening in Progress Candidates having Java and PL SQL both primaries are extremely rare. Wait time is high
---------------	--	--	--	--	--	--

New Scrum Team Requirements

Scrum Team # 1

Scrum Master will be shared between these two teams

Chapter Lead	Cost Center	Position	Location	No of Positions	No of Selections	Name of Selected Candidates	External /Internal	Projected Onboarding Date (Ascensus)	Status
Arun Dash	181090	Java Tech Lead	Onsite	1	1	Pragna Koneru	Internal	August 4	Ascensus onboarding in Progress
	181090	Dev Lead	Offshore	1	1	Kaushik Dutta	External	August 25	BGV in Progress. Persistent Onboarding in progress
	181090	QA Lead	Offshore	1	1	Sampada Kulkarni	Internal	August 11	Ascensus onboarding in Progress
	181090	Java Developer	Offshore	1	1	Vijay Pingili	Internal	August 11	Ascensus onboarding in Progress
	181090	QA Developer	Offshore	1	1	Avinash Savekar	Internal	August 4	Ascensus onboarding in Progress
	181090	BA	Offshore	1	1	Anoop Naik	Internal	August 4	Ascensus onboarding in Progress
	181090	Scrum Master	Offshore	1	1	Brahmomoy Bose	External	August 18	Ascensus onboarding in Progress

Tentative Team Onboarding Date: Mid-Aug

Expected Start Date: September 1

Scrum Team # 2

Scrum Master will be shared between these two teams

Chapter Lead	Cost Center	Position	Location	No of Positions	No of Selections	Name of Selected Candidates	External /Internal	Projected Onboarding Date (Ascensus)	Status
Arun Dash	181090	Java Tech Lead	Onsite	1	0	To be confirmed		August 25	Open
	181090	Dev Lead	Offshore	1	1	Sneha Krishnamurthy	External	August 25	BGV in Progress. Persistent Onboarding in progress
	181090	QA Lead	Offshore	1	1	Rajesh Meshram	Internal	August 25	Ascensus onboarding in Progress
	181090	Java Developer	Offshore	1	1	Mudhshar Uddin	External	August 11	Ascensus onboarding in Progress
	181090	QA Developer	Offshore	1	1	Payal Rout	Internal	August 11	Ascensus onboarding in Progress
	181090	BA	Offshore	1	1	Shivali Pawar	Internal	August 4	Ascensus onboarding in progress

Tentative Team Onboarding Date: Mid-Aug

Expected Start Date: September 1

Budget tracker: [07-25-2025 Ascensus GS Budget Tracker.xlsx](#)

Delivery Updates:

Team Odyssey

- **Key issues highlighted in the last release:**
 - Pre-MR Dev and Testing Discipline, Active Release Support, Requirement Clarity & Communication, Tooling & Productivity, Feedback Handling & Accounting
- **Key actions aligned:**
 - Reinforce local build/test validation before submitting MRs - *Team to follow a pre-MR checklist and 24-hour review expectation*
 - Conduct Kanban refresher session with Agile coach (SM) to reiterate roles, responsibilities, key artifacts - *SM working on it*
 - Formalize post-freeze change process with risk acceptance signoff from stakeholders - *Tech Leads and CL to ensure in next releases*
 - Maintain a release troubleshooting log - *Tech leads taking ownership*

- Ensure appropriate access is in place - *Access granted to appropriate DBs aligned with offshore compliance*
 - Demonstrate stronger ownership in troubleshooting as domain knowledge improve - *Reiterated to the team*
 - Reinforce adherence to design and engineering review checkpoints; Proactively identify and clarify logic gaps
 - Integrate AI tools into development and testing workflow - *Team has undergone Copilot training at both sides; Access granted to utilize Copilot in workflows*
 - Normalize feedback as part of the development process - *Ongoing coaching for tech leads for better communication and receptivity*
- LCT team discussed and assigned ownership to logged obstacle for action items detailed here: [OB-143](#)
- Odyssey's scheduled work for next release 8/8:
 - Nevada Universal Enrollment (Desktop) **Amber**
 - TN post-release enhancements (State Employee) **Amber**
 - CMS Migration Research (Spike) **Green**
- Potential risks:
 - Stage 1 was down for a couple of days due to Partner testing NV - team got unblocked yesterday (8/30) and seems still on track:
 - TN post release enhancements: **ODY-767** (aged-based box styling) is still in To-Do
- ODY is going through KT and ramp up to support CMS Integration in Unite work - *Gerald provided KT call on 7/21*
- July Share-out link: [Team Odyssey Monthly Shareout - July 2025 - Government Savings- Software Development. - Ascensus - Confluence](#)
- Process Metrics: [Team Odyssey Metrics - Jira](#)
- Metric insights:
 - A lot of items for custom work were created this month (not yet refined) in preparation for upcoming months.
 - **Cycle Time (4.87 days)** is much shorter than **System Time (25.86 days)**, indicating:
 - Work sits in the backlog a long time before being picked up.
 - Once development starts, work is completed efficiently.
 - **Opportunity:** Improve backlog refinement or prioritization to reduce delays before work starts.
 - **Throughput (4.43) > Arrival Rate (3.70)** Work is getting resolved faster than its created. This is healthy and sustainable.
- Enablement Queue: [Enablement Queue.ppt](#)

Team Synergy (QIPs and tier 1 triage support)

- First share out was held 7/24, details can be seen here: [Team Synergy Monthly Shareout July-25](#)
- First LCM was conducted 7/17, one obstacle ([OB-146](#)) was logged tracked by the team.
- Process metrics can be found here: [Synergy metrics dashboard](#).
- Metrics Insights:
 1. To date, 6 tickets have been triaged and resolved by Synergy (enabled by KT provided). These will be reflected in July metrics.
 2. 13 QIPs completed
 3. High **Lead Time (23 days)** and **System Time (24.3 days)** vs. relatively short Cycle Time means lots of waiting This is expected from a newly formed team.
- Tier-1 triage process has been established (click [here](#) to consult) and have begun the process starting 6/30
 - Synergy has remained keeping a log of triage efforts to identify opportunities on how to expand knowledge and what areas are needed
 - [Synergy \(Tier-1\) Triage log - Government Savings- Software Development. - Ascensus - Confluence](#)
 - *Initiative to integrate data that is manually being captured in the log into RT is ongoing Brenda and Fred have this action item.*
- Confluence page for Synergy can be found clicking [here](#).
- Scope of current and upcoming work can be consulted in Aha! by clicking [here](#).

Automation Team

Detailed Updates Reference: <https://confluence.ascensus.com/x/OgkNF>

- **Regression Suite Stabilization & Expansion:**
 - Daily runs stabilized (flakiness triaged) across 529(NY, IL), ABLE plans, adding more plans to daily regression; and new scenarios continuously added
 - MFA Automation Integrated in the login flow added to regression suite by week's end.
 - Expansion: Test cases for new features being prioritized with SMEs to be included in appropriate regression, release, and smoke suites
- **CI/CD Pipeline Expansion:** Actively collaborating with the DevOps team to integrate Prime V3 automation in the GitLab-based pipelines (*effort to include UE/IDP automation to daily suite*)
- **Sardine Performance Baseline:** JMeter tests integrated with BlazeMeter dashboards for baseline versioning
- **QTest enhancements:**
 - Archival: Standardization of QTest folder structure is underway, archival of legacy scripts has begun
 - Collaboration with Persistent & Tricentis: team getting direction and support to fix QTest dashboard/reporting integration issues
- **Team Performance Review:** Performance being monitored closely; transition plan discussed to proactively replace one member due to performance issues
- **QA Enablement:** QAC Lab syllabus is being developed to enhance and add training resources for QA onboarding

Appreciations Received - Prashant Mali (JIRA Admin):

- Valuable addition to the Jira/Aha admin team
- Appreciated for his professionalism, initiative, and collaborative spirit, and ability to handle complex, custom tasks independently
- Worked on a number of impactful initiatives, including the creation of multiple team Jira boards (both Scrum and Kanban), and the rollout of several Jira administration improvements

- Played a key role in supporting teams with specialized requirements, such as QA Automation (config enhancements around severity-driven due dates, escalation notifications, mandatory RCA/RCC fields)
- Instrumental in assisting with Aha! configuration changes, mapping, and integrations

Session: 7/17/25

Staffing:

- Ascensus Persistent Teams: <https://confluence.ascensus.com/x/Hbw8Eg>
- Requirement tracker: [07-17-2025 Ascensus GS Resource Status Tracker.xlsx](#)

Rolling Requirements:

Chapter Lead	Position	Location	Name	Status	Remarks
Lide Winburn	Data Engineer	Onsite	Santhosh Kumar Gudipati	Selected	Candidate onboarded
	Data Engineer	Onsite	Pawan Gupta	Selected	Candidate onboarded
	Data QA	Onsite	Anand Madan	Selected	Ascensus onboarding in Progress
	Data Engineer (Support)	Offshore		Open	Selected candidate did not join. Interviews are scheduled
Dharmender Verma	Oracle PL/SQL Dev	Offshore	Harshal Bhoge	Selected	BGV in Progress. Persistent Onboarding in progress
	Java Dev	Offshore	Tharkesh N	Selected	BGV in Progress. Persistent Onboarding in progress
	Oracle PL SQL QA	Offshore		Open	Screening in Progress
Mark Foong	iOS Mobile Developer	Nearshore		Open	Interviews are in progress
Henry Dittmer	Data Engineers (2) (with Dell Boomi experience)	Offshore		Open	Profile Search is in progress. We will update by Monday about the candidate's availability
Rajib Akhter	DevOps (AWS, Jenkins etc)	Offshore		Open	Screening in progress DevOps Candidates with AWS certification are rare. Wait time is high
Henry Dittmer	Java +PL/SQL Dev	Offshore		Open	Profiles review in Progress Candidates having Java and PL SQL both primaries are extremely rare. Wait time is high

New Scrum Team Requirements

Scrum Team # 1

Scrum Master will be shared between these two teams

Chapter Lead	Position	Location	No of Positions	No of Selections	Name of Selected Candidates	External /Internal	Projected Onboarding Date (Ascensus)	Status
Arun Dash	Java Tech Lead	Onsite	1	1	Pragna Koneru	External	August 4	BGV in Progress. Persistent Onboarding in progress
	Dev Lead	Offshore	1	1	Kaushik Dutta	External	August 25	BGV in Progress. Persistent Onboarding in progress
	QA Lead	Offshore	1	1	Sampada Kulkarni	External	August 11	BGV in Progress. Persistent Onboarding in progress
	Java Developer	Offshore	1	1	Priyanka Keche	External	August 11	BGV in Progress. Persistent Onboarding in progress
	QA Developer	Offshore	1	1	Avinash Savekar	Internal	August 4	Ascensus onboarding in Progress
	BA	Offshore	1	1	Anoop Naik	Internal	August 4	Ascensus onboarding in Progress
	Scrum Master	Offshore	1	0	To be confirmed	External	August 18	Interviews are in progress

Tentative Team Onboarding Date: Mid-Aug

Expected Start Date: September 1

Scrum Team # 2

Scrum Master will be shared between these two teams

Chapter Lead	Position	Location	No of Positions	No of Selections	Name of Selected Candidates	External /Internal	Projected Onboarding Date (Ascensus)	Status
Arun Dash	Java Tech Lead	Onsite	1	0	To be confirmed		August 25	Final feedback pending
	Dev Lead	Offshore	1	1	Sneha Krishnamurthy	External	August 25	BGV in Progress. Persistent Onboarding in progress
	QA Lead	Offshore	1	1			August 25	1 Interview is schedule on 7/18
	Java Developer	Offshore	1	1	Vijay Pingili	External	August 11	BGV in Progress. Persistent Onboarding in progress
	QA Developer	Offshore	1	1	Payal Rout	External	August 11	BGV in Progress. Persistent Onboarding in progress
	BA	Offshore	1	1	Shivali Pawar	Internal	August 4	Ascensus onboarding in progress

Tentative Team Onboarding Date: Mid-Aug

Expected Start Date: September 1

Budget tracker: [07-17-2025 Ascensus GS Budget Tracker.xlsx](#)

Delivery Updates:

Team Odyssey

Historic release for Odyssey, release 6 plans on July 11th:

1. Indiana Universal Enrollment (Desktop)
 2. Indiana Universal Enrollment (Mobile)
 3. TN (Desktop)
 4. Sub-bene AK
 5. Sub-bene AK National
 6. Sub-bene MD
- Odyssey planning for next release 8/8 scheduled for 7/15.
 - Nevada Universal Enrollment (Desktop)
 - TN post-release enhancements (State Employee)
 - ODY is going through KT and ramp up to support CMS Integration in Unite work
 - Enablement Queue: [Enablement Queue.ppt](#)
 - Process Metrics: [Team Odyssey Metrics - Jira](#)

Action item: To investigate the issue highlighted towards last releasee's delivery - Anuj

Team Synergy (QIPs and tier 1 triage support)

- Synergy has closed **11** QIPs to date: [Issue navigator - JIRA](#)
- Tier-1 triage process has been established and have begun the process starting 6/30
 - Synergy has remained keeping a log of triage efforts to identify opportunities ton how to expand knowledge and what areas are needed
 - [Synergy \(Tier-1\) Triage log - Government Savings- Software Development. - Ascensus - Confluence](#)
 - Team has been identifying and taking appropriate KTs from Buddy iOS team on Astro Feed Failures and Unite Feed Failures
 - After the identified KTs, team may take up to 50% of the RT tickets. As of today, they are able to take one ticket per day based on the knowledge they have got on Astro feeds
 - Following are the KTs Team Synergy received so far:
 - UI - Team iOS - 6/30 (QIP's)
 - ASTRO Job fails - Team iOS - 7/11(RT Triage)
 - QA process and navigating database tables - Team Frontier - 7/15.
 - Planning more KT's on Astro Feed failures and Unite feed failures, one scheduled on 07/18(Team IOS).
- First share out scheduled for July 23rd - expect to have process metrics dashboard by then
 - Drafting process [Synergy metrics dashboard](#) (Brenda), still WIP.
- Confluence page for Synergy can be found clicking [here](#).
- Scope of current and upcoming work can be consulted in Aha! by clicking [here](#).
- [AGS Sev 2 Incident Management - Government Savings- Software Development. - Ascensus - Confluence](#)

Automation Team

Detailed Updates Reference: <https://confluence.ascensus.com/x/68t5Ew>

- **Sardine Performance Testing Completed**
First round completed and published for IDP Login flow:
[Sardine Perf Results Dashboard](#)
- **Regression Coverage Finalized for Key Modules**
Includes Legacy Login, Web Registration, Enrollment, Contribution, Withdrawal, Account Maintenance, Account balance etc.
[Automation Regression Coverage Dashboard](#)
- **Migration to Prime V2 Underway**
Member Withdrawal & Contribution flows now being ported from Vespa & added to regression suit.
- **JIRA Dashboard, Alerts & Bug Lifecycle Defined, configured and enforced across the QA Automation team.**
Bug lifecycle defined, dashboards and email alerts active.
[JIRA Dashboard](#)
[Defect management, bug Life cycle & RCA Process](#)
- **MFA Now Supported in Automation**
Major framework upgrade allows running MFA-enabled flows organically.
- **Working with Persistent & Tricentis**
Addressing issues in qTest Insights and test result integration.

Action item: Report showing how many test cases are added to the nightly regression at each release - Anuj to work with Swapnil

Session: 7/2/25

Delivery Updates:

Team Odyssey

- Monthly Share out
 - Last: June 26
 - Odyssey June Shareout link: [Team Odyssey Monthly Shareout - June 2025 - Government Savings- Software Development. - Ascensus - Confluence](#)
 - Recording: [Team Odyssey Monthly Shareout-20250626_083413-Meeting Recording.mp4](#)
- Latest plan successfully released: NV Able on 06/13
- Plans being worked on and upcoming release (7/11):

Plan	Jira ID	Type	Status	Owner
Trowe	{ODY-716}	Standard [IDP]	Dev Done, Stage 1 QA in progress	Sameer, Vinay
Maryland Direct	{ODY-684}	Standard [IDP]	Dev Done, Stage 1 QA in progress	Vinay, Bany
AK Direct	{ODY-473}	Standard [IDP]	Dev Done, Stage 1 QA in progress	Sameer, Vinay
Indiana (Web + Mobile)	{ODY-169}	Custom	70% Dev Done, Stage 1 Partially Tested	Bany, Sameer, Vinay
Tennessee (Web)	{ODY-645}	Custom	60% Dev Done, Stage 1 Partially Tested	Sameer and Vinay standard, Bany custom work
Iowa	{ODY-525}	Custom	To Do	Bany
New Mexico	[ODY-578]	QIP	Dev Done Awaiting Stage 1 Merge	Bany

- Confirmation that during LCM obstacles are being logged from Odyssey is their presence in the backlog obstacle: [Link](#).
- Enablement Queue: [Enablement Queue.ppt](#)
- Process Metrics: [Team Odyssey Metrics - JIRA](#)

Team Synergy (QIPs and tier 1 triage support)

- Synergy has closed 6 QIPs to date: [Issue navigator - JIRA](#)
- Tier-1 triage process has been established and have begun the process starting 6/30
 - [AGS Sev 2 Incident Management - Government Savings- Software Development. - Ascensus - Confluence](#)
 - Analysis was done paired with iOS to establish triage times using incoming times heatmap.
 - Tier-1 triage time: 8:00AM
 - Tier-2 triage time: 10AM
- Synergy will start keeping a log of triage efforts to identify opportunities on how to expand knowledge and what areas are needed
 - [Synergy \(Tier-1\) Triage log - Government Savings- Software Development. - Ascensus - Confluence](#)
- First share out scheduled for July 23rd - expect to have process metrics dashboard by then
- Confluence page for Synergy can be found clicking [here](#).
- Scope of current and upcoming work can be consulted in Aha! by clicking [here](#).

Automation Team

- Detailed Updates Reference: <https://confluence.ascensus.com/x/68t5Ew>
- Automation Regression Suite: All key (7) modules for legacy system will be fully automated by end of current sprint (07/09) & added to daily nightly regression.
- Process updated: Nightly regression updates: New Bug Handling Process implemented — *Fix or revert by 10:00 AM EST* same business day, main branch locked until then. for more details click [here](#)
- [JIRA Dashboard](#) setup completed this week — live tracking, team velocity, defect tracking & notification enabled.
- Performance Test Projects: Sardine Performance Testing underway — first run scheduled this Thursday.
- qTest Insight Dashboards & Reporting: qTest Reporting working; automation result integration in progress. Related to insight Dashboard, working with Persistent team
- qTest Manual Test case archival & Folder reorganization finalized: modular, plan-tagged, reusable structure in qTest

Staffing:

- Ascensus Persistent Teams: <https://confluence.ascensus.com/x/Hbw8Eg>
- Requirement tracker: [07-01-2025 Ascensus GS Resource Status Tracker.xlsx](#)

Rolling Requirements:

Chapter Lead	Position	Location	Name	Status
Lide Winburn	Data Engineer	Onsite	Santhosh kumar Gudipati	Selected Onboarding in Progress
	Data Engineer	Onsite	Pawan Gupta	Selected Onboarding in Progress
	Data QA	Onsite		Interviews are in progress. 2 Client interviews scheduled this week
	Data Engineer	Offshore	Neha Waghchure	Selected BGV in Progress
Dharmender Verma	Oracle PL/SQL Dev	Offshore	Harshal Bhoge	Selected BGV in Progress
	Java Dev	Offshore		Interviews are in progress
	Oracle PL SQL QA	Offshore		Interviews are in progress
	Automation QA	Offshore		On hold, CL to decide later post developers joining
Mark Foong	iOS Mobile Developer	Nearshore / Offshore		3 profiles to be shared today for review
Rajib Akhter	DevOps (AWS, Jenkins etc)	Offshore		Interviews in Progress Candidates having Java and PL SQL both primaries are extremely rare. Wait time is high
Henry Dittmer	Java +PL/SQL Dev	Offshore		Profiles review in Progress Candidates having Java and PL SQL both primaries are extremely rare. Wait time is high

New Scrum Team Requirements

Total Scrum Teams 2

Scrum Master will be shared between these two teams

Chapter Lead	Position	Location	No of Positions	Status
Arun Dash	Java Tech Lead	Onsite	2	Interviews are in progress. 1 Client interview is scheduled today
	Dev Lead	Offshore	2	Interviews are in progress. 1 Client interview is in pipeline
	QA Lead	Offshore	2	Interviews are in progress.
	Java Developer	Offshore	2	Interviews are in progress
	QA Developer	Offshore	2	Interviews are in progress
	BA	Offshore	2	1 Client interview conducted feedback pending. 1 is scheduled tomorrow
	Scrum Master	Offshore	1	Interviews are in progress

Expected Start Date: Mid-Aug

Budget tracker: [07-01-2025 Ascensus GS Budget Tracker.xlsx](#)

GS Invoice Email:

- Going forward start May invoice email subject will be in following format: "Government Savings CostCenter Month Year Invoice" i. e. "Government Savings 181090 May 2025 Invoice" or "Government Savings 24525 May 2025 Invoice"

Business Domain Onboarding Page [WIP]:

- [Business Domain KT Center - Government Savings- Software Development. - Ascensus - Confluence](#)

Session: 6/18/25

Staffing:

- Ascensus Persistent Teams: <https://confluence.ascensus.com/x/Hbw8Eg>
- Key updates:
 - New requirements (WIP)
 - 3 Onshore
 - 2 Data engineer - 1 candidate selected, 1 in progress
 - 1 Data QA - Interviews are in progress
 - 2 Offshore
 - 1 Java + PL SQL Developer (Skillsets more aligned to Java + PL SQL Developer than Data Engineer profiles shared originally) - L1 Interviews are in progress
 - 1 DevOps - Interviews are in progress
 - 4 Offshore - SFRP Platform
 - 1 Java Developer
 - 1 PL/SQL Developer
 - 1 Functional QA with PL/SQL - Profile shared for evaluation
 - 1 Automation QA - Profile shared for evaluation
 - New Pod Team (7 members)?
- Requirement tracker: [06-16-2025 Ascensus GS Resource Status Tracker.xlsx](#)

Team Odyssey

- Monthly Share out
 - Last: May 29
 - [Team Odyssey Monthly Share out - May 2025 - Government Savings- Software Development. - Ascensus - Confluence](#)
 - [Team Odyssey Monthly Shareout-20250529_083229-Meeting Recording.mp4](#)
 - Upcoming: Jun 26
- Latest plan released: NV Able on 06/13
- Plans being worked on (subject to change as per priority):
 - Indiana on 07/11
 - Tennessee on 07/11
 - Maryland on 07/11
 - PA Direct pushed to Sept
- To note: We are proactively working on onsite tech lead identification as a back-up option
- Enablement Queue: [Enablement Queue.ppt](#)
- Process Metrics: [Team Odyssey Metrics - JIRA](#)

Team Synergy (QIPs and tier 1 triage support)

- Onboarding and KT for 4 newly joined team members is ~100% complete. Team has completed local setup and have access to RT, Stage DB, Email whitelisted and Putty.
 - [Environment and KT - Government Savings- Software Development. - Ascensus - Confluence](#)
 - [iOS KT - Enrollment](#) (KT on IDP UE to ramp up on tier 1 support)
- Team board is set up and completed couple of QIP's with due date for June13: [SYN Board - Backlog - Jira](#)
- Confluence page for Synergy can be found clicking [here](#).
- Scope of current and upcoming work can be consulted in Aha! by clicking [here](#).

Automation Team

- High level updates: <https://confluence.ascensus.com/x/68t5Ew>
- qTest Insight Dashboards & Reporting: Sandbox set up; Training session to be conducted this week as per team's availability
- Status: [June 16: Progress Summary & Execution Status - - Government Savings- Software Development. - Ascensus - Confluence](#)

Budget tracker: [06-18-2025 Ascensus GS Budget Tracker.xlsx](#)

GS Invoice Email:

- Going forward start May invoice email subject will be in following format: "Government Savings CostCenter Month Year Invoice" i.e. "Government Savings 181090 May 2025 Invoice" or "Government Savings 24525 May 2025 Invoice"

Session: 6/04/25

Staffing:

- Ascensus Persistent Teams: <https://confluence.ascensus.com/x/Hbw8Eg>
- Key updates:
 - Synergy:
 - 4 membered offshore Dev and QA onboarded; KT to be completed by this week
 - Krishna formally onboarded to Persistent on Jun 2
 - Offshore BA to be onboarded by first week of July; Working on immediate backup profiles
 - Automation:
 - Both automation developers onboarded and started working with Swapnil
 - New requirements (WIP)
 - 3 Onshore (2 Data engineer, 1 Data QA)
 - 2 Offshore (1 Data engineer, 1 DevOps)
 - Attrition:
 - As aligned with Gerald and Mark, Bany has taken up lead position with immediate effect. Bany's performance will be closely monitored
- Requirement tracker: [06-03-2025 Ascensus GS Resource Status Tracker.xlsx](#)

Team Odyssey

- Monthly Share out on May 29:
 - [Team Odyssey Monthly Share out - May 2025 - Government Savings- Software Development. - Ascensus - Confluence](#)
 - [Team Odyssey Monthly Shaerout-20250529_083229-Meeting Recording.mp4](#)
- Latest LCM:
- Enablement Queue: [Enablement Queue.ppt](#)
- Latest plan released: Arkansas on 5/18
- Plans being worked on (subject to change as per priority):
 - NV Able on 06/13
 - Indiana on 07/11
 - PA Direct pushed to Sept
- Process Metrics: [Team Odyssey Metrics - JIRA](#)

Team Synergy

- Onboarding and KT for 4 newly joined team members is ~80% complete, expect to be done by 6/5.
- Onboarding plan and progress can be seen here: Environment and KT - Government Savings- Software Development. - Ascensus - Confluence
- Team board is set up: [SYN Board - Backlog - Jira](#)
- Timesheets - Tempo
 - First timesheet has been submitted for May and Offshore TL has been enabled for proper monthly timesheet inspection within Tempo App.
 - Tempo training provided by Scrum Master was completed 5/28.
 - Krishna was removed from Pixel 5/30 and added to Synergy 6/2 (allocation 100%)
- Confluence page for Synergy can be found clicking [here](#).
- Scope of current and upcoming work can be consulted in Aha! by clicking [here](#).

Automation Team

- Swapnil working on documenting requirement for dashboard and reporting
 - Swapnil introduced to Persistent Automation experts who can be leveraged, if needed, for discussions
- Delivery status: [Q2 Regression Suite – Release 2 Summary \(May 28, 2025\) - Government Savings- Software Development. - Ascensus - Confluence](#)
- Automation team roadmap: [QA Automation Squad roadmap: Lucidspark](#)

Budget tracker: [06-03-2025 Ascensus GS Budget Tracker.xlsx](#)

Asks:

- To provide detailed JD including role clarity, location, and experience range for us to avoid any delay in profile screening

GenAI tool Sasva

- Installation: Technical and Environmental updates being worked out
 - Feed Analysis SASVA Demo done on May 23
 - RT Tracking Session with Rob Fries and Mark Foong done on May 22 for feasibility check
-

Session: 5/21/25

Requirement tracker: [05-21-2025 Ascensus GS Resource Status Tracker.xlsx](#)

- Key updates:
 - Pixel:
 - 4 membered offshore Dev and QA team has joined Ascensus ecosystem on May 16
 - Krishna to start on Jun 2 - offer rolled out and accepted
 - Offshore BA selected on May 15 - ongoing background check
 - Automation:
 - 2nd resource Sagar Rath joined on May 20; Swapnil and Sagar have connected
 - Analyst profiles:
 - Feed Analyst to start on May 22
 - RT Tracking Analyst: Next interview on May 23
 - Attrition:
 - Vivek More due to unforeseen personal circumstances, with last working day on May 23 - alternate options being actively discussed
- Asks:
 - To provide detailed JD including role clarity, location, and experience range for us to initiate the search
 - Team Ranger starting date and any updates on team structure 7 members: (1 onsite lead, offshore - 1 Dev lead, 2 Devs, 1 Test lead, 1 Test engineer, 1 SM) - to be on hold basis Odyssey (should be autonomous + behind on new product releases + frontend) and Pixel

Automation Team

- Formal Session conducted on May 20. Swapnil introduced to Persistent Automation experts who can be leveraged, if needed, for discussions
 - Next steps: Swapnil to document GS specific nuances for automation and dashboarding; set up further tailored connects with experts when read
 - Further Staffing?
- Delivery status: <https://confluence.ascensus.com/x/4DknEw>
- Automation team roadmap: [QA Automation Squad roadmap: Lucidspark](#)

GenAI tool Sasva

- Installation: Technical and Environmental updates being worked out
- Feed Analysis SASVA Demo on May 23
- RT Tracking Session with Rob Fries on May 22 for feasibility check

Team Odyssey

- Enablement Queue: [Enablement Queue.ppt](#)
- Latest plan released: Arkansas on 5/18
- Ongoing plans: PA Direct, Indiana
- Process Metrics: [Team Odyssey Metrics - JIRA](#)

Budget tracker: [05-16-2025 Ascensus GS Budget Tracker.xlsx](#)

Asks:

Session: 5/7/25

Requirement tracker: [05-07-2025 Ascensus GS Resource Status Tracker.xlsx](#)

Budget tracker: [04-29-2025 Ascensus GS Budget Tracker.xlsx](#)

Team Odyssey

- Latest share out: [Team Odyssey Monthly Share out - April 2025 - Government Savings- Software Development. - Ascensus - Confluence](#)
- Process Metrics: [Team Odyssey Metrics - JIRA](#) (to be iterated on further on 5/7)
- Enablement Queue: [Enablement Queue.ppt](#)
- Latest KT: 4/28 with team innovators on mobile enablement

Automation team

- Resources: 1st joined on 4/30; Ascensus onboarding in progress for the 2nd
- Meeting cadences: Weekly sync up Swapnil <> Anuj, Daily Stand ups
- Automation team roadmap: [QA Automation Squad roadmap: Lucidspark](#) (to be reviewed and iterated with Henry on 5/7)
- Expert sessions: Internal discussion organized on 5/8 with automation experts within PSL and Swapnil, formal session to be set up soon after

GenAI tool Sasva

- Sample feeds shared with Sasva team on 5/1
- RT Demo: Coordinating with Mark and Sasva team

Asks:

- Help avoid delays in Ascensus onboarding process
