



QA Automation Program

Bi-Weekly Leadership Update

Prime v2 | Prime v3 (UE / IDP) | API | Performance Testing

EXECUTIVE SUMMARY

What Changed Since Last Update

Scaled Coverage

Automation expanded materially across Prime v2 and v3, with v2 nearing sustain-only mode while v3 grows faster than planned due to business demand.

Programs Established

API and Performance testing programs are operational with validated suites, awaiting pipeline decisions to move forward.

New Constraints

Execution is no longer the bottleneck. Governance, ownership clarity, and pipeline direction now determine our ability to sustain momentum.

Leadership Alignment Needed

Five critical decisions will unblock the next phase and protect execution velocity:

1 Migration Ownership

Establish notification and coverage responsibility for Legacy to IDP plan migrations

2 Prime v3 Charter

Define scope: partial feature coverage or full regression successor to v2

3 Pipeline Direction

Finalize GitLab versus GitHub strategy for API and Performance automation

4 Capacity Protection

Secure part-time BA/admin support to maintain intake discipline and JIRA hygiene

5 Intake Reinforcement

Enforce "no ad-hoc work outside JIRA" to prevent fragmentation



Prime v2 Regression Status

381+

Test Cases


Expanded from ~250 baseline

7

Core Modules

Complete coverage achieved

Daily regression runs are stable and repeatable. Legacy-only plans have been explicitly identified, while NYD and similar plans migrated intentionally to v3. Prime v2 is effectively in closure mode from a core-module perspective.

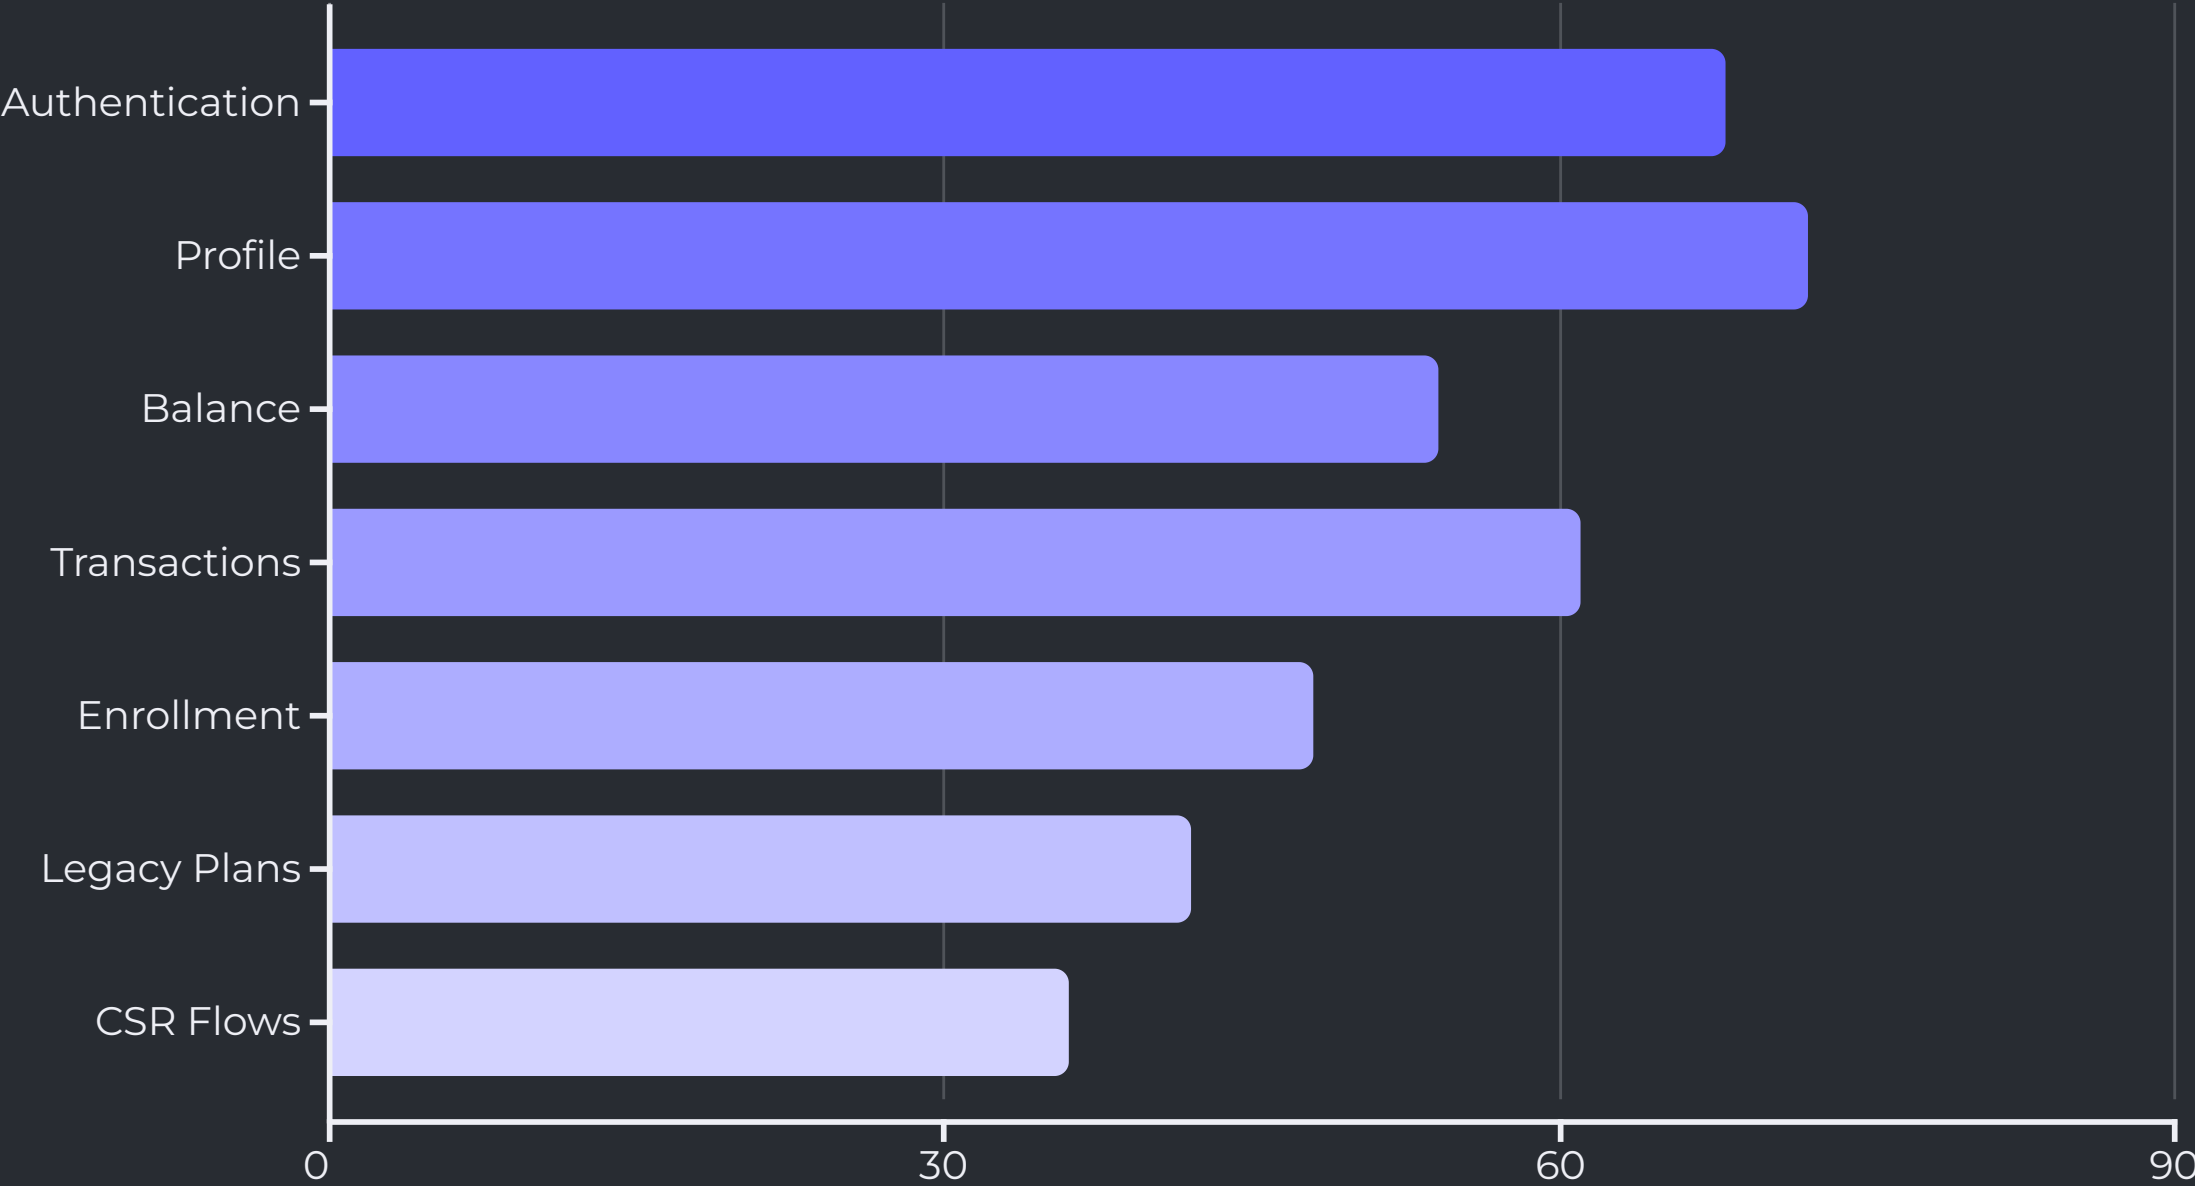

Prime v2: Emerging Risk

The Problem

Plans are migrating from Legacy to IDP without QA notification. Automation failures surface after migration, forcing reactive rework to remove coverage from v2 and rebuild in v3.


Impact on Operations

- Wasted engineering effort on duplicate work
- Loss of regression signal confidence during transition windows
- Ownership ambiguity creates coordination delays
- Hidden technical debt accumulates in test suites

Leadership Ask


Migration owners must notify QA in advance and own coverage transition responsibility. Migration without QA coordination creates hidden cost and operational noise.

Prime v3 Automation Progress

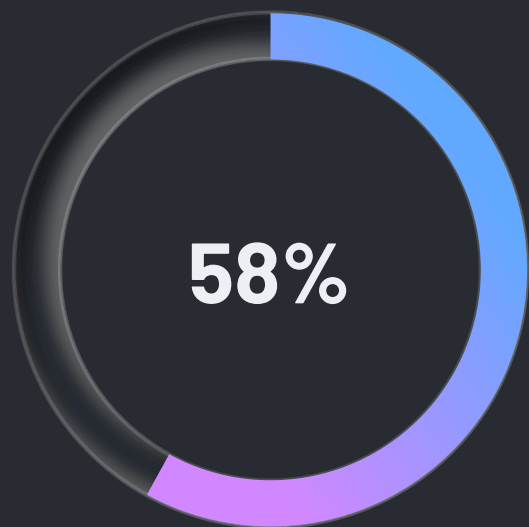


UE Growth

From ~140 to ~221 test cases

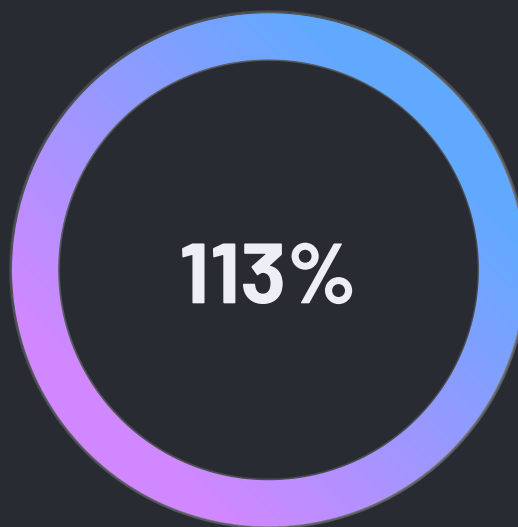

IDP Expansion

From ~16 to ~34 test cases

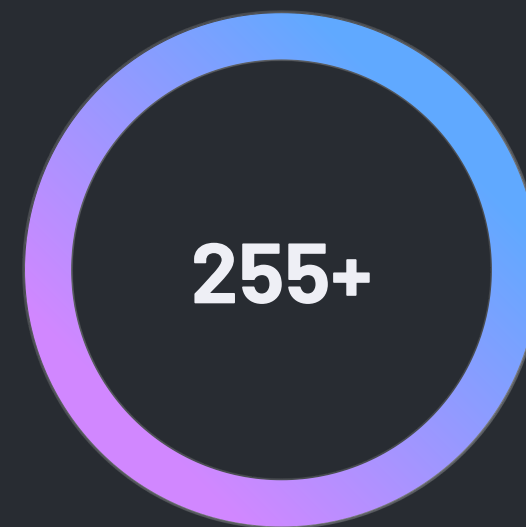


Total Coverage

Combined test case count

Growth is demand-driven, not speculative. Key drivers include NYD requirements, international phone number changes, member and CSR profile updates, and closure of UE withdrawal coverage gaps.

Prime v3: Direction Needed

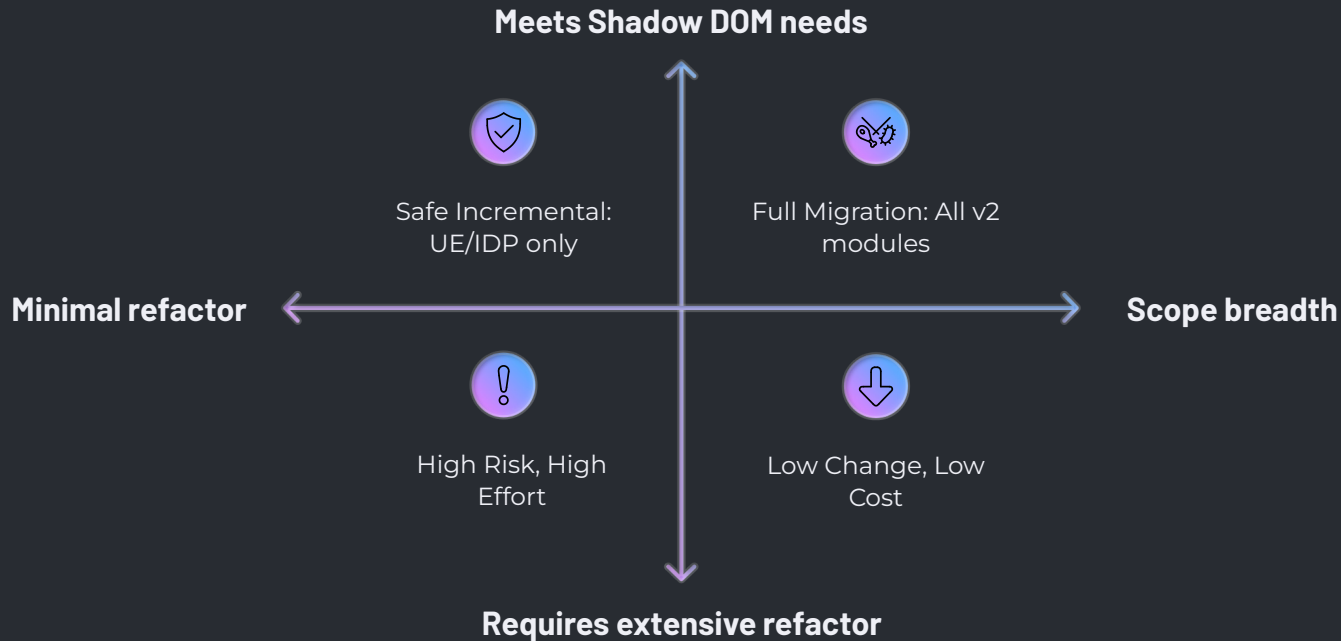

IDP uses Shadow DOM technology, requiring v3 framework architecture and significant refactoring. Legacy code cannot be safely copied forward without breaking.

Technical Reality

The Shadow DOM constraint means every new module requires ground-up implementation in the v3 framework. This is engineering investment, not configuration.

Strategic Question

Should Prime v3 stop at current features, or become the full regression successor to Prime v2 covering profile, balance, transactions, and all core modules?

- ❏ If v3 is the future, we should build it intentionally—not by accident.

API Program Status

01

Authentication Selected

Authentication APIs chosen as first implementation slice based on criticality and stability

03

Environments Validated

Stage1 and QC4 environments tested and verified for reliability

02

Suites Built

Test suites developed and running successfully in local environments

04

Gaps Addressed

ACV discrepancies identified and resolved incrementally with stakeholders

📌 Technically ready to deploy. Operationally waiting on pipeline direction finalization (GitLab vs GitHub).

Performance Testing Status

Ownership Transferred

Performance testing responsibility successfully transferred to QA with auth performance flows documented and understood.

Current Progress

- Existing tests being stabilized for repeatability
- Goal progression: establish baseline → nightly automation → expand coverage
- Auth flows prioritized as initial focus area



Gap: No Manual Baseline

QTest lacks performance baseline data for comparison

Ask: SME Confirmation


Need clarity on login, enrollment, IDP vs legacy ownership

Blocker: Pipeline Dependency

Same GitLab/GitHub decision blocking API program




Capacity and Governance Risk



Increasing Volume

Test suite size growing across all programs. Daily regression analysis load expanding with each sprint.




Support Requests

Ad-hoc support requests consuming capacity outside planned work. No intake discipline enforcement.



Process Degradation

JIRA hygiene slipping due to bandwidth constraints. Backlog health declining week over week.



Signal Dilution

Risk of regression signal quality degradation through overcommitment and fragmented focus.

This is a scaling problem, not a performance problem. The team is executing well but approaching sustainable capacity limits.

Resourcing and Operating Model

Proposed Operating Model

Feature teams build initial automation for new capabilities. QA assumes ownership once tests enter regression suite. No ad-hoc work accepted outside JIRA intake process.

Resourcing Ask

Part-time BA or QA admin role at 30-40% capacity to handle:

- Intake coordination and prioritization
- JIRA hygiene and backlog health
- Documentation and process enforcement
- Stakeholder communication

Small investment prevents large inefficiency and protects engineering focus on automation development.

The Bottom Line

Execution Capability: Proven

Prime v2 scaled without regression instability. Prime v3 gaps closed proactively. API and Performance programs established without dedicated SMEs. Offshore team owns daily RCA independently.

What Determines Success Now

Governance clarity, ownership models, and pipeline direction are the determining factors. With leadership alignment, the program scales cleanly. Without it, effort fragments and velocity degrades.



❏ We're ready for the next phase. Leadership enablement is the lever.
